




1

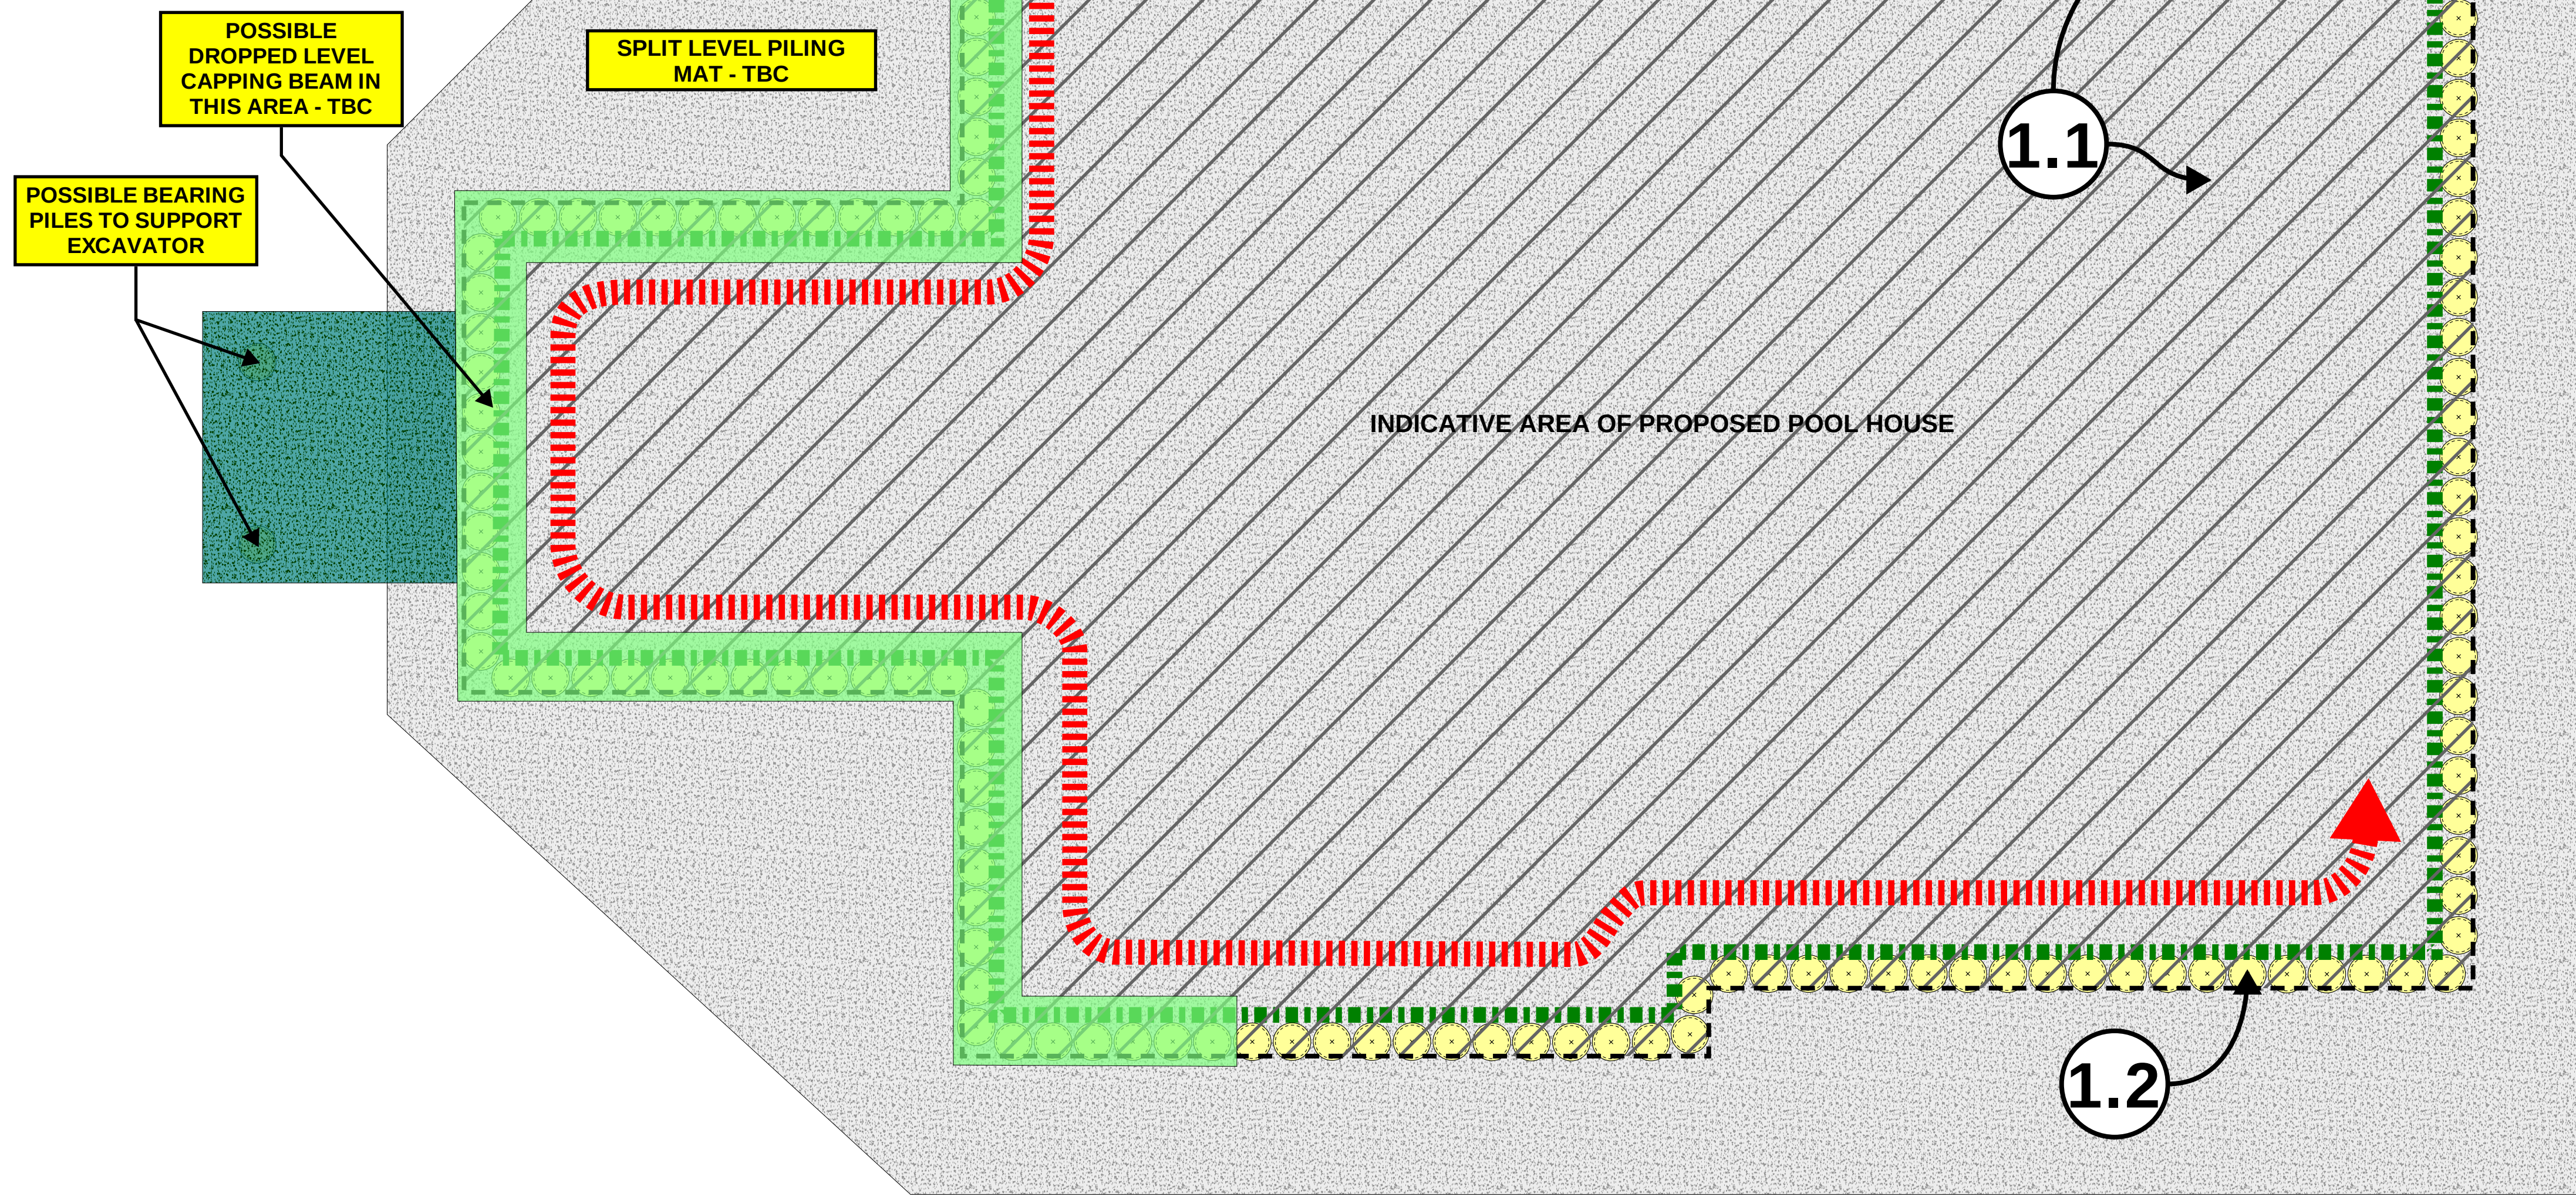

PLAN

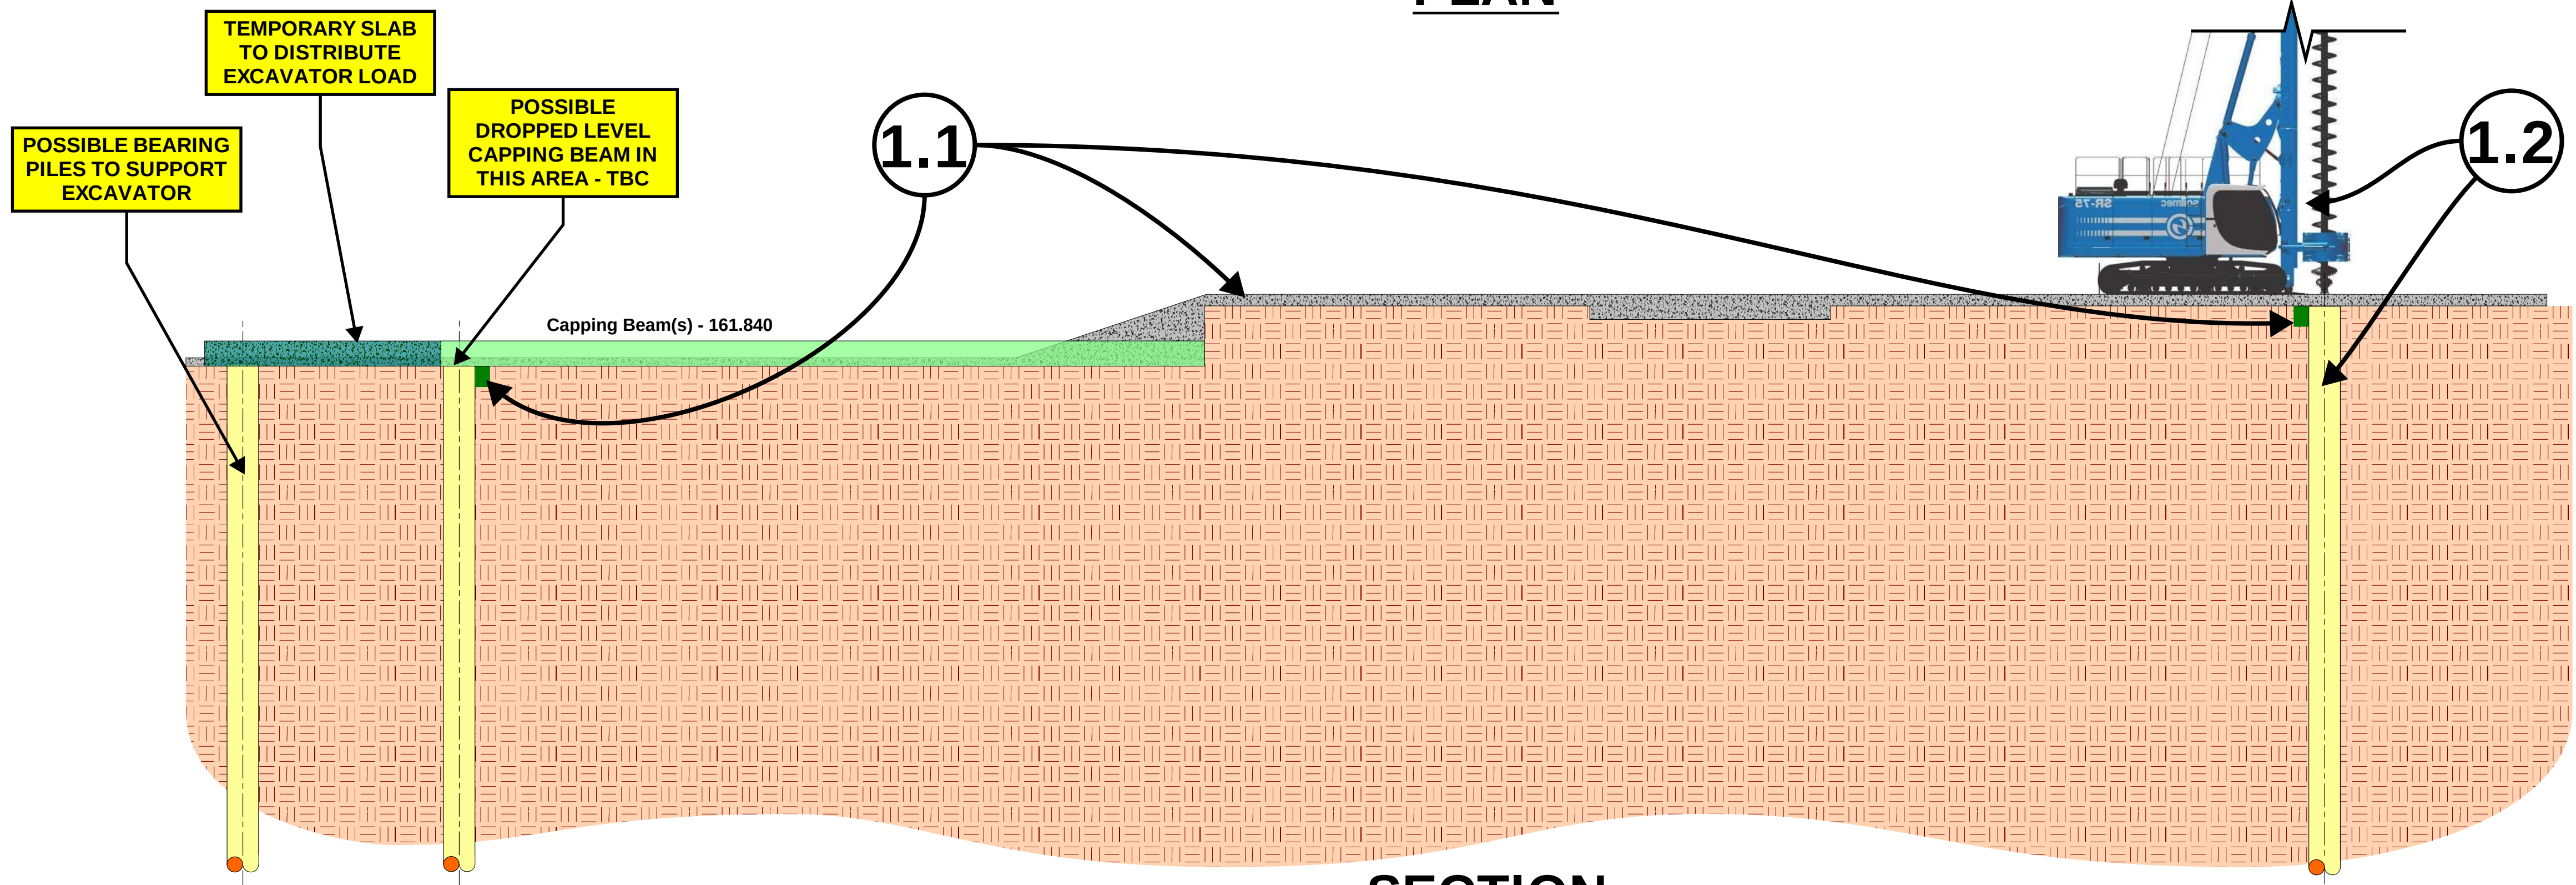

SECTION



NOTES:

PROVISIONAL SEQUENCE OF WORKS

- 1.1) Install Piling mat, guide beams around proposed Pool House area**
- 1.2) Mobilise Piling Rig (Soilmec SR75) & Install perimeter wall Piles**

[illegible]

SIZE GROUP

STRUCTURES

DRAWN BY CP	CHECKED BY	DATE 17 / 10 / 25
----------------	------------	----------------------

CONTRACT
TOTTENHAM HOUSE


REFERENCE

POOL HOUSE


PROVISIONAL CONSTRUCTION SEQUENCE (STAGE 1 of 7)

SCALE (@ A1) SEE SCALE BAR	PROJECT NUMBER ST23-04	
DRAWING NUMBER ST24-SOW-001		REV 0


2

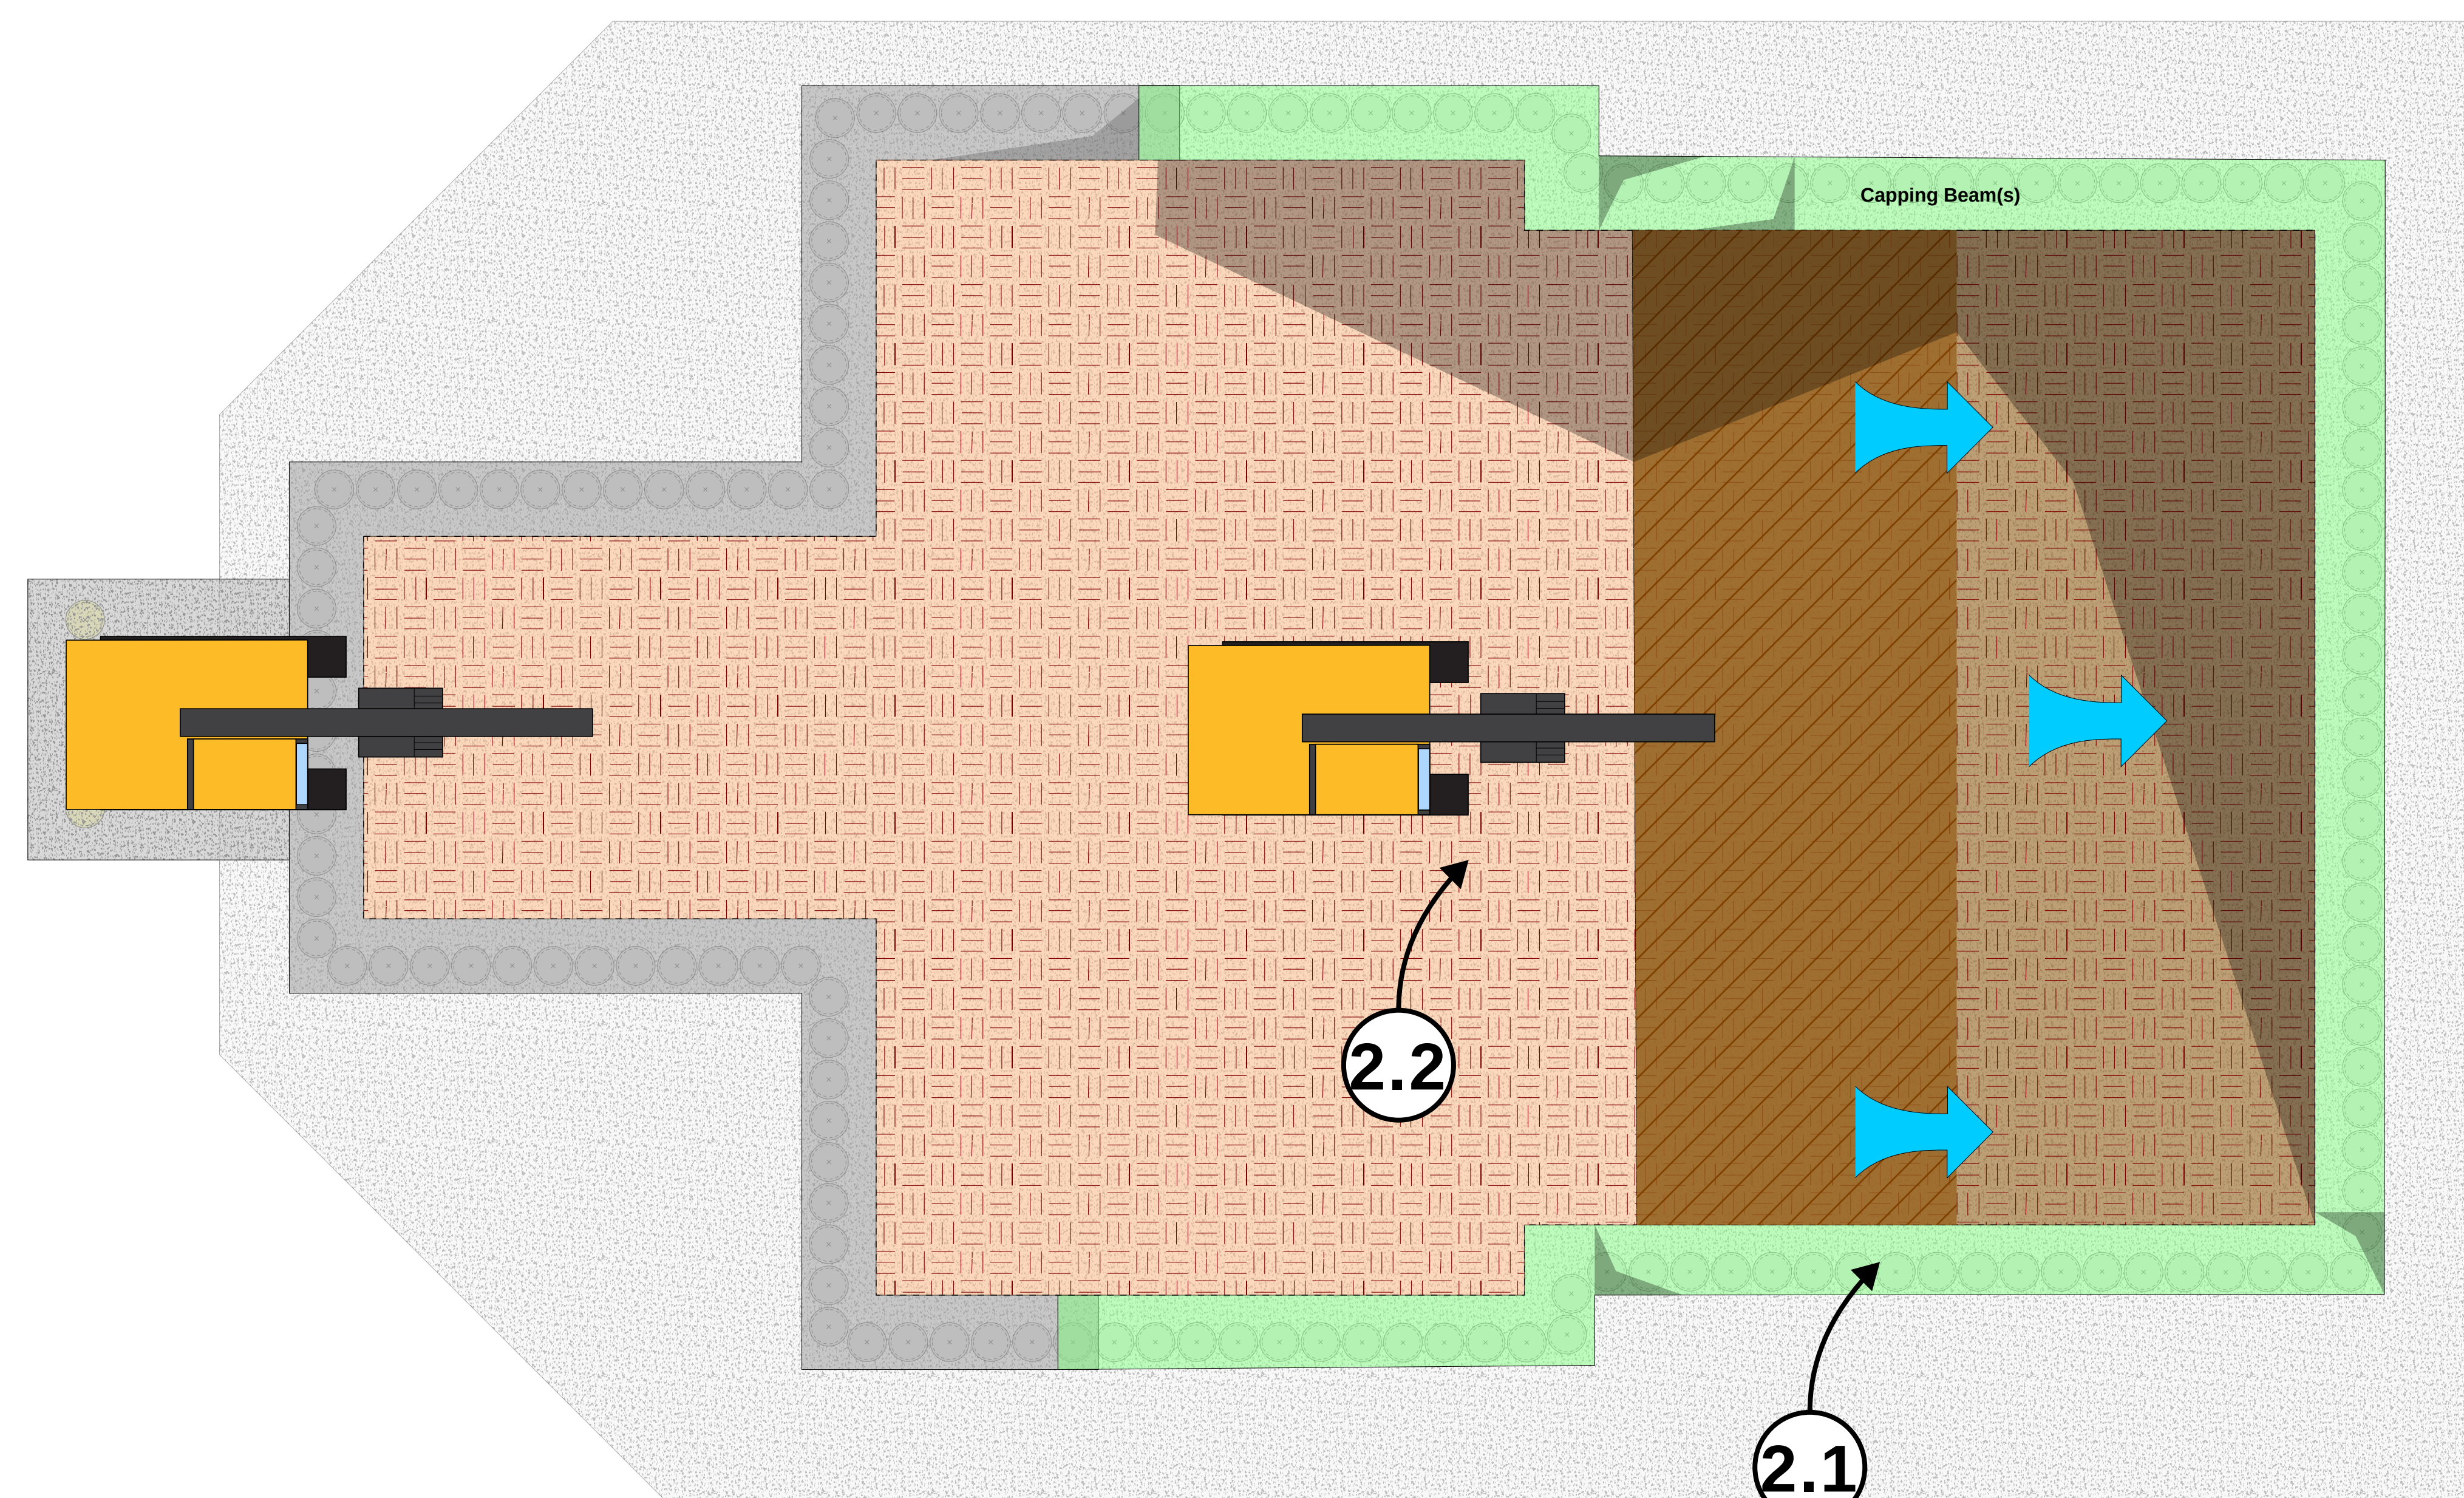

PLAN

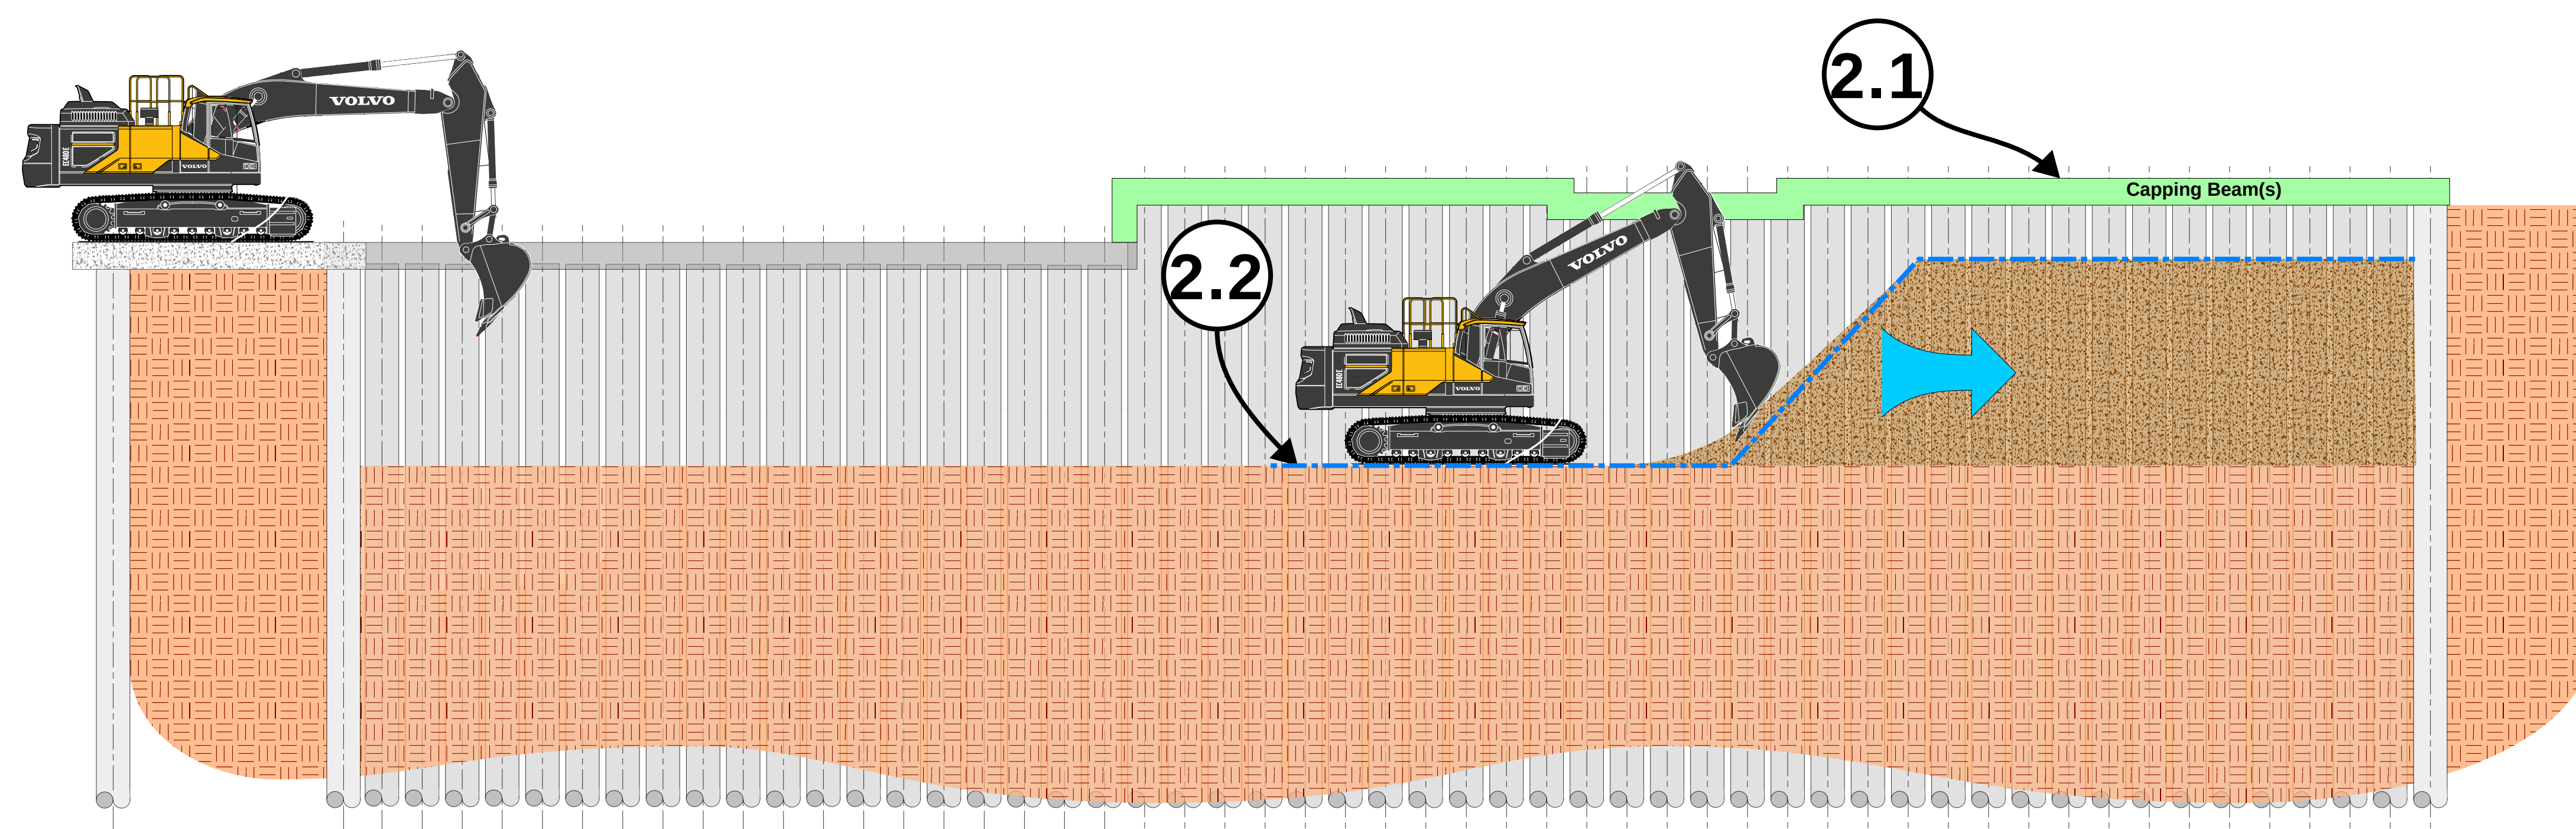

SECTION



NOTE

PROVISIONAL SEQUENCE OF WORKS

- 2.1) Install remainder of RC capping Beams at GF level
- 2.2) Undertake Early reduce in levels down to just below proposed Mezzanine Level

[illegible]

SIZE GROUP

STRUCTURES

DRAWN BY CP	CHECKED BY	DATE 17 / 10 / 25
----------------	------------	----------------------


CONTRACT
TOTTENHAM HOUS

REFERENCE
POOL HOUSE


PROVISIONAL CONSTRUCTION SEQUENCE (STAGE 2 of 7)

SCALE (@ A1) SEE SCALE BAR	PROJECT NUMBER ST23-04	
DRAWING NUMBER ST24-SOW-002		REV 0

③

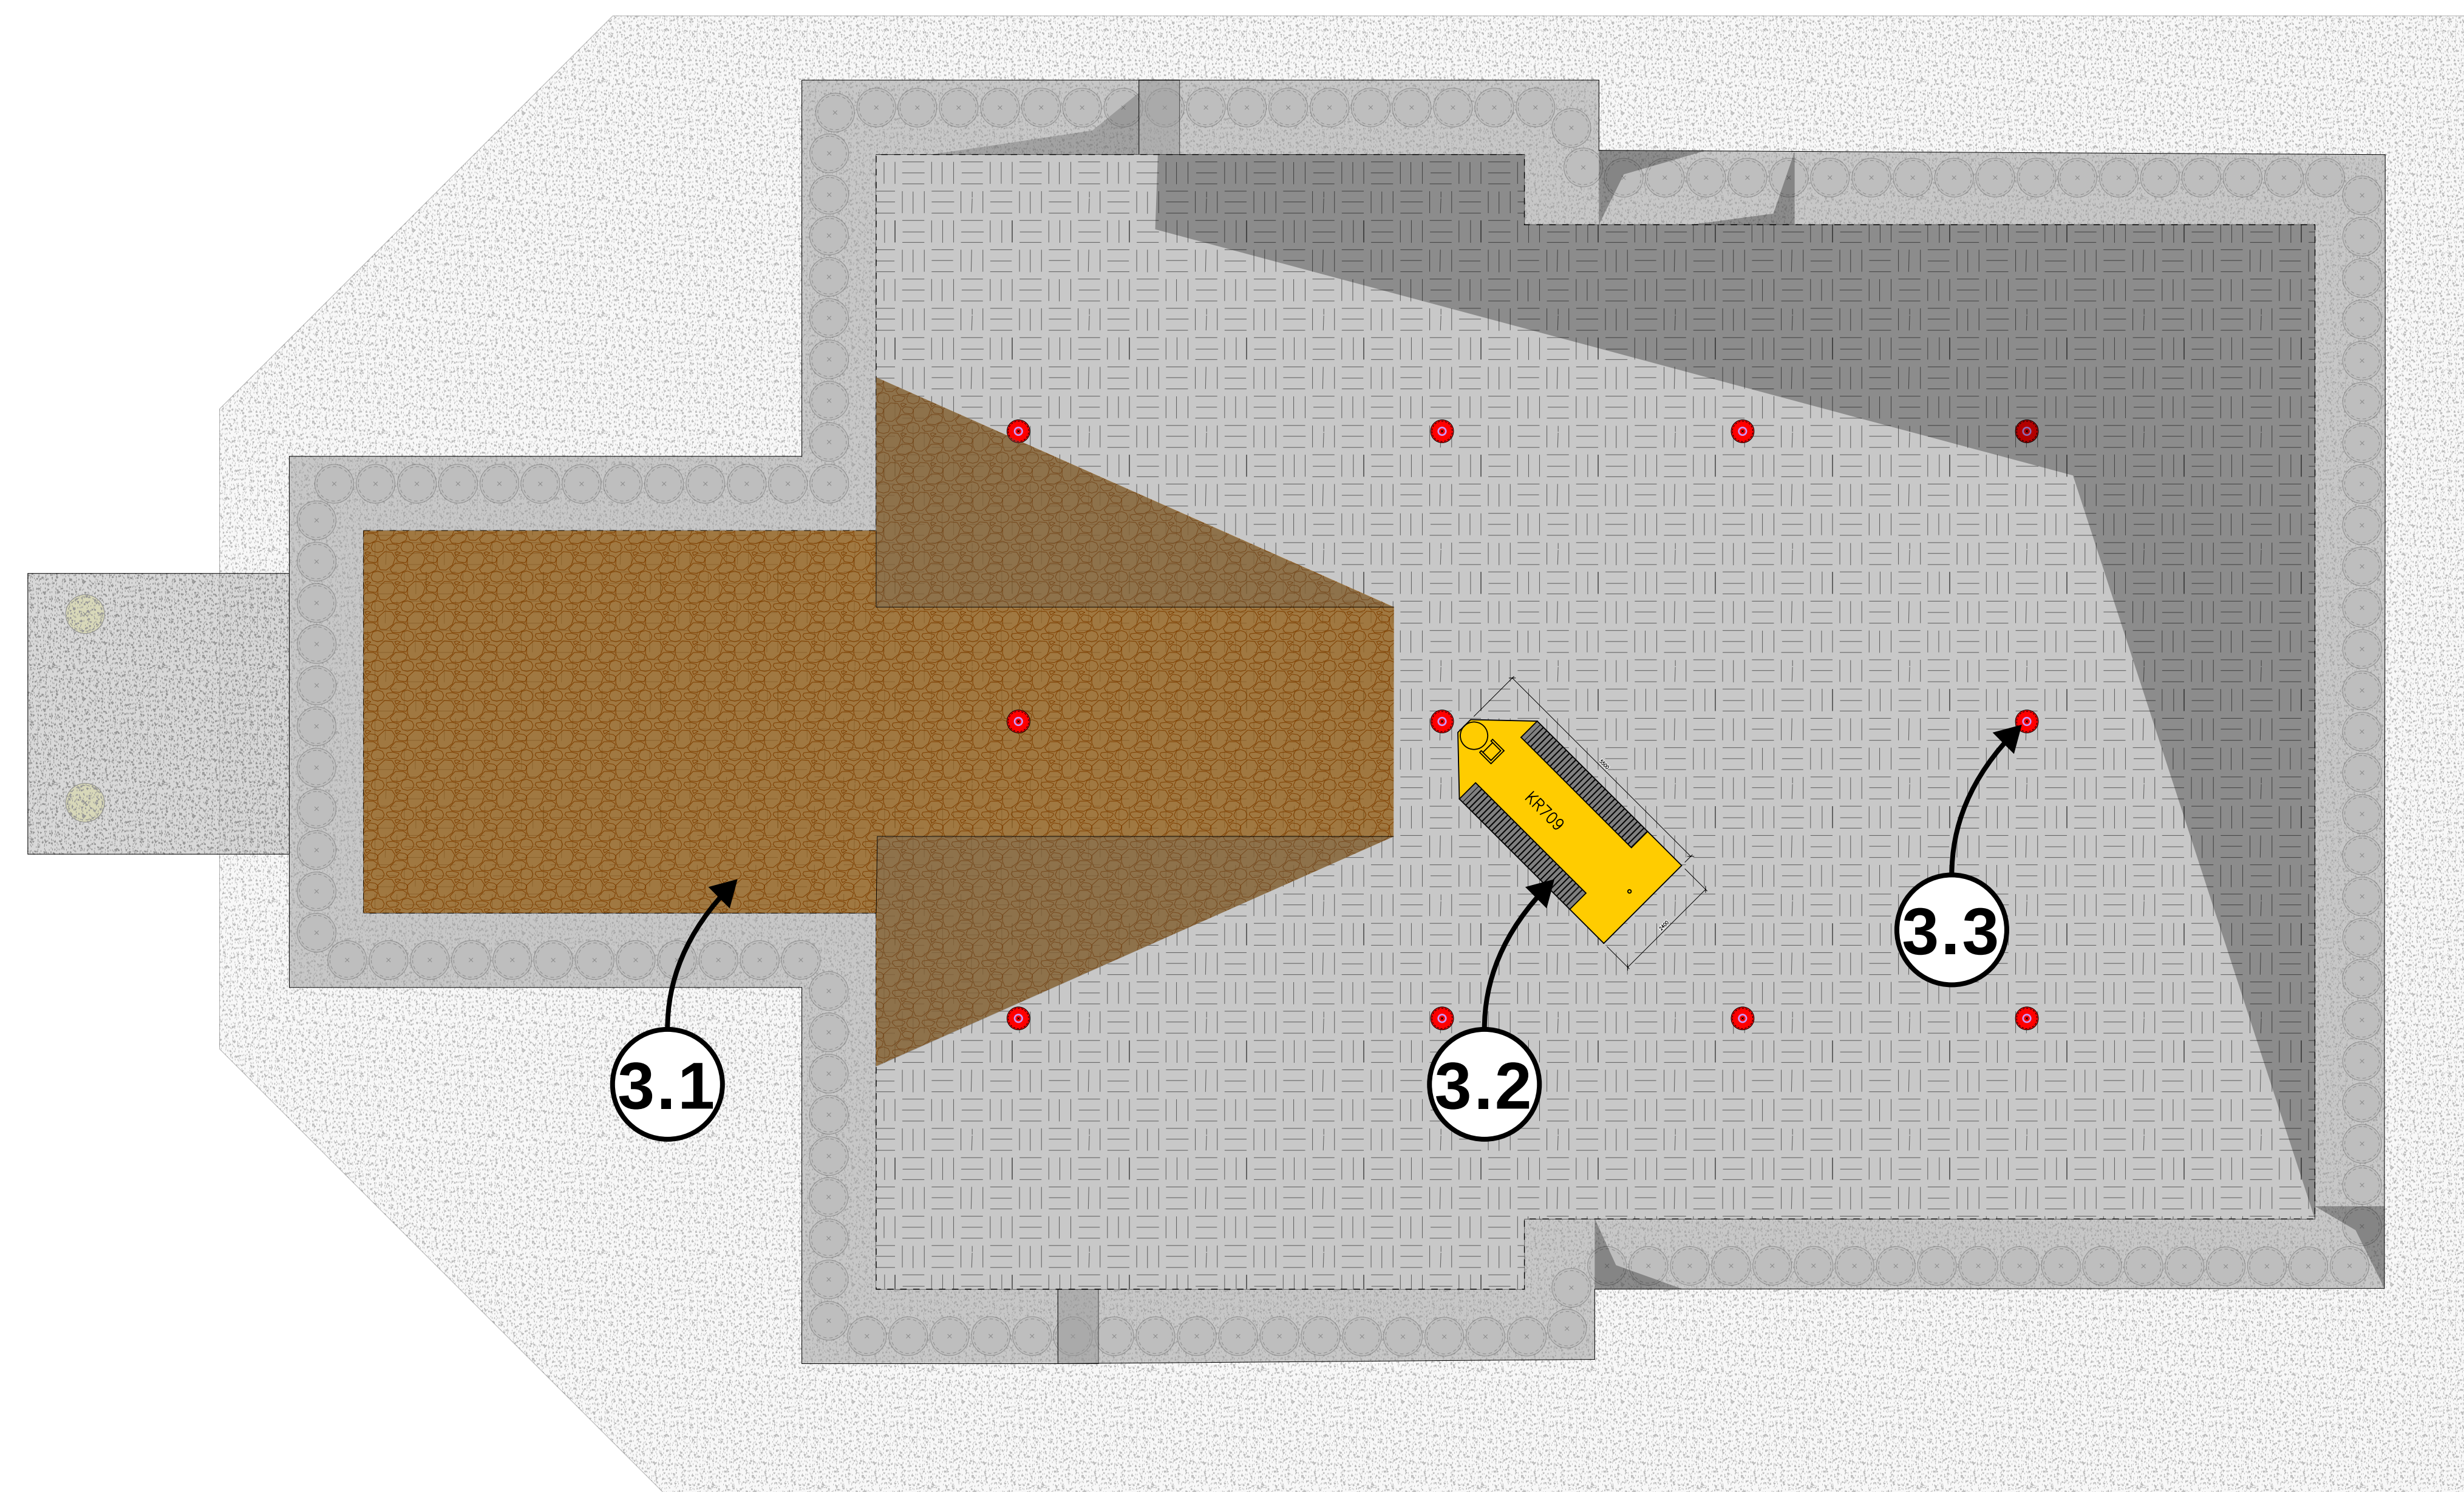

PLAN

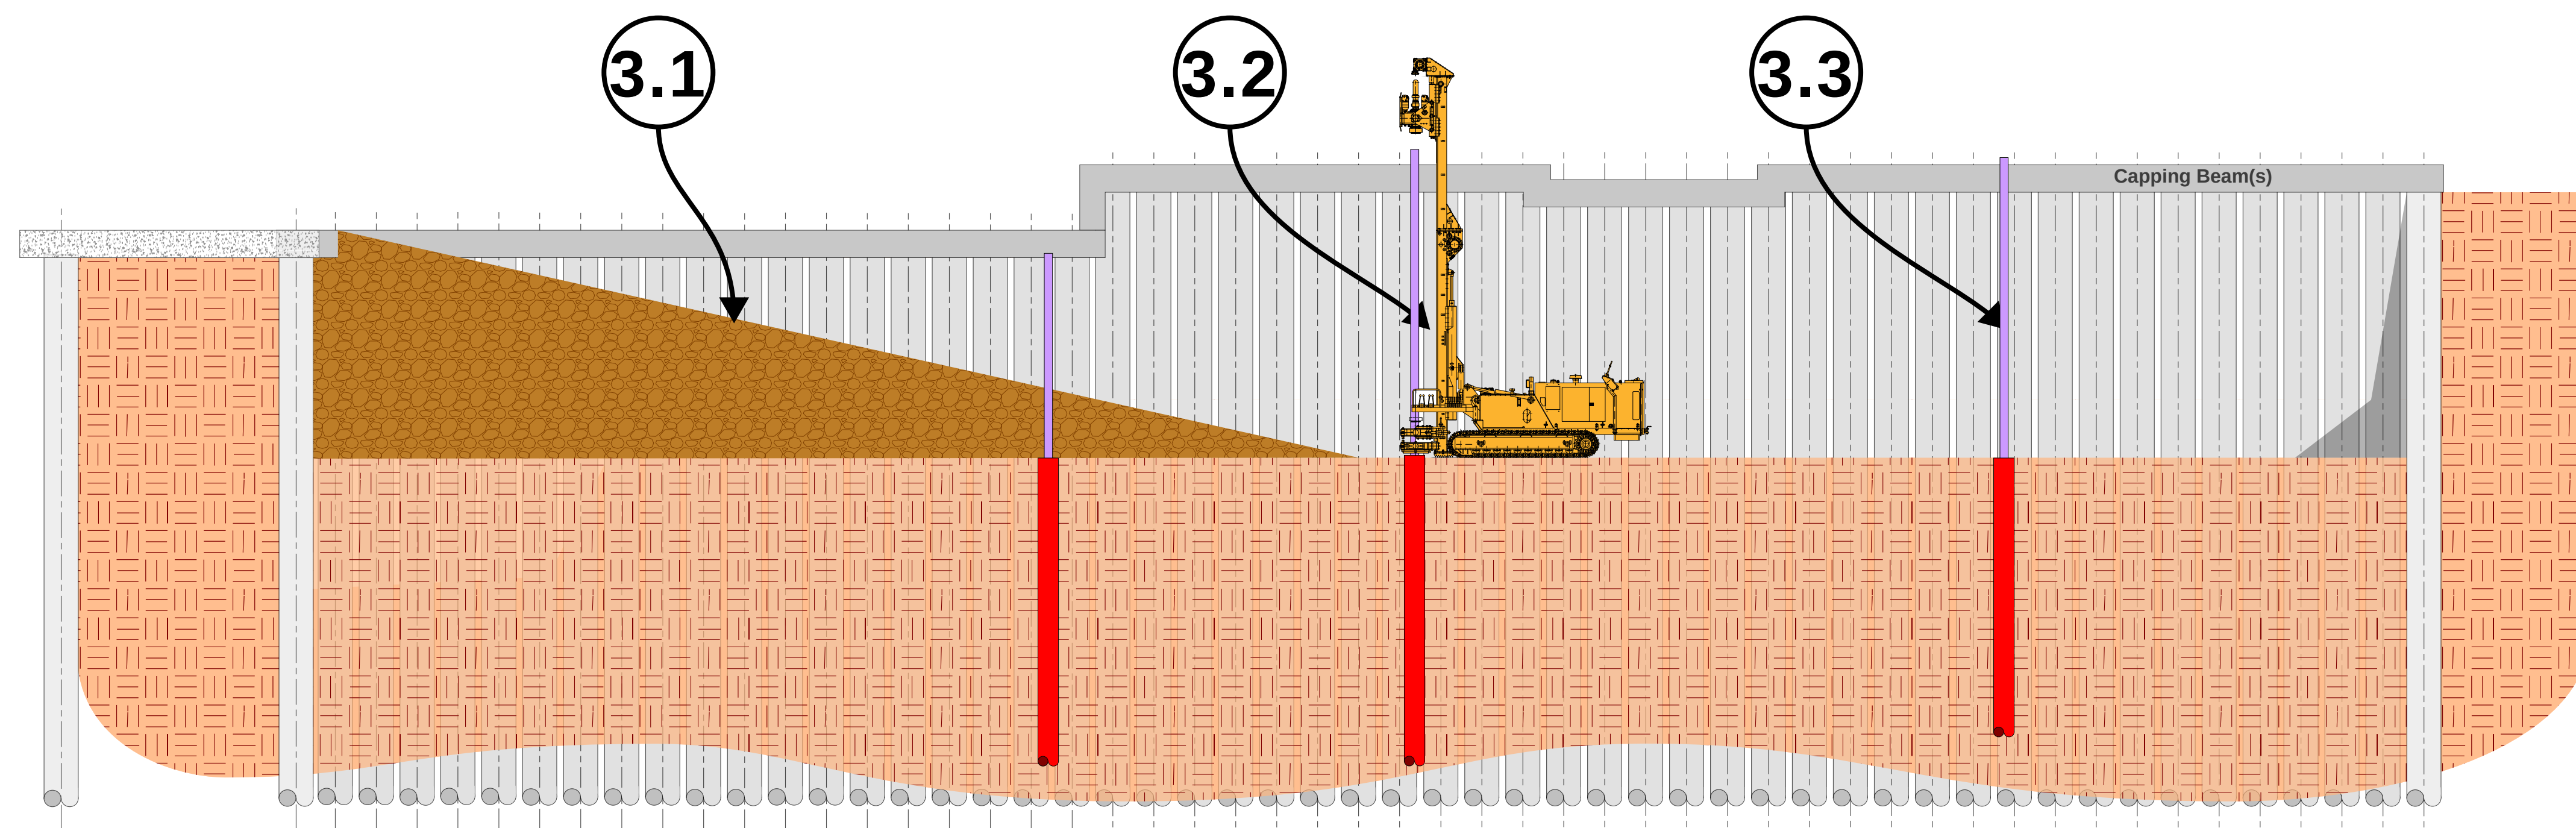

SECTION

NOTES

PROVISIONAL SEQUENCE OF WORKS

- 3.1) Finalise Ramp into site, suitable for proposed Mini Piling rig**
- 3.2) Provide Piling surface at Reduced Level & Mobilise Suitable Mini-Piling rig**
- 3.3) Install a number of Temporary Bearing Piles with Steel Plunge Sections extending up to Underside of Ground Floor Slab Levels**

[illegible]

SIZE GROUP

STRUCTURES

DRAWN BY CP	CHECKED BY	DATE 17/10/25
----------------	------------	------------------


CONTRACT
TOTTENHAM HOUSE

REFERENCE
POOL HOUSE


PROVISIONAL CONSTRUCTION SEQUENCE (STAGE 3 of 7)

SCALE (@ A1) SEE SCALE BAR	PROJECT NUMBER ST23-04
DRAWING NUMBER ST24-SOW-003	REV 0


4

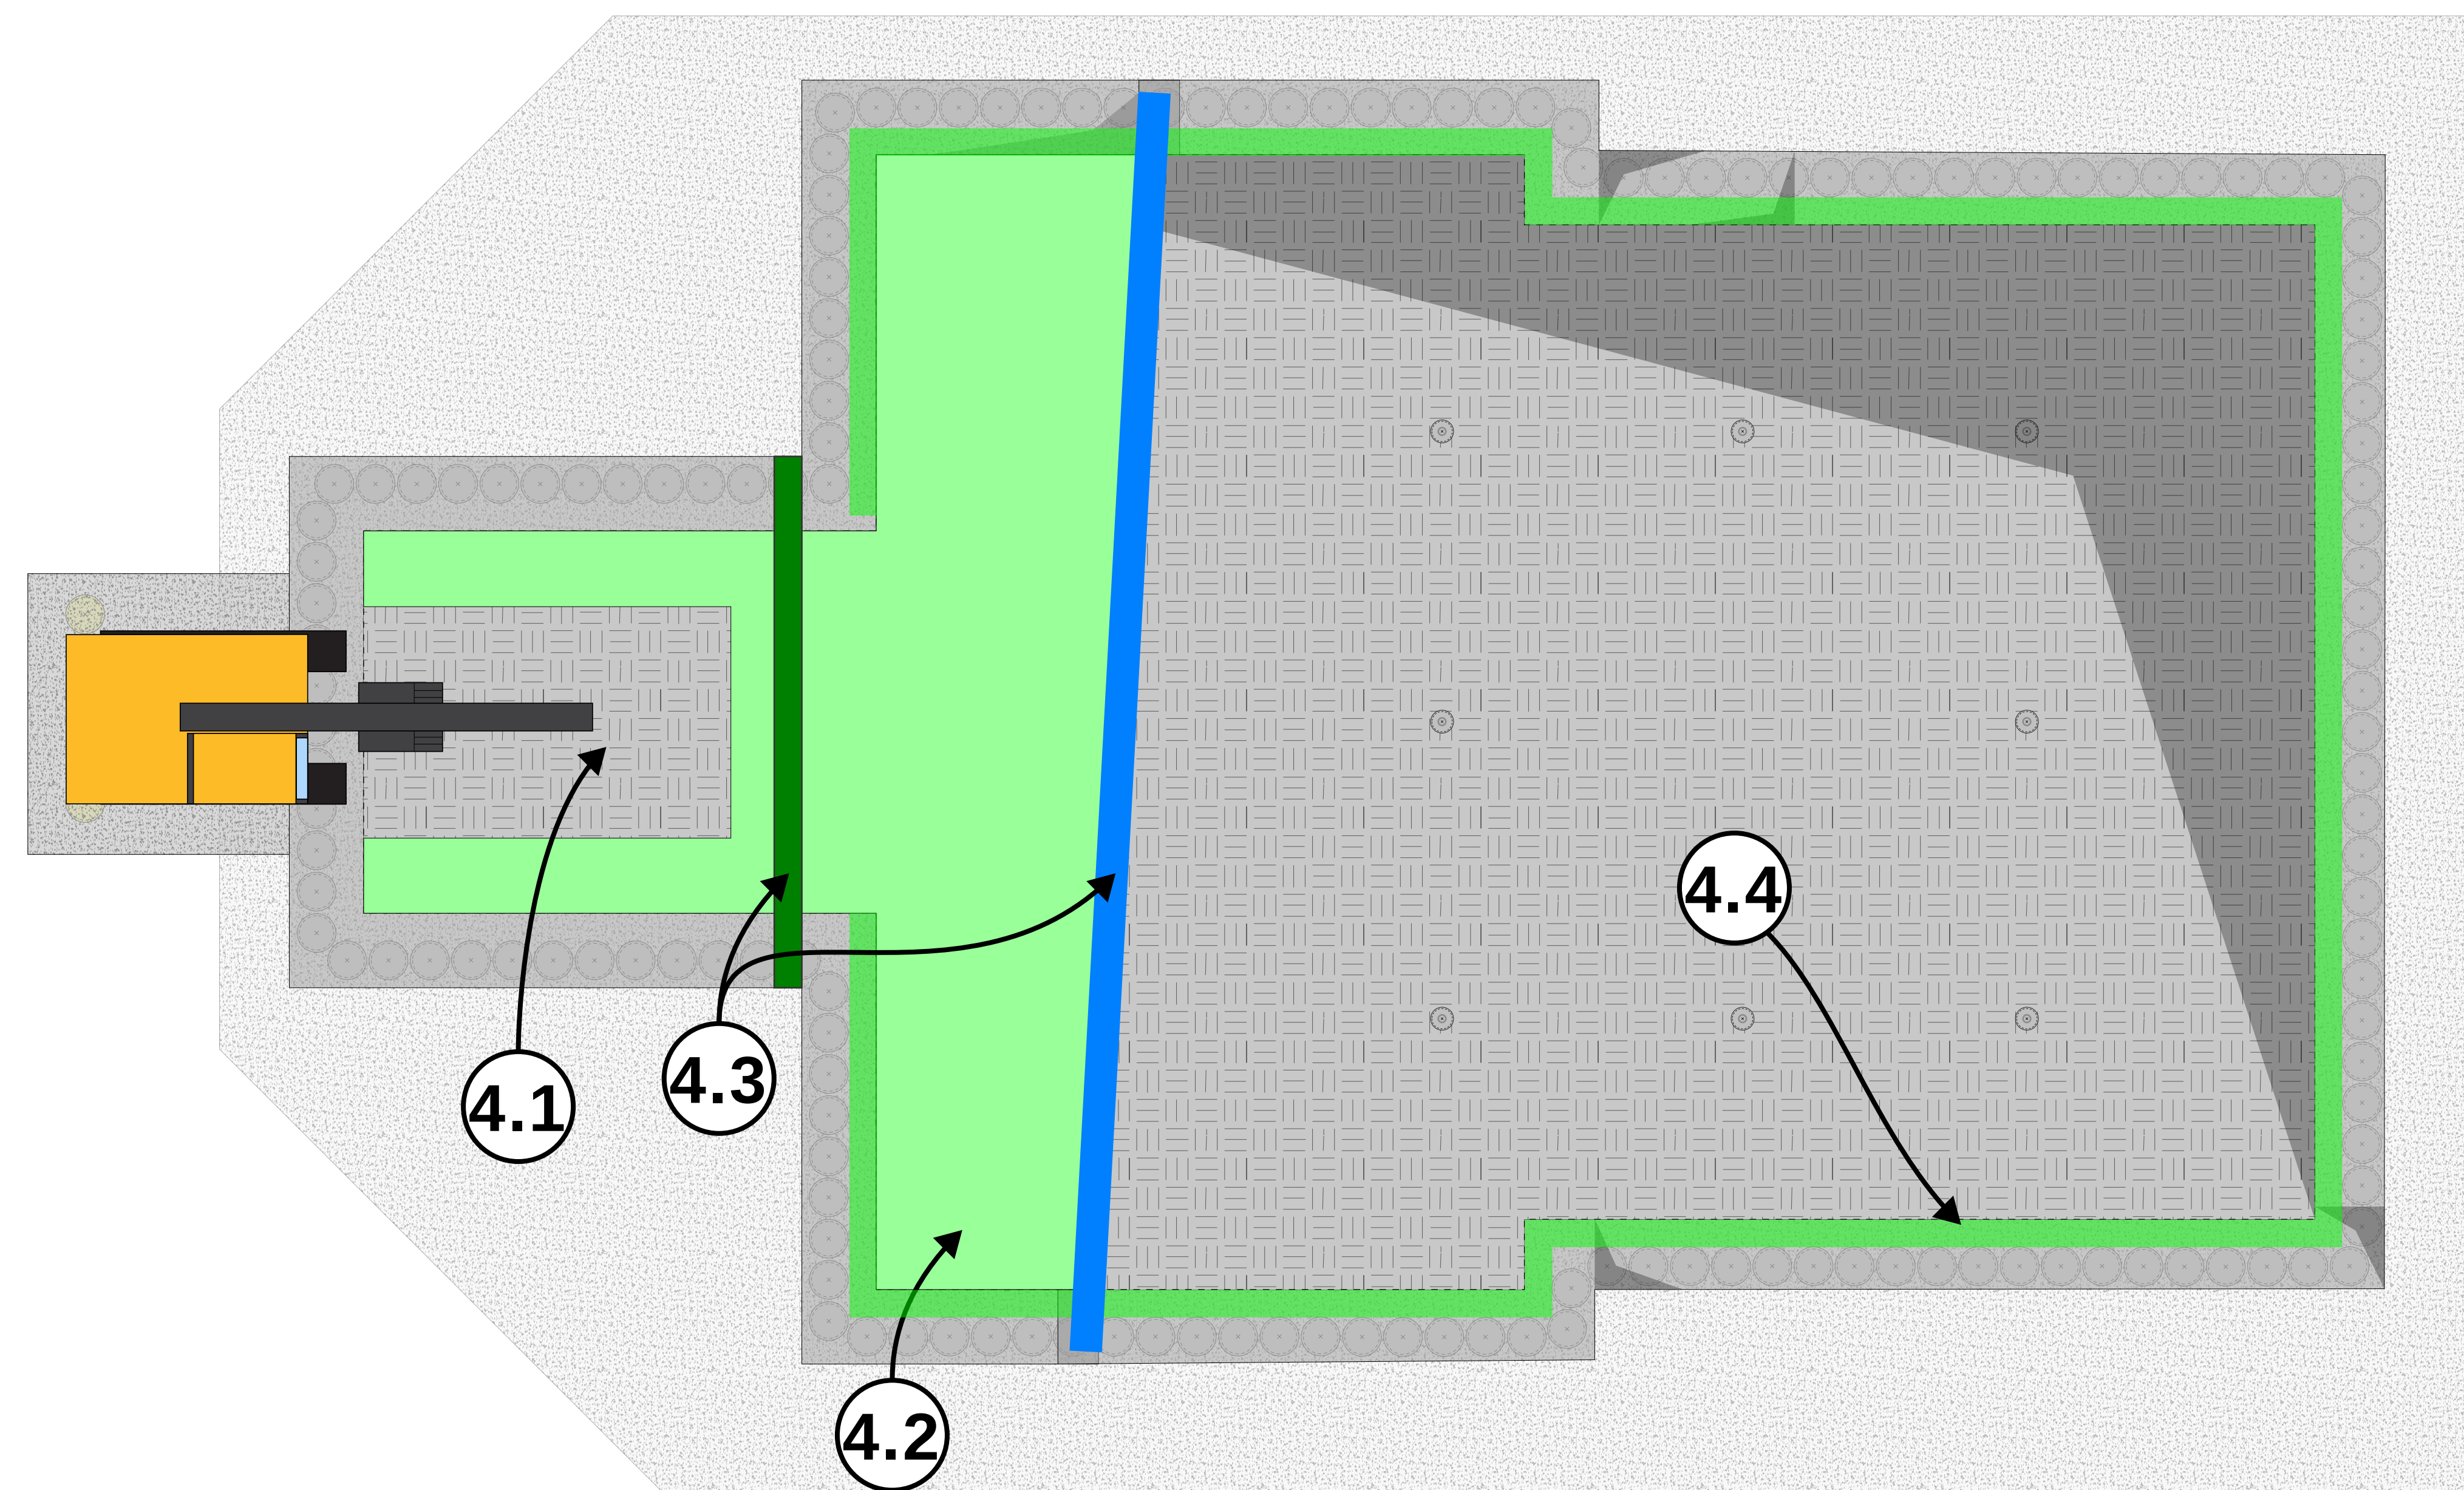

PLAN

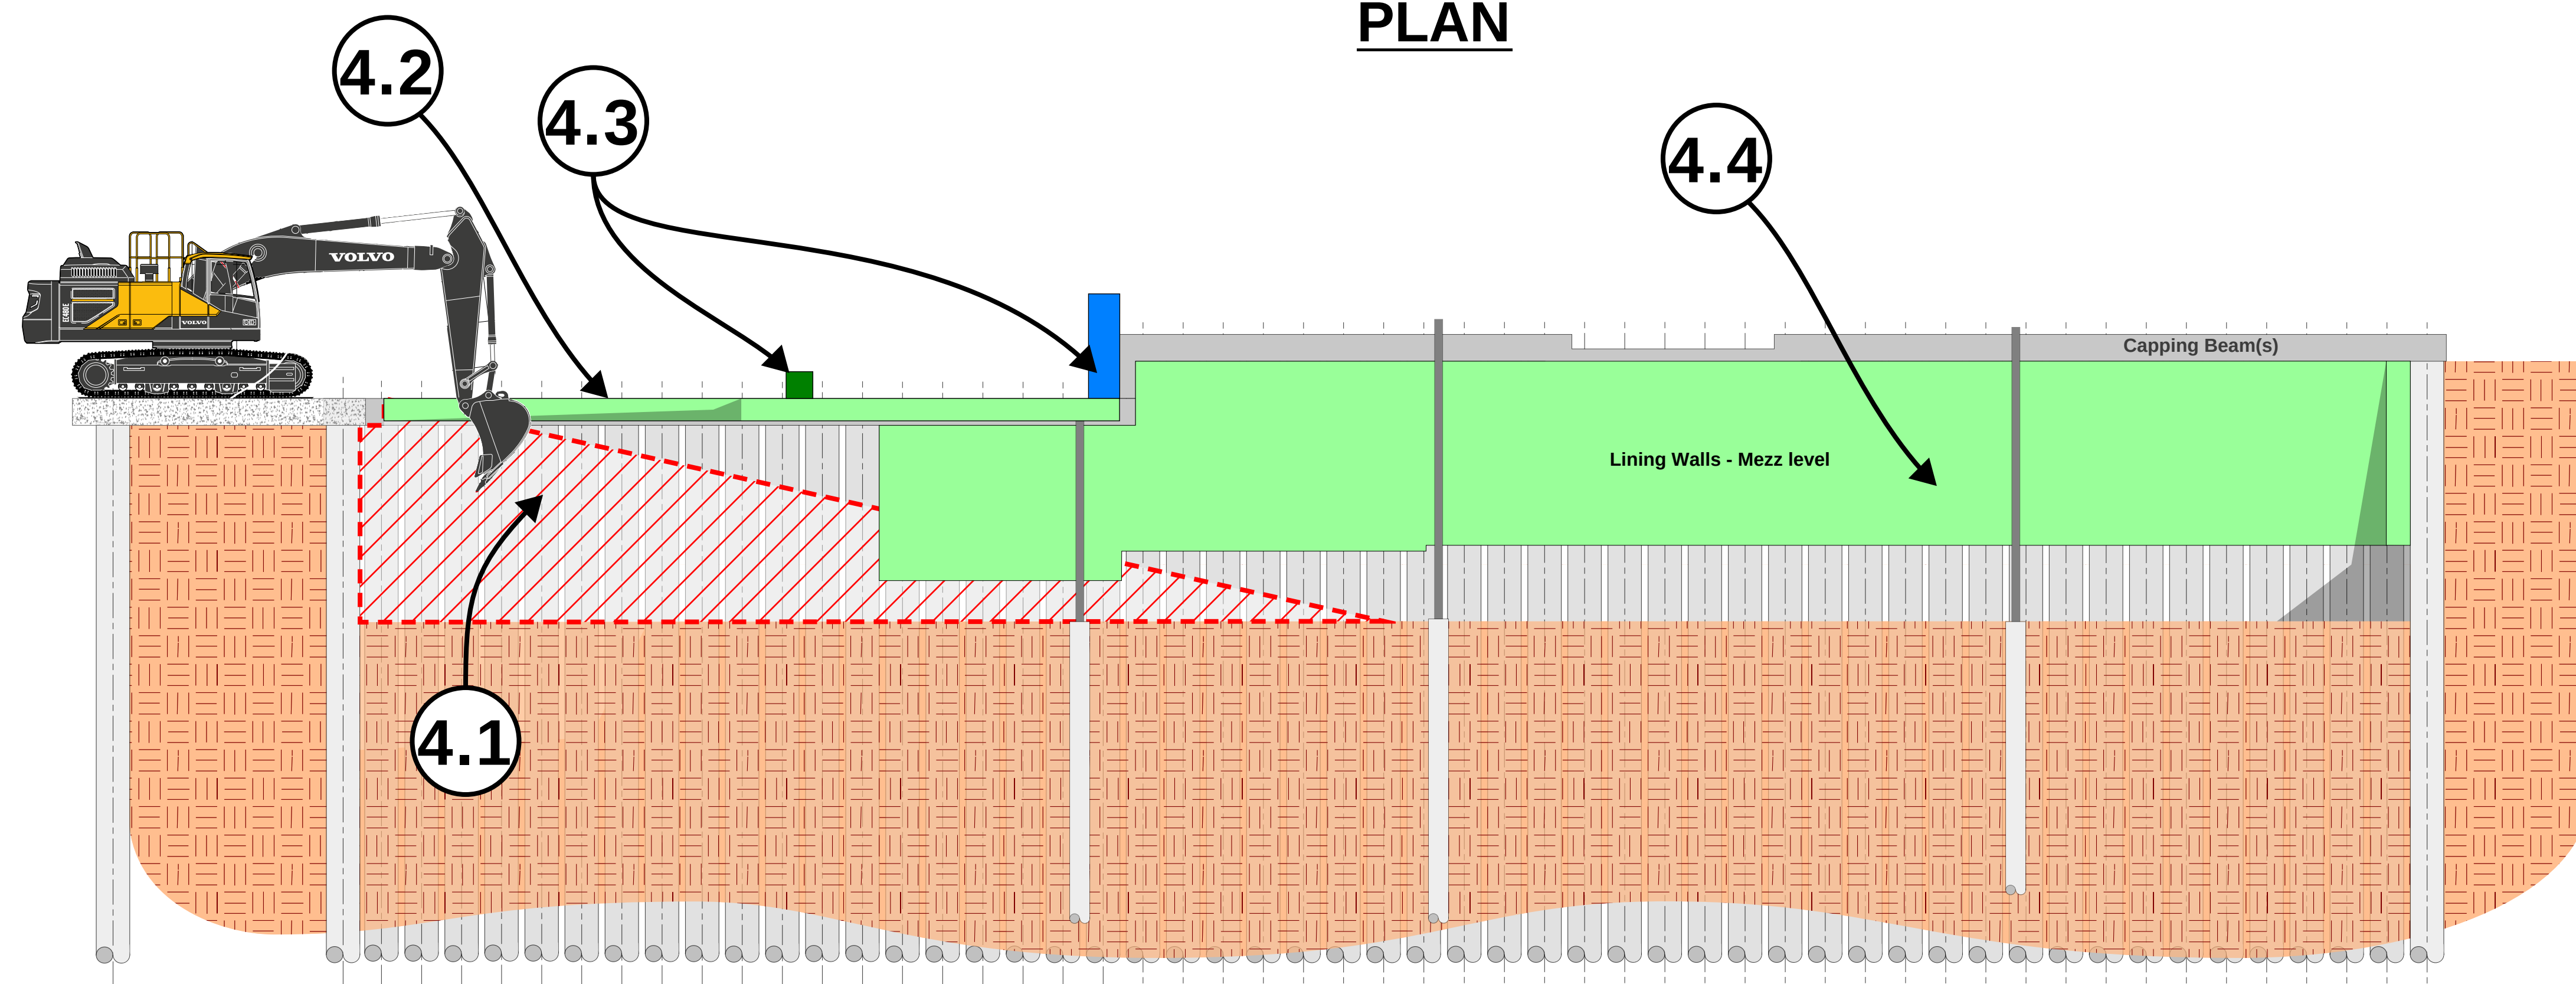

SECTION



NOTES

PROVISIONAL SEQUENCE OF WORKS

- 4.1) Remove Ramp
- 4.2) Construct lowest section of proposed GF RC slab, leaving aperture for continued excavations
- 4.3) Construct RC 'Upstand' Beam & Thickened RC 'Cross' wall to previously installed RC Slab
- 4.4) Construct RC Lining walls to RHS of 'Cross Wall'

[illegible]

SIZE GROUP

STRUCTURES

DRAWN BY CP	CHECKED BY	DATE 17 / 10 / 25
----------------	------------	----------------------



CONTRACT
TOTTENHAM HOUSE

REFERENCE
POOL HOUSE

PROVISIONAL CONSTRUCTION SEQUENCE (STAGE 4 of 7)

SCALE (@ A1)	PROJECT NUMBER	
SEE SCALE BAR	ST23-04	
DRAWING NUMBER		REV
ST24-SOW-004		0

5

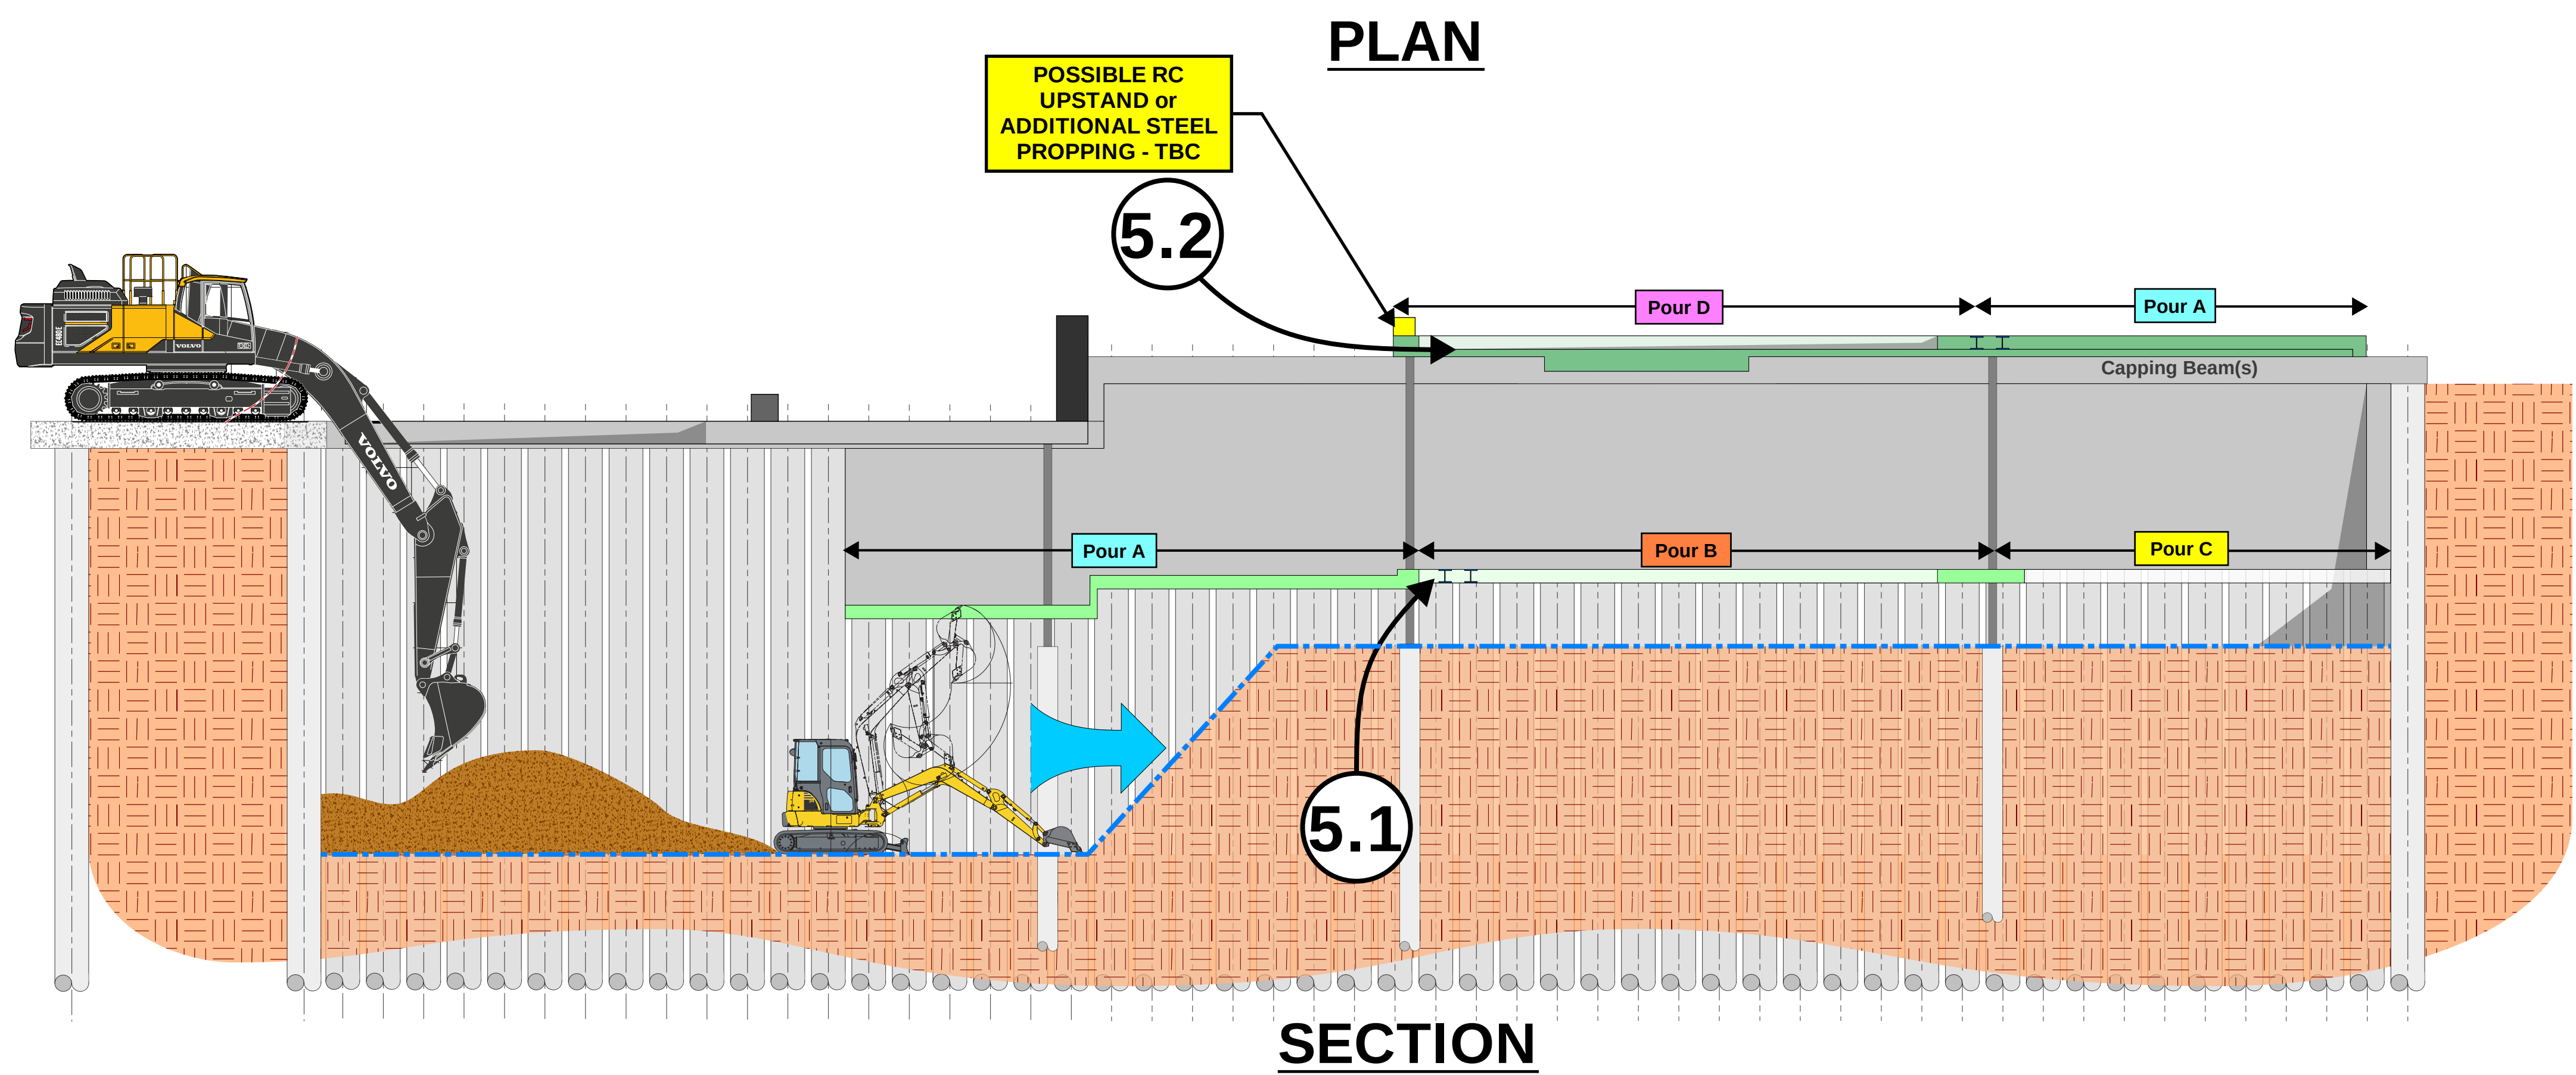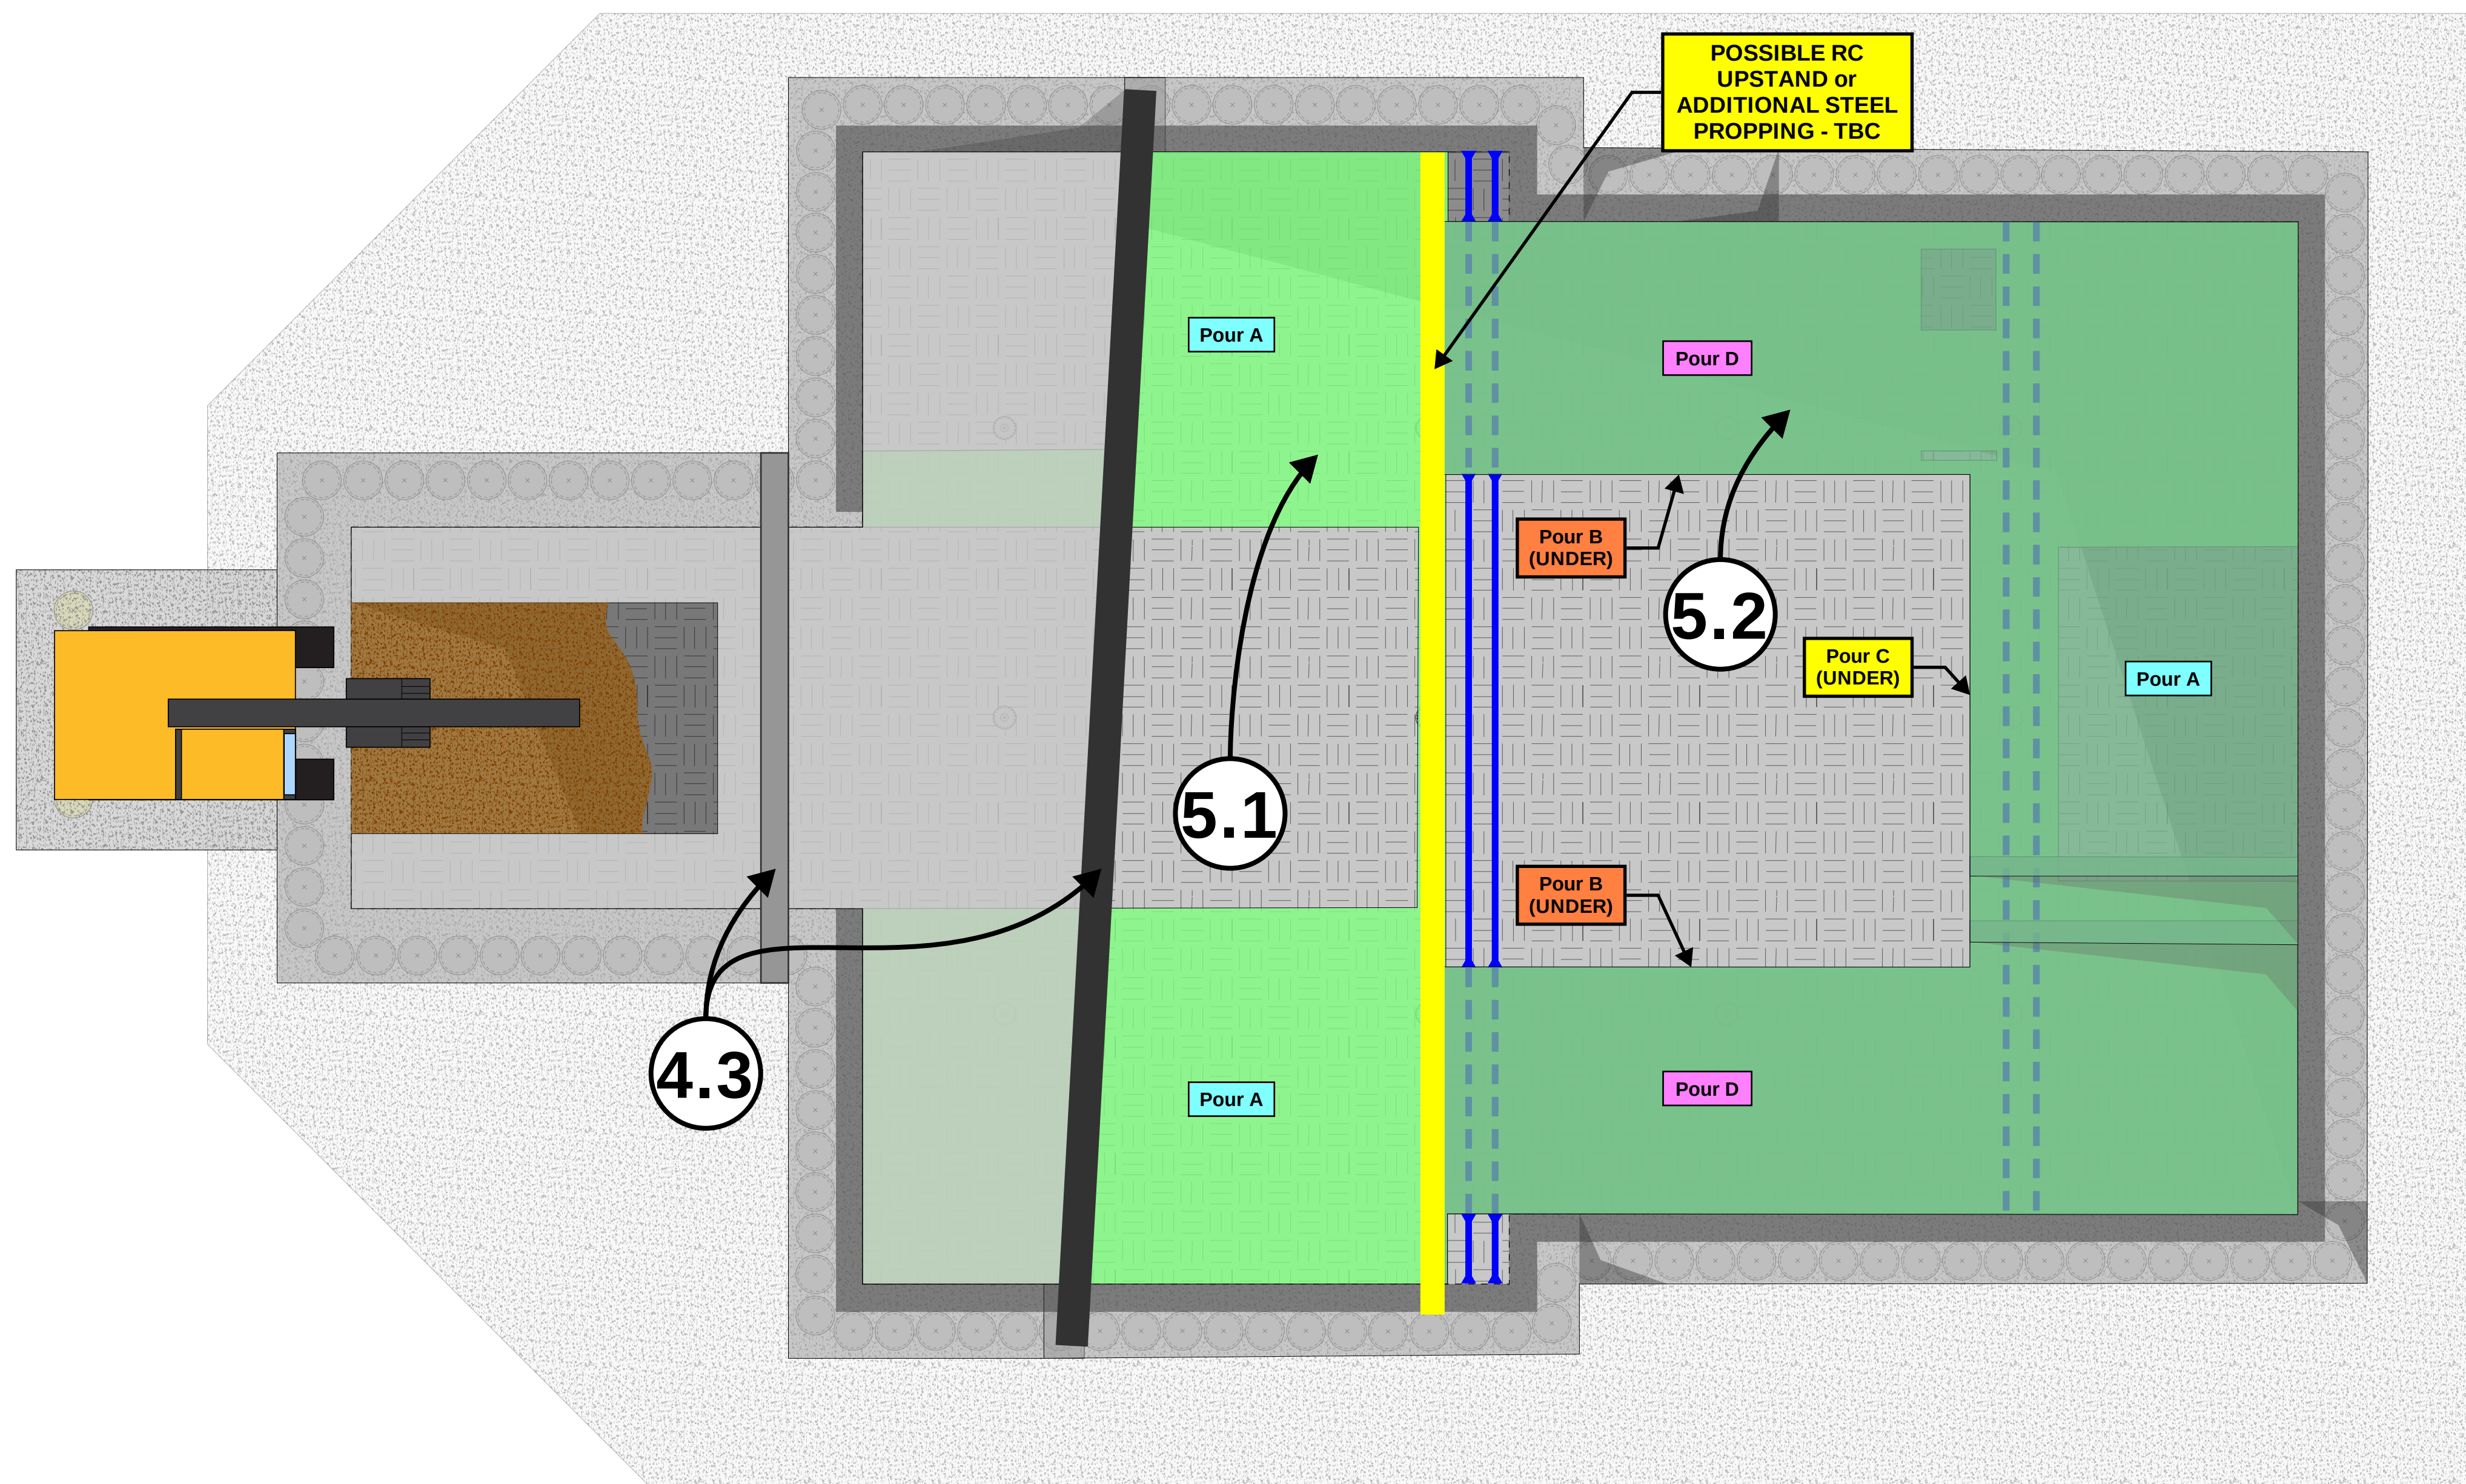

PROVISIONAL SEQUENCE OF WORKS

- 5.1) Construct Mezzanine Level Slabs, providing Temporary / sacrificial horizontal propping
- 5.2) Construct Ground Floor Level Slabs, providing sacrificial horizontal propping
- 5.3) After an appropriate curing period of 'Pour A' at Mezzanine level, excavation to Basement formation level can commence, starting at and working away from mining access aperture.

[illegible]

SIZE GROUP

STRUCTURES

DRAWN BY CP	CHECKED BY	DATE 17 / 10 / 25
----------------	------------	----------------------

CONTRACT
TOTTENHAM HOUSE

REFERENCE
POOL HOUSE

PROVISIONAL CONSTRUCTION SEQUENCE (STAGE 5 of 7)


SCALE (@ A1)
SEE SCALE BAR

PROJECT NUMBER
ST23-04


DRAWING NUMBER
ST24-SOW-005

REV
0

6

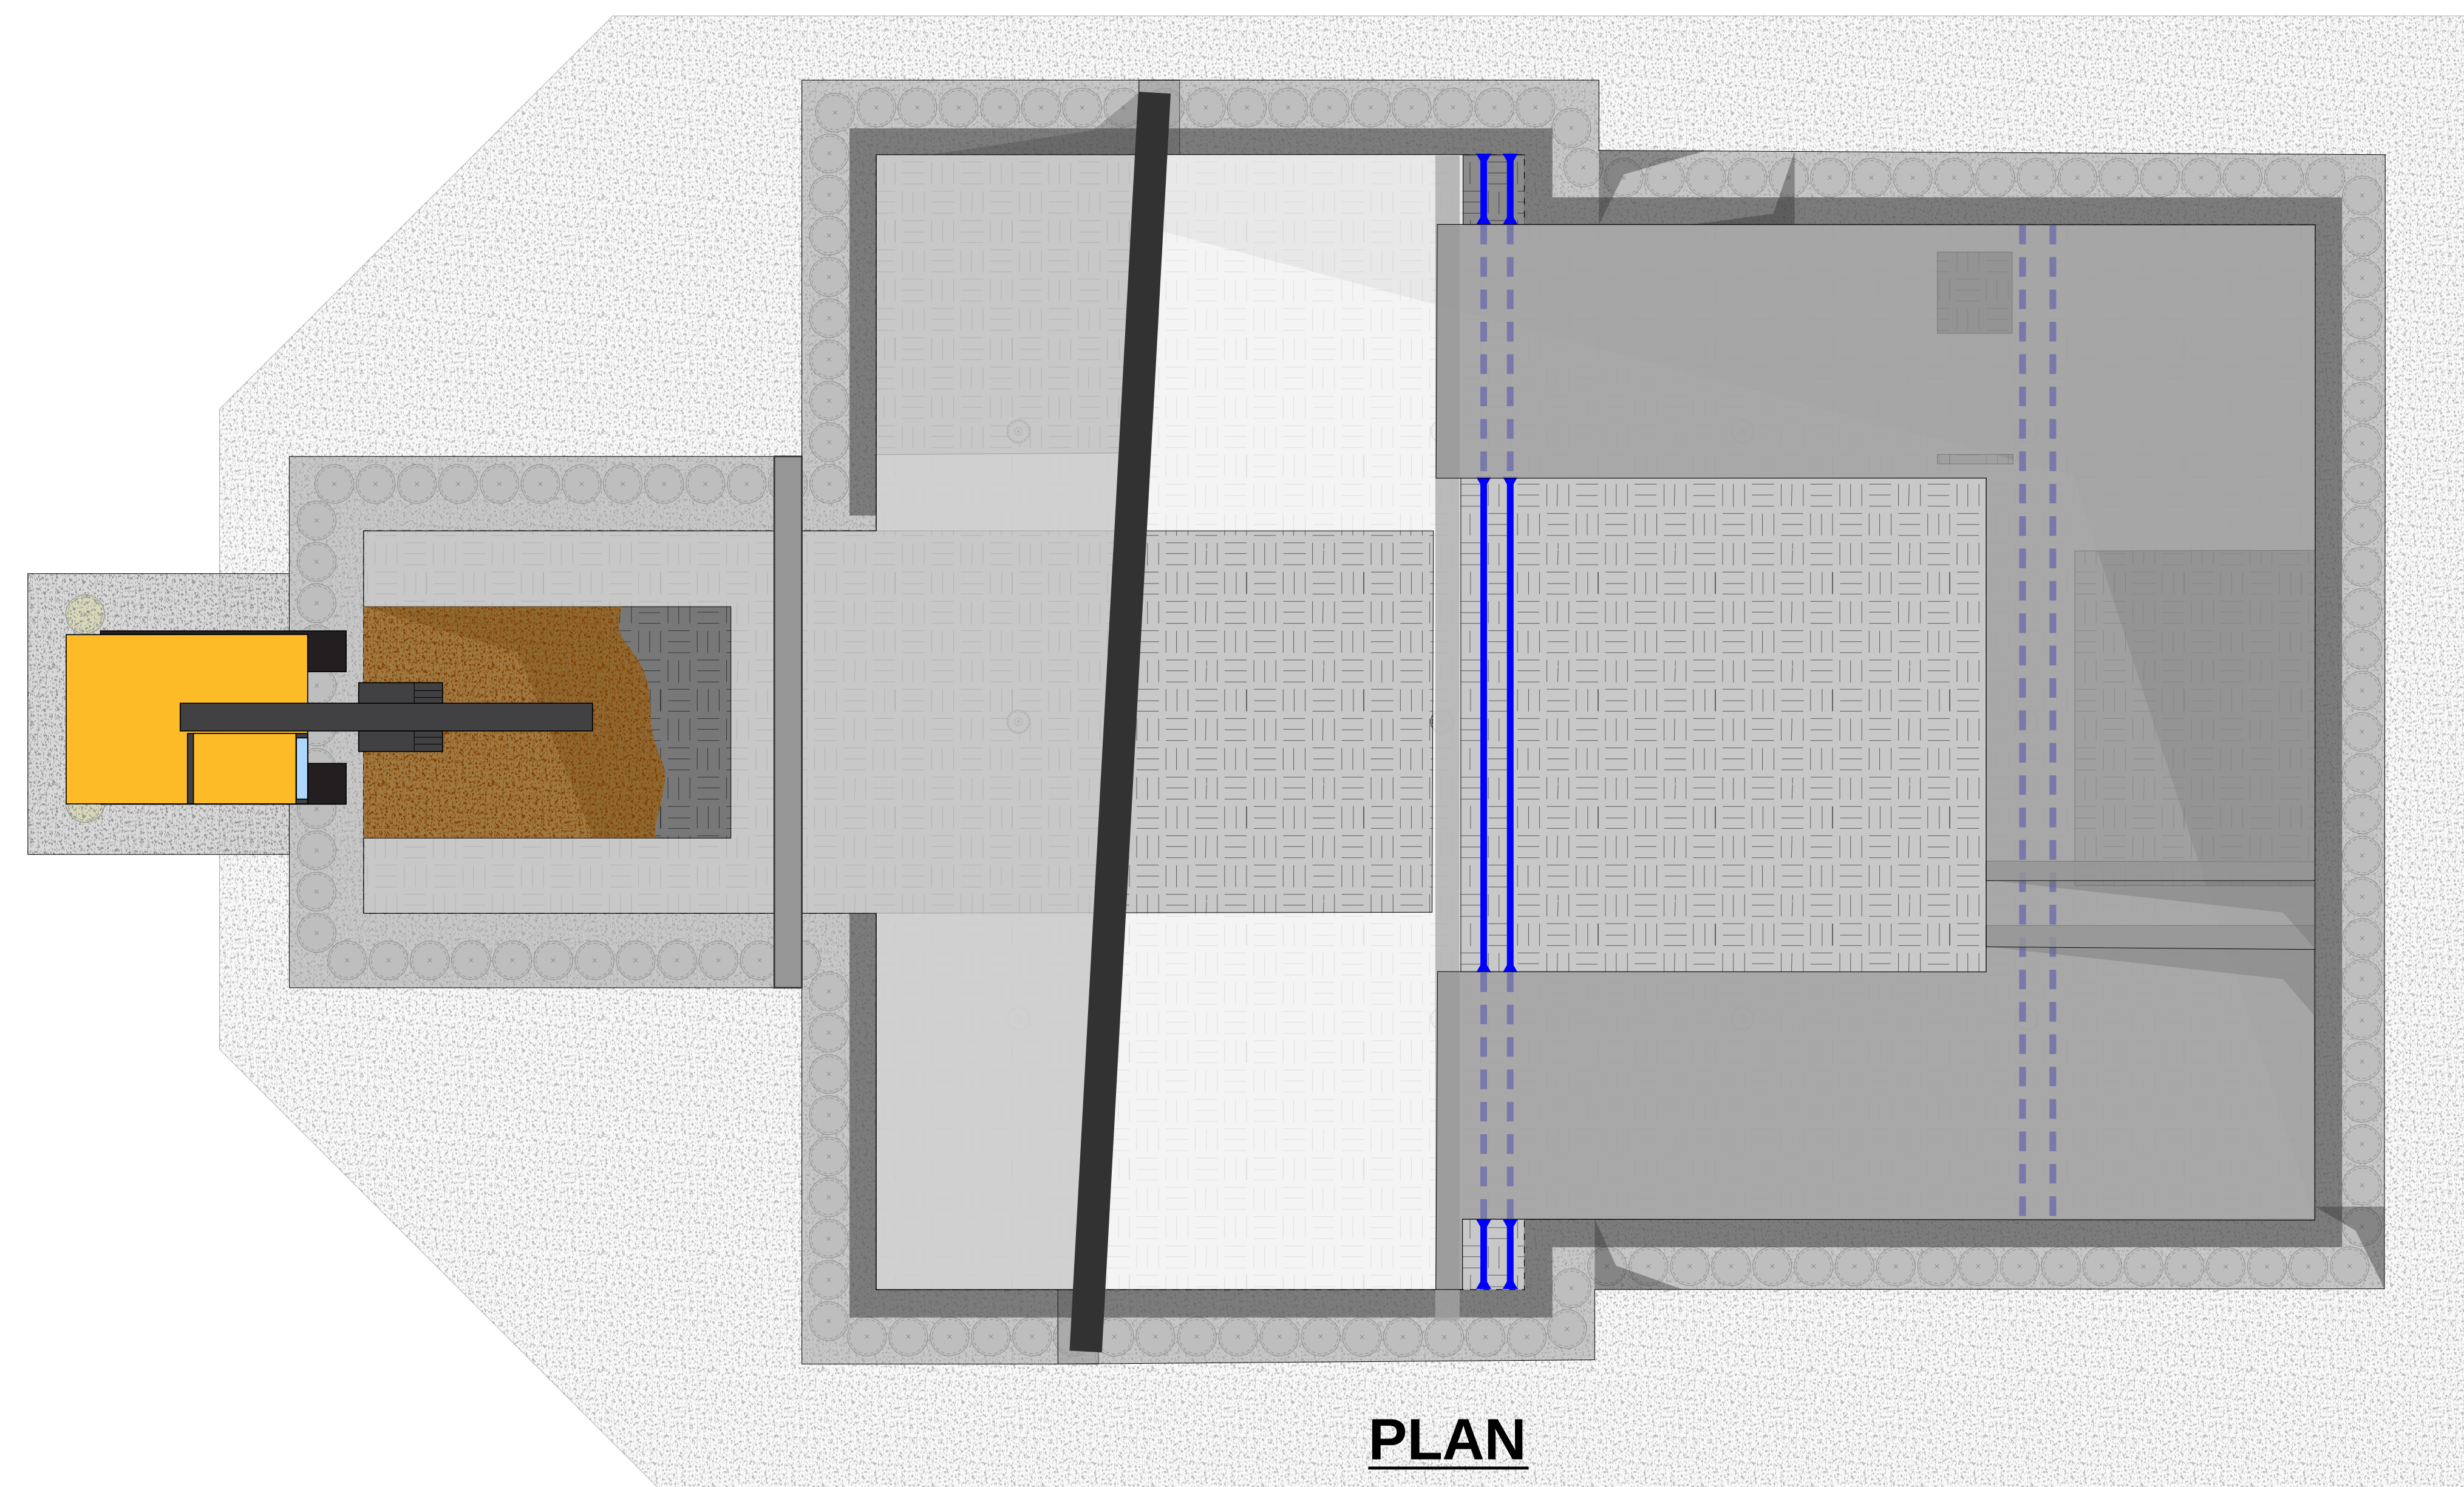

PLAN

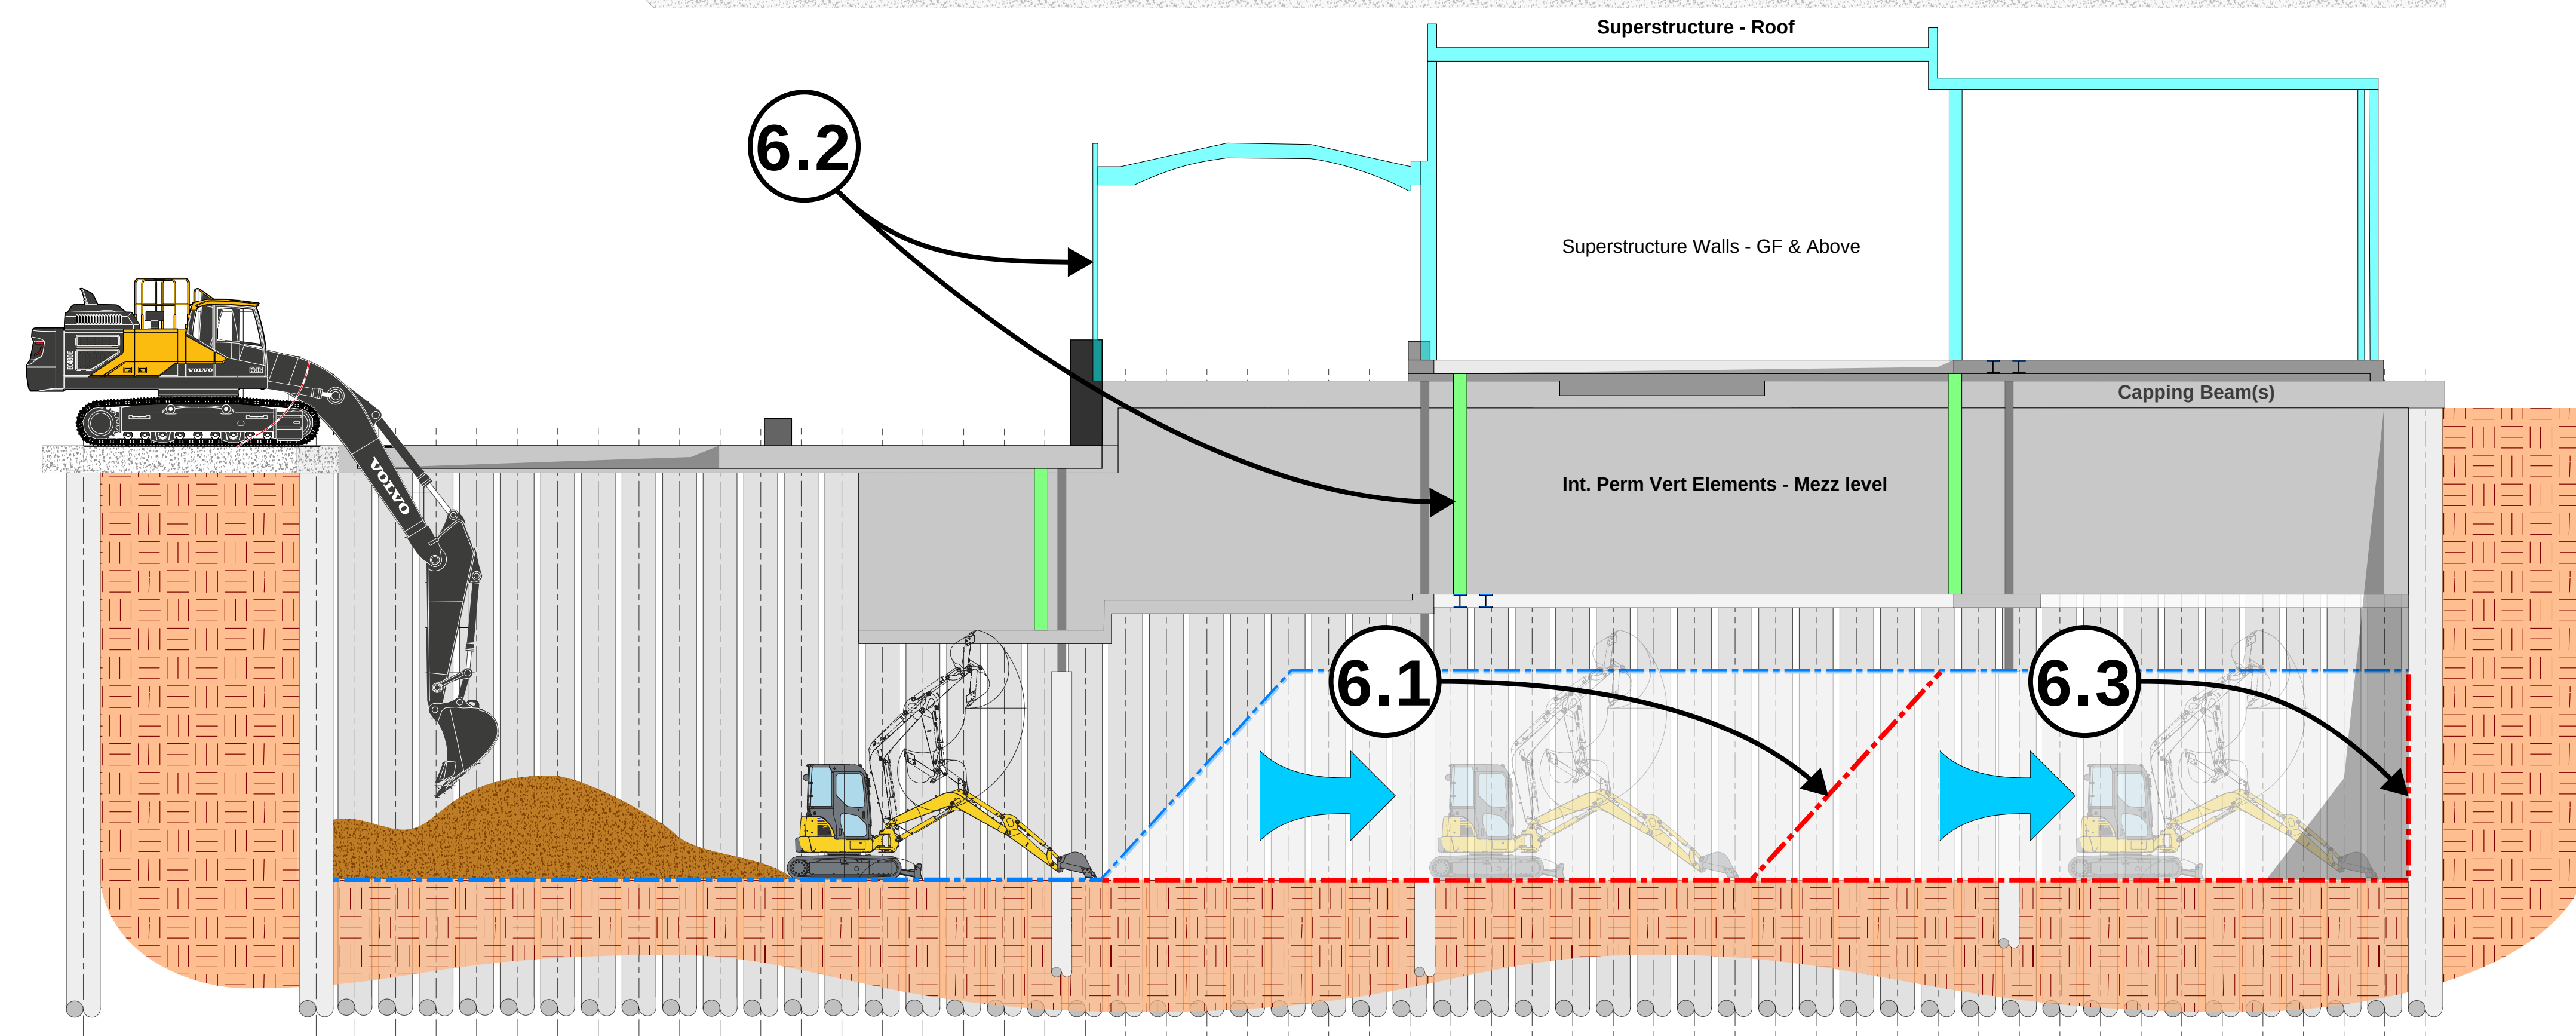

SECTION

NOTES:

PROVISIONAL SEQUENCE OF WORKS

- 6.1) Undertake progression of further Reduction in levels to proposed Basement formation level
- 6.2) Commence Superstructures RC works from Mezzanine Level upwards, following sufficient curing time
(Not shown graphically on Plan)
- 6.3) Complete excavation works down to Basement formation level across the entire Basement footprint

[illegible]

SIZE GROUP

STRUCTURES

DRAWN BY CP	CHECKED BY	DATE 17 / 10 / 25
----------------	------------	----------------------

CONTRACT
TOTTENHAM HOUSE

REFERENCE
POOL HOUSE

PROVISIONAL CONSTRUCTION SEQUENCE (STAGE 6 of 7)

SCALE (@ A1)	PROJECT NUMBER
--------------	----------------


SEE SCALE BAR

SEE SOURCE DATA
DRAWING NUMBER
ST24-SOW-006


REV

0


7

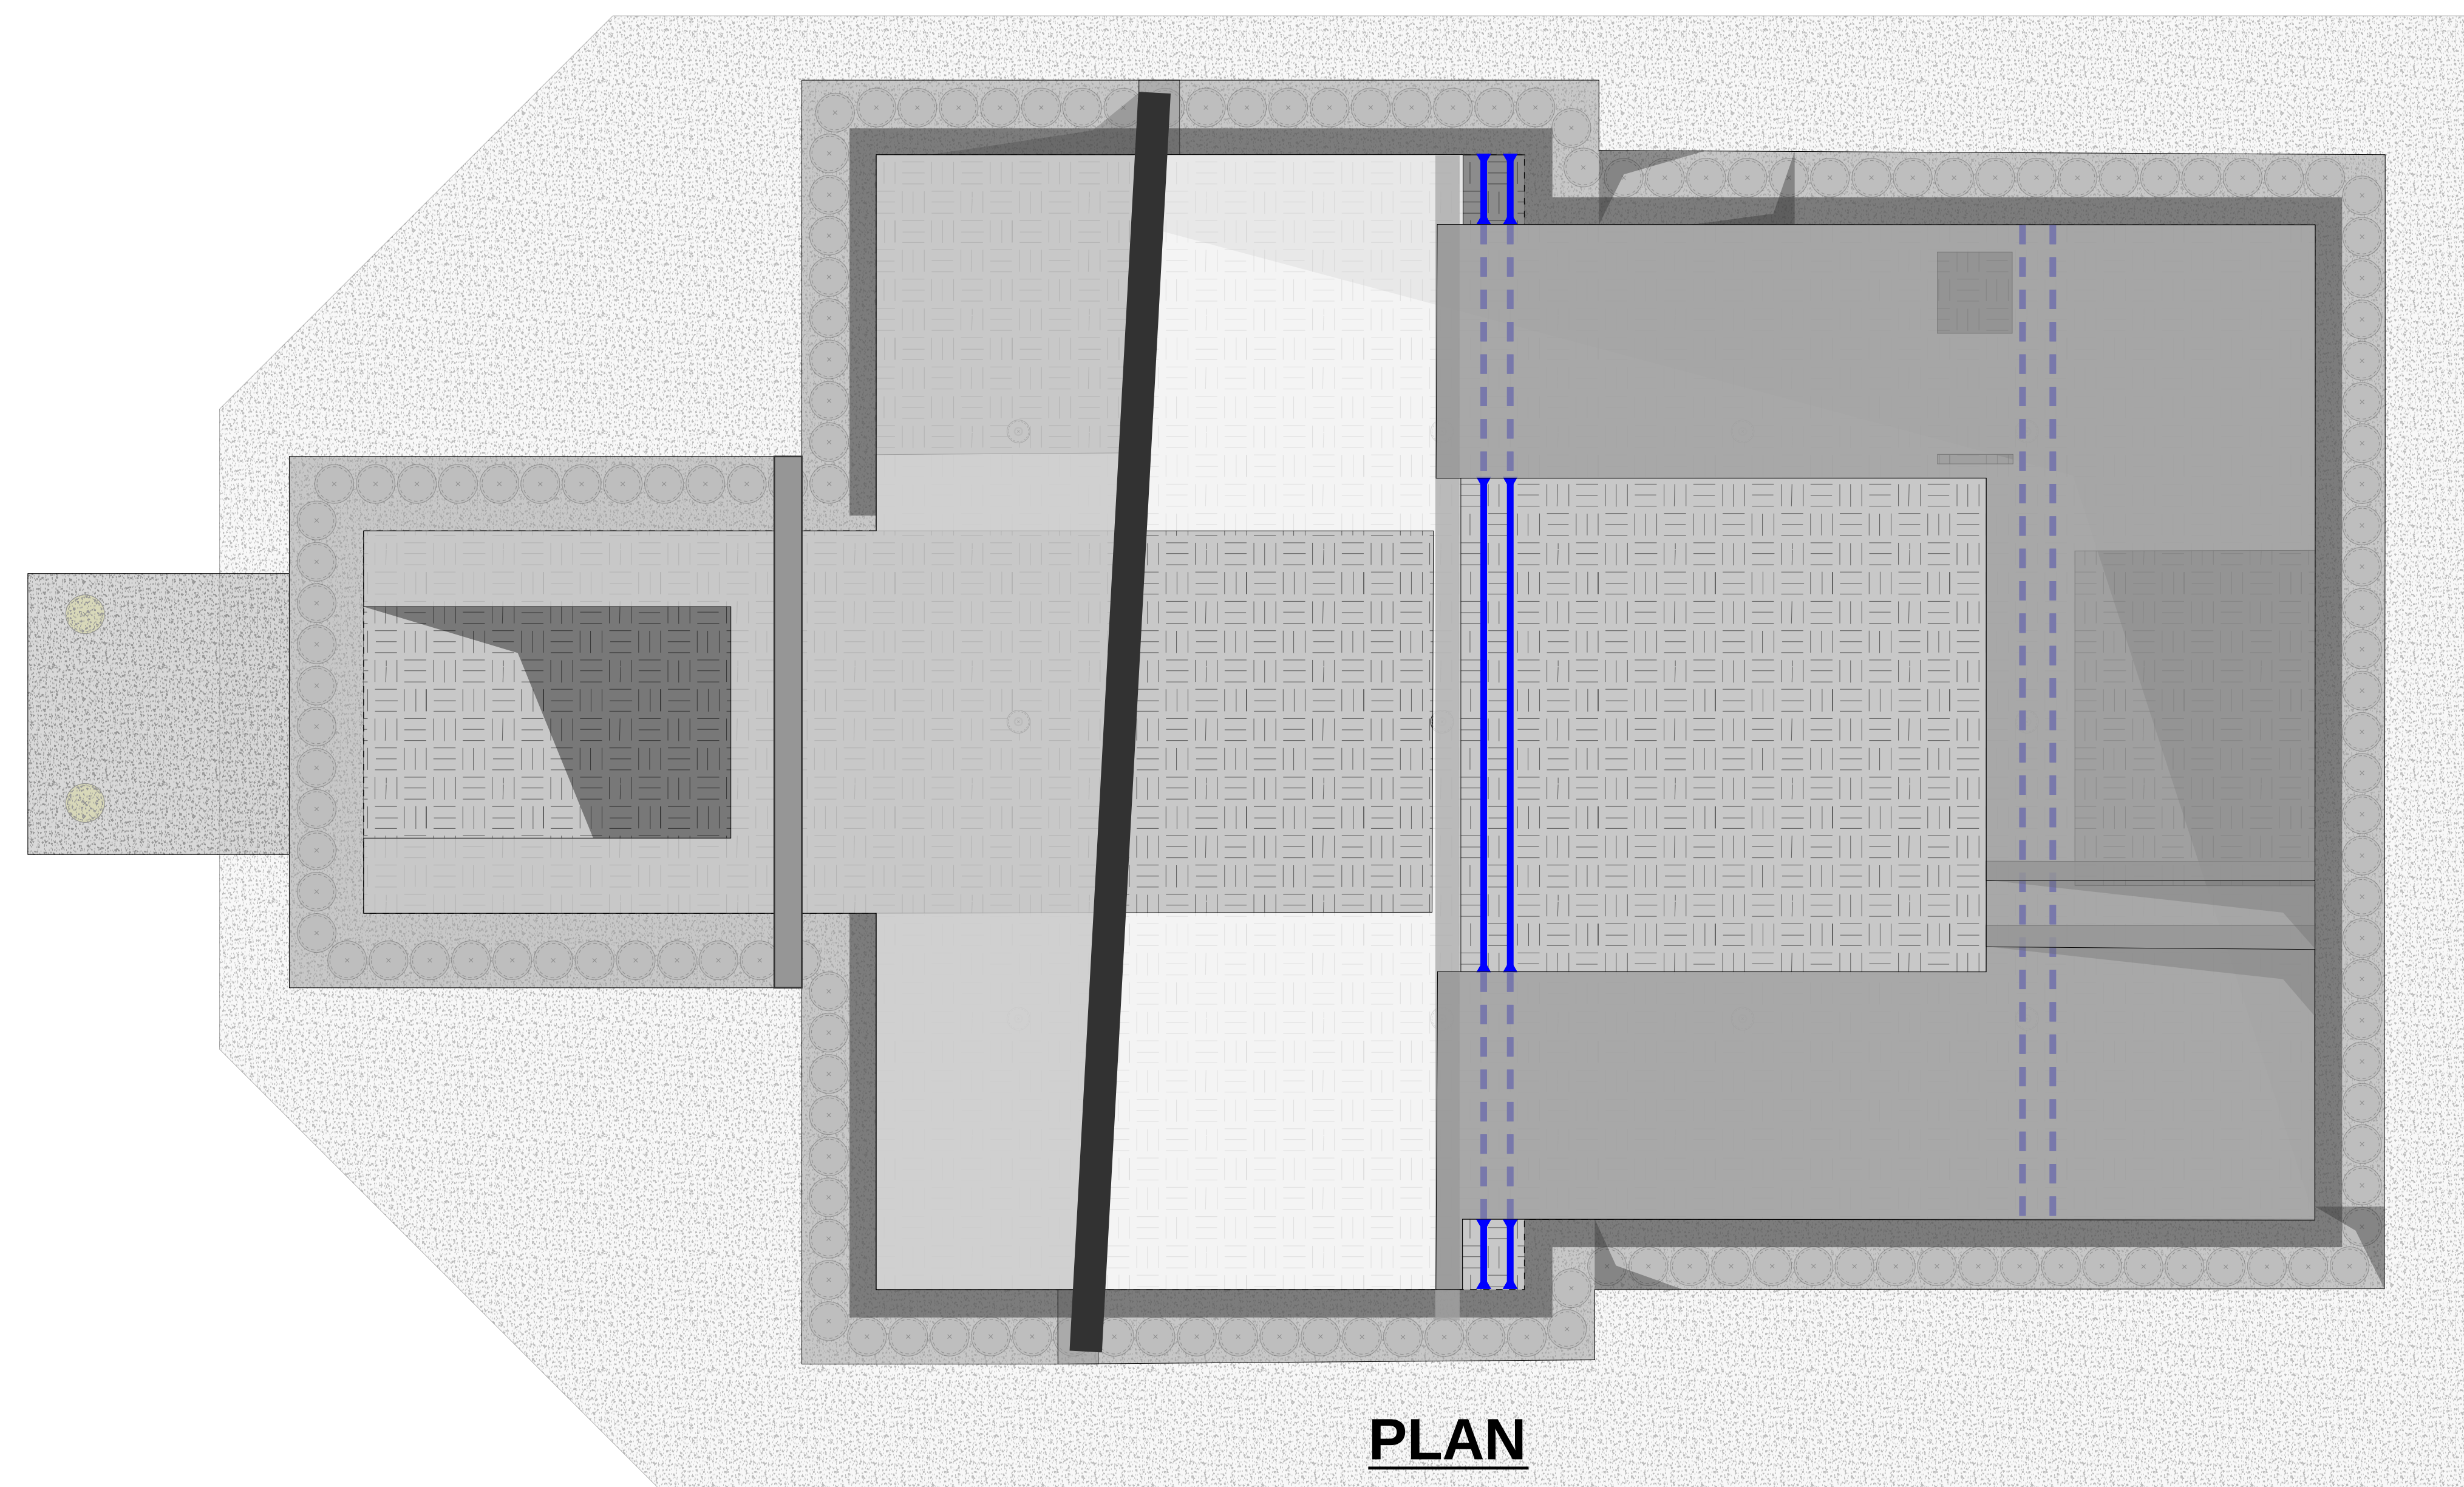

PLAN

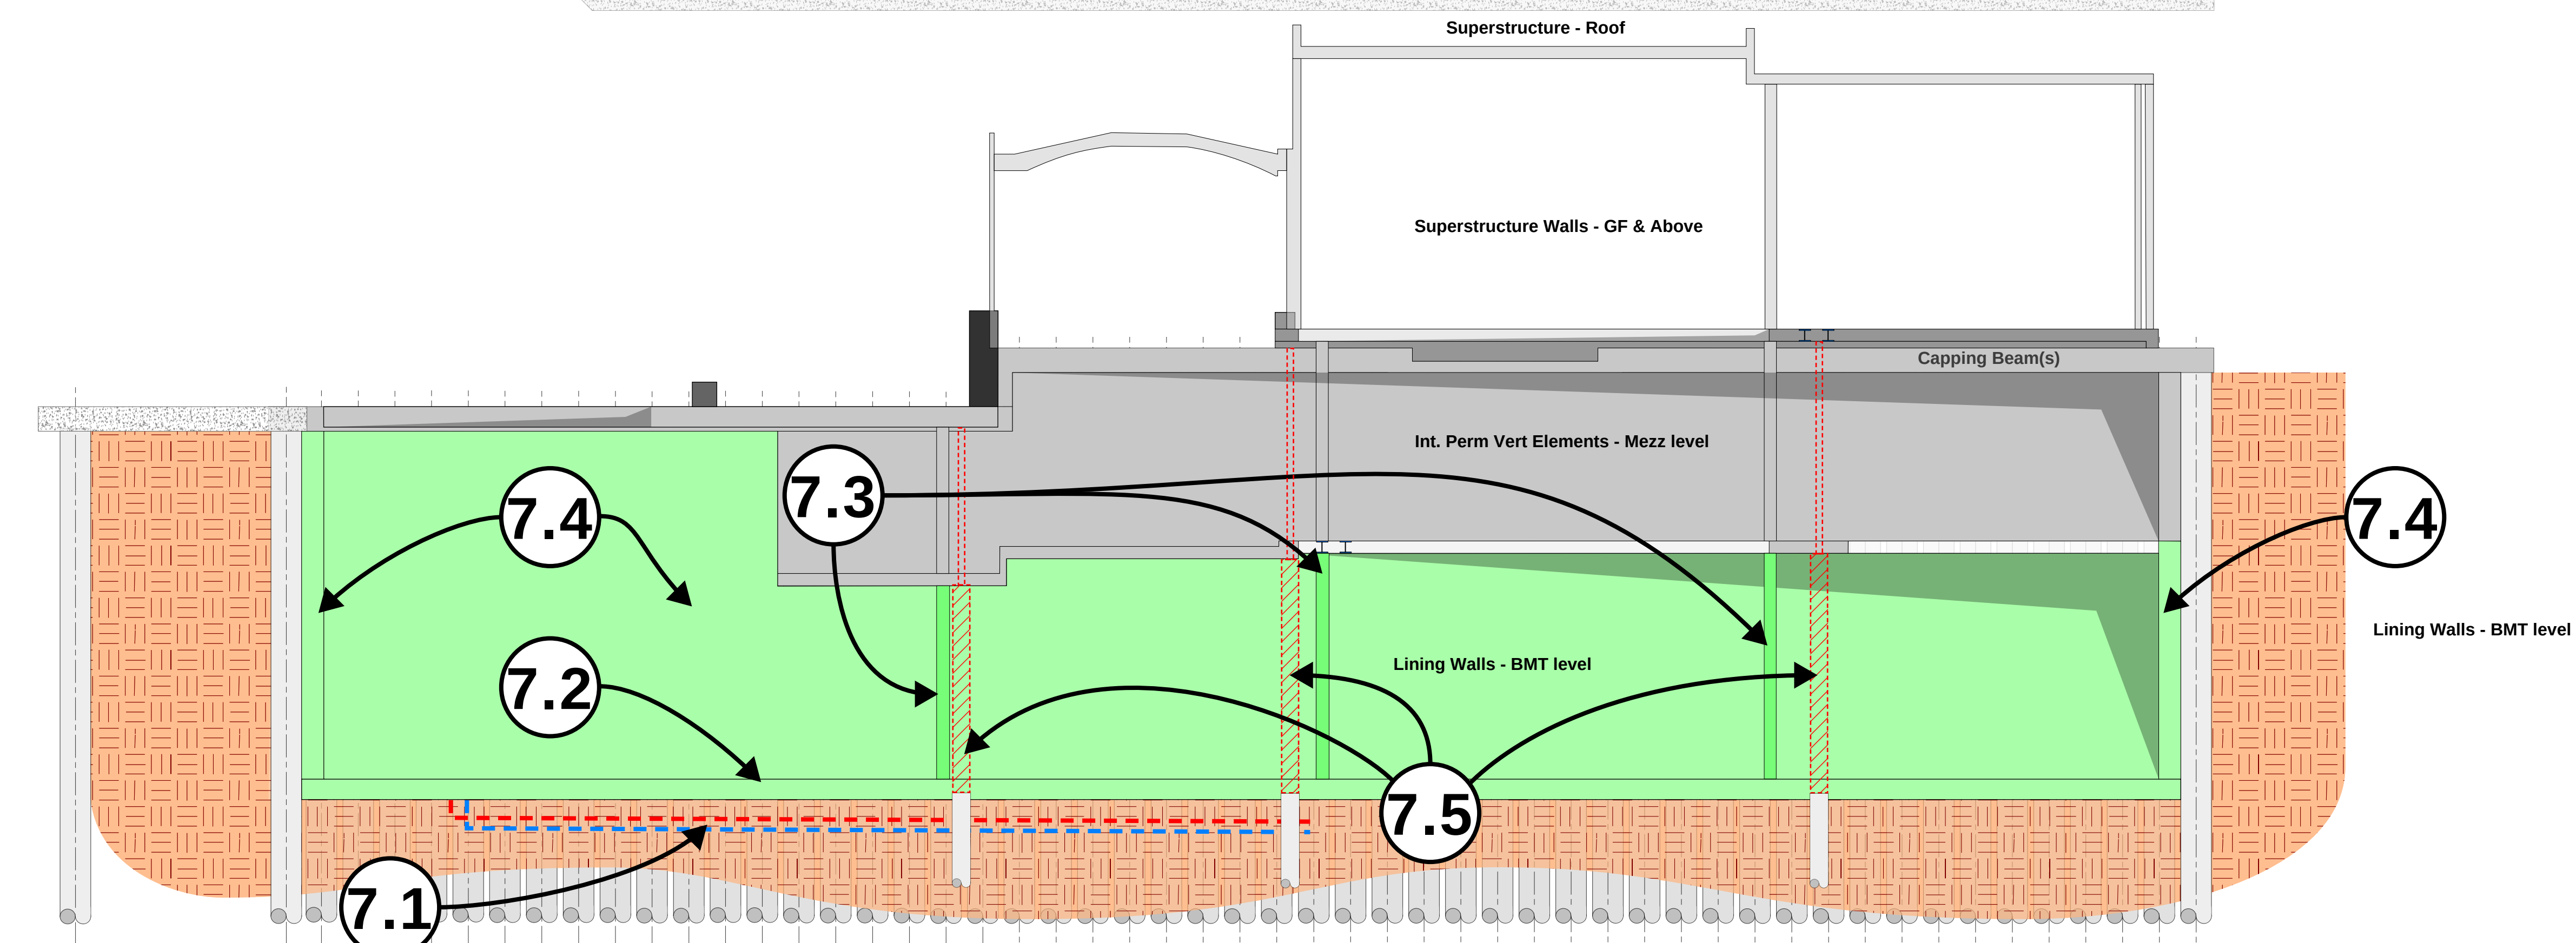

SECTION



NOTES:

PROVISIONAL SEQUENCE OF WORKS

- 7.1) Install below slab drainage
- 7.2) Construct Basement Level slabs
- 7.3) Construct Basement Level Internal vertical elements
- 7.4) Construct Basement Level RC lining walls
- 7.5) Remove Temporary Piles / Plunge Posts and make good slab locally

[illegible]

SIZE GROUP STRUCTURES

DRAWN BY CP	CHECKED BY	DATE 17 / 10 / 25
----------------	------------	----------------------

CONTRACT
TOTTENHAM HOUSE

REFERENCE
POOL HOUSE
PROVISIONAL CONSTRUCTION SEQUENCE
(STAGE 7 of 7)

SCALE (@ A1) SEE SCALE BAR	PROJECT NUMBER ST23-04
DRAWING NUMBER ST24-SOW-007	REV 0
