

Arbortrack Systems Ltd
The Granary Studio
Crewe Lane
Kenilworth
Warwickshire
CV8 2LA

Telephone: 07986 122074
E-mail: james@arbortrackservices.com

Arboricultural Impact Assessment

& Method Statement:

Blackland Lakes
Stockley Lane
Calne
SN11 0NQ

REPORT PREPARED FOR:

Mr Rupert Crockett
Blackland Lakes Limited
Stockley Lane
Calne
SN11 0NQ

REPORT PREPARED BY

James Bell
MSc. (Env). Arbor. A. Tech. Cert.

Ref: jwmb/rpt1/blacklandlakes/AIAAMS

Date: 7th January 2026

The content and format of this report are for the exclusive use of the client. It may not be sold, lent, hired out or divulged to any third party not directly involved in the subject matter without the written consent of Arbortrack Systems Ltd.

CONTENTS

1.0	Introduction	3
1.1	Purpose & Use of the Report	3
1.2	Terms of Reference	3
1.3	Tree Survey	3
1.4	Development Proposals & Impact Assessment	4
1.5	Sequence of Works	4
1.6	Site Supervision	5
1.7	Site Monitoring & Contact Information	5
1.8	Statement Adoption	5
2.0	Pre-Development Site Preparation	6
2.1	Arboricultural Works	6
2.2	Preparation of Surfaces	6
2.3	Installation of Tree Protection Barrier	6
2.4	Pre-Development Site Inspection	6
3.0	Development Phase	7
3.1	General Precautions	7
3.2	Root Protection Areas	7
3.3	Site Access Accommodation & Storage	7
3.4	Routing & Installation of Services	7
3.5	Demolition Measures	8
3.6	Changes in Grade	8
3.7	Construction Measures	8
3.8	Removal of Tree Protection Barrier	8
3.9	Post-Construction Landscaping	9
4.0	Summary of Proposed Methods	9
4.1	Table of Impacts & Mitigation	9
5.0	Completion	9
5.1	Completion Meeting	9
Appendix A	Tree Protection Plan	
Appendix B	Tree Survey Schedule & Recommended Tree Works	
Appendix C	Fencing Specification to BS5837:2012	
Appendix D	Glossary & General Guidelines	
Appendix E	Tree Constraints Plan	

1.0 Introduction

1.1 Purpose & Use of the Impact Assessment & Method Statement

- 1.1.1 This arboricultural impact assessment & method statement report has been prepared for submission to Wiltshire Council (WC) to accompany a planning application for a new Padel Tennis facility at Blackland Lakes, Stockley Lane, Calne, SN11 0NQ. This statement is intended to demonstrate the feasibility of construction without harm to the retained tree resource on and adjoining the site. See the material accompanying this report for full scheme details. Please note that this report is for planning purposes only and is not a tree risk assessment.
- 1.1.2 This document lays down the methodology for any proposed works that may have an effect upon the trees on and adjacent to the site. It is essential within the scope of any contracts related to the development proposals that this method statement is observed and adhered to. It is recommended that this document form part of the work schedule and specification issued to the building contractors and can be used to form part of the contract.
- 1.1.3 Copies of this document should be available for inspection on site. The developer will inform the local planning authority within twenty-four hours if the designated arboriculturist is replaced.

1.2 Terms of Reference

- 1.2.1 I am instructed by Mr Rupert Crockett to prepare an arboricultural impact assessment & method statement report to accompany a planning application for a new Padel Tennis facility at Blackland Lakes, Stockley Lane, Calne, SN11 0NQ with reference to British Standards publication: Trees in relation to design, demolition & construction - Recommendations (BS5837:2012).
- 1.2.2 The tree protection plan at Appendix A is based on topographical survey drawing reference RT/225/0065/P/0001 from Warner Surveys, 5th floor, 1 Temple Way, Bristol BS2 0BY and Site Plan drawing reference 04 from PMG Architecture & Surveying, Sentinel House, Harvest Cres, Fleet GU51 2UZ.

1.3 Tree Survey

- 1.3.1 A BS5837:2012 survey of the trees near the proposals was conducted on 17th November 2025 by James Bell of Arbortrack Systems Ltd. Full tree survey data is provided at Appendix B.
- 1.3.2 Data from the iGeology app from the British Geological Survey suggests that it is likely that the site has a bedrock geology of Gault Formation - Mudstone and Lower Greensand Group – Sandstone with an unrecorded superficial geology. The prevailing soil conditions evidently provide a reasonable medium for tree growth. Any potential for soil compaction (highly deleterious to root function) during development will depend on the proportion of clay present in the upper profile. The presence of clay in this location would appear to be unlikely, but cannot be precluded. Further to confirmation of the precise soil type present, a structural engineer may be able to advise further on the local geology and its implications, if any, for development.
- 1.3.3 No Ancient Semi-Natural Woodland (ASNW) is present near the site: see the Department for Environment Fisheries & Rural Affairs (DEFRA) MAGIC website for details at <http://magic.defra.gov.uk/MagicMap.aspx>.
- 1.3.4 The status of surveyed trees has not been established with WC; however, their online mapping suggests that none of the trees on site are subject to a Tree Preservation Order (TPO) and that the site does not stand within a Conservation Area (CA).

1.4 Development Proposals & Impact Assessment

- 1.4.1 The proposals are for a new Padel Tennis facility on the site of an existing campsite. See proposals at Appendix A and accompanying material for full details.
- 1.4.2 The following low-quality trees will be removed to allow or facilitate development: 1, G11 (partial), 17, 19, 20, 21, 23, 25, 27, 29, 37, 38, 47, 48, G49 (partial), G52 (partial) & 54. The loss of these trees is a low and acceptable impact and is likely to have a minimal amenity impact on the surrounding area. It is also recommended that trees 4 & 5 are felled for arboricultural best practice – see Appendix B for details.
- 1.4.3 The following trees will be cut back for clearance off the Padel Tennis facility: 18, 26, 28, 33, 34, 35, 36, 45, 46, 51 & 55. These works are largely to low-quality hawthorn/landscape planting and will not compromise the screening function delivered by these trees.
- 1.4.4 Necessary tree removals do not compromise screening on the northern and southern flanks and have been kept to a minimum.
- 1.4.5 Existing hardstanding within the root protection areas (RPA) of trees 2, 15, 16, 18, 51, 53, 55, 59, 60 & 61 will act as ‘de facto’ ground protection. Existing surfacing can be extended within the RPA of tree 59 (to replace soft ground) to accommodate parking bays-provided a 1m separation between this tree and new hard standing is delivered. Details can be agreed via the discharge of a condition of the approved proposals, if necessary.
- 1.4.6 The great majority of site works will take place beyond the RPAs of retained trees and canopies. Retained trees will be protected throughout the course of development by fencing to the specification recommended by BS5837:2012 - see Appendix C for details.

1.5 Sequence of Works

- 1.5.1 The sequence of works should be as follows:

- tree works required to allow or facilitate development – see Appendix B
- erection of tree protection barrier (TPB) on advised line(s) – see Appendix A
- relocation of existing structures
- laying/extending of service runs
- main construction phase
- removal of TPB
- soft landscaping

1.6 Site Supervision

1.6.1 An individual, e.g. the Site Agent, must be nominated to be responsible for all arboricultural matters on site. This person must:

- be present on-site for the majority of the time
- be aware of the arboricultural responsibilities
- have the authority to stop any work that is causing, or has the potential to cause, harm to any retained tree
- be responsible for ensuring that all site operatives are aware of their responsibilities toward trees on site and the consequences of the failure to observe these responsibilities
- make immediate contact with the local authority and/or the designated arboriculturist in the event of any tree-related problems occurring, whether actual or potential

1.7 Site Monitoring

1.7.1 The site agent will be responsible for monitoring all arboricultural works, inspecting protective fencing and monitoring all on-site works in the context of tree protection. The designated arboriculturist will be available for site visits on a basis to be agreed upon between the client and planning authority when/if appropriate or required, i.e. if required by condition. It is recommended that a record of site visits is maintained for inspection on-site and copies forwarded to the developer/agent and to the local planning authority. A certificate of practical completion can be produced for sites deemed by all parties to merit this.

1.7.2 It is the responsibility of the client to advise Arbortrack when the project begins and to forward on the approval notice when published on the planning portal, should supervision requirements be stipulated.

1.7.3 Principal contact information: 1/. Mr James Bell. Arbortrack Systems Ltd. Arboricultural Consultant. 07986 122074. 2/. WC Tree Officer. 0300 456 0114. 3/. Site agent. Details to be advised. 4/. Mr Paul Gallie. PMG Architecture & Surveying. Architect. 01252 975470. paul@pmgarchitecture.co.uk. 5/. Mr Jonathan Walton. Opus Works Consultancy Ltd. Planning Consultant. 07768 968030. jonathan.walton@opus.works.

1.8 Statement Adoption

1.8.1 It is recommended that, in due course, acceptance of the recommendations in this report is demonstrated by, for example, the architect specifying in writing to the building contractor that tree care conditions apply in the execution of the contract and by an estimate or written undertaking from the contractor to the architect demonstrating that the practical aspects of observation of such recommendations have been priced in.

1.8.2 If conflicts between any part of a tree and the proposals arise during the course of development, these can often be resolved quickly and at little cost if a qualified arboriculturist is consulted promptly. Lack of such care is often apparent quickly, and the decline and death of such trees can spoil design aims and can, of course, affect saleability, as well as reflecting poorly on the construction and design personnel involved. Trees that have been the recipients of careful handling during construction add considerably to the appeal and value of the finished development.

2.0 Pre-Development Site Preparation

2.1 Arboricultural Works

- 2.1.1 See Appendix B for full details of tree works required to allow or facilitate development or for arboricultural best practice.

2.2 Preparation of Surfaces – n/a

2.3 Installation of Tree Protective Barrier

- 2.3.1 The tree protection barrier (TPB) must be comprised of a vertical and horizontal scaffold framework, braced to resist impacts, with vertical tubes spaced at a maximum level of 3m. On to this, weldmesh panels should be securely fixed with wire scaffold clamps: see section 6.2.2 and Figure 2 of BS5837:2012 (Appendix C). The suggested location(s) of the TPB is shown in Appendix A.
- 2.3.2 This TPB is to be erected before any construction work commences on site, is to remain 'in situ' and undamaged for the duration of all work or each phase and is only to be removed once all work is completed. If any work other than preparatory tree work is deemed necessary prior to the erection of fencing, the designated arboriculturist should be informed to enable his/her presence to oversee the work being carried out.
- 2.3.3 The only other exception is the completion of soft landscaping, but if any excavations, however minor, are to be carried out as part of soft landscaping within RPAs, an arboricultural assessment must be carried out beforehand, and any arboricultural protection measures incorporated. The TPB should carry waterproof warning notices denying access within RPAs.
- 2.3.4 The Tree Protection Plan in Appendix A illustrates where the protective fencing should be located to form the boundary of the Tree Protection Zone (TPZ). The TPZ is an exclusion zone, and suitable steps should be taken to prevent access by pedestrians and vehicles and the storage of any works materials and equipment should be located outside of the TPZ.

2.4 Pre-Development Site Inspection

- 2.4.1 At the instigation of the client/site agent or WC, upon the erection of the fencing, the designated arboriculturist will meet the relevant local authority member on-site to check the standard of the work(s). If there are any amendments required to the protective fencing, these will be agreed upon at this meeting, confirmed in writing, and undertaken thereafter.

3.0 Development Phase

3.1 General Precautions

- 3.1.1 No fires shall be made on any part of the site or within 10m of the furthest extent of the canopy of any tree or group tree to be retained on-site or on land adjoining.
- 3.1.2 No spilling or pouring of fuels, oils, solvents, or tar shall be made on any part of the site.
- 3.1.3 No materials that are likely to have an adverse effect on tree health, such as oil, bitumen or cement, will be stored or discharged within 10 metres of the trunk of a tree that is to be retained.
- 3.1.4 No spillage or discharge of wet mortar or concrete shall be made on any part of the site.
- 3.1.5 No storage of materials shall be made within the protective fences.
- 3.1.6 No breaching or moving of the protective fences shall occur without the approval of the designated arboriculturist.
- 3.1.7 Alterations in levels within the tree protection fence areas shall be avoided.

3.2 Root Protection Areas

- 3.2.1 The RPA is a desirable zone of protection around the trees' rooting system, and these have been marked on the plan in Appendix A. The RPAs will lie within the TPZ and, therefore, be fully fenced off (see Appendix A) unless appropriate ground protection is offered or if the impact on the RPA is deemed very low and acceptable.

3.3 Site Access, Accommodation & Storage

- 3.3.1 Many site activities are potentially damaging to trees, e.g. material storage, parking, soil compaction and the use of plant machinery. In this latter example, particular care is required to ensure that the operational arcs of excavation and lifting machinery, including their loads, do not physically damage trees when in use or while accessing the site.

3.4 Routing & Installation of Services

- 3.4.1 Any new service runs should avoid RPAs of retained trees where possible. If unavoidable, any trenches within the RPAs of site trees should be hand-dug and kept as narrow as possible. They should not extend to within 1m from the base of any retained tree trunk. Exposed roots larger than 25mm in diameter should be retained with their bark intact and, when exposed, wrapped in dry hessian sacking.
- 3.4.2 Where crown interference with mature trees is a possibility, over-ground services will be routed in an alternative direction. In relation to this, any landscaping taking place should accommodate the presence of over-ground services and take mature tree size into account.

3.5 Demolition Measures

- 3.5.1 If required, access facilitation pruning should be undertaken to prevent injurious contact between the demolition plant and the tree(s). Any such pruning should be undertaken in accordance with the British Standards publication: Tree work – Recommendations (BS3998:2010).
- 3.5.2 Demolition/removal of structures (including underground structures) within what would otherwise be an RPA should proceed with due caution to avoid unnecessary damage to trees.
- 3.5.3 All plant and vehicles engaged in demolition works (removals only), if not operating on existing hard standing, should either operate outside the RPA or should run on a temporary surface designed to protect the underlying soil structure. See section 6.2.3.3 for further detail.
- 3.5.4 Where trees stand adjacent to structures scheduled for demolition, it will be necessary to undertake demolition inwards within the footprint of the existing building (often referred to as “top down, pull back”).
- 3.5.5 If the weather is “dry,” the site should be watered down to reduce dust travelling to adjacent properties. Where levels of dust build-up on trees occur, it may be necessary to seek the advice of the designated arboriculturalist on remedial measures, e.g. hose down the tree(s) immediately following any significant accumulation of dust.
- 3.5.6 Heavy plant used to remove materials should work systematically *away from retained trees*. The aim is to ensure that spoil is removed away from RPAs, but it is very important that the original soil levels are not altered.

3.6 Changes in Grade

- 3.6.1 The upper layer of topsoil (top 60cm) contains the majority of a tree’s roots, and if this is disturbed by a change in ground level, serious damage can be caused. On this basis, as a minimum, level changes to soil should be avoided within RPAs.
- 3.6.2 If any significant section of ground level requires raising within RPAs, this should be achieved using coarse, granular material such as pebbles. See section 7.4.4.4 of BS5837:2012.
- 3.6.3 If ground levels need to be altered within 1.5 metres of any tree trunk, prior agreement must be sought from and given by the local authority tree officer.

3.7 Construction Measures

- 3.7.1 No specialist construction methods are required for the proposals in terms of trees.

3.8 Removal of Tree Protective Barrier

- 3.8.1 The protective fencing may be removed only upon completion of the development phase when all drainage and service runs have been installed and any site machinery has been removed.

3.9 Post-Construction Landscaping

- 3.9.1 Following the development phase, retained trees may be subject to either landscaping or seeding beneath their canopies.
- 3.9.2 Any approved landscaping works should avoid the changing of ground levels or deep digging in the vicinity of trees except where already approved. Mechanised cultivation, such as tractor-mounted rotovation, must not be used within the RPA of retained trees.
- 3.9.3 Heavy machinery should not be used in the vicinity of any retained trees unless adequate ground protection is in place.
- 3.9.4 If herbicides are to be used, they should be appropriate to their purpose and not used in such a way as to damage any retained trees or vegetation.
- 3.9.5 Ideally, retained trees should be within a shrub area as this reduces the chances of compaction and disturbance of root systems.

4.0 Summary of Proposed Methods

4.1 Table of Impacts and Mitigation

- 4.1.1 The table below summarises the main areas where trees could become damaged by the proposed development and the methods that need to be adopted in order to prevent such damage:

<u>Impact</u>	<u>Mitigation</u>	<u>Reference</u>	<u>Trees Affected</u>
Passage of machinery and storage of materials over RPAs	Construction of protective fencing to acceptable standards	Sections 2.3. Fencing spec Appendix C, Tree Protection Plan Appendix A	2, 3-10, 38a-46, G49 (partial), G50, 51, G52 (partial), 53 & 55-59

5.0 Completion

5.1 Completion Meeting

- 5.1.1 Following completion of the approved works on site, the designated arboriculturist can meet with a local authority representative and agree upon any remedial works deemed necessary (if any).
- 5.1.2 Any works agreed upon in the above meeting will be confirmed in writing and should be performed to BS3998:2010.
- 5.1.3 Any work proposed post-development should be checked to avoid a penalty for performing illegal work on a protected tree.

APPENDIX A

APPENDIX B

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter	Protection Radius	Age Class	Growth Vitality	Structural Condition	B.S. Cat	Sub Cat	Useful Life	Comments
			N	S	E	W										
1	Willow, Weeping	8	4	3	3	4	2.5	340	4.1	Early Mature	Normal	Good	C	2	20+	Garden ornamental Ivy clad Hazel, dogwood, fog rise, thorn in hedge @ base
2	Willow, Weeping	10	7	6	5	5	3	466	5.6	Early Mature	Normal	Good	B	2	20+	Ivy clad Garden ornamental
3	Hazel, Common	4	4	2	2	4	1	225 #	2.7	Early Mature	Normal	Fair	C	2	20+	Multi stem stool
3a	Hazel, Common	4	5	1	1.5	1.5	1	159 #	1.9	Early Mature	Normal	Fair	C	2	20+	Multi stem stool
4	Hawthorn, Common	4	2	2	1.5	1.5	2	252 #	3.0	Early Mature	Dead	Poor	U			Multi stem stool Ivy smothered
5	Hawthorn, Common	4	1	1	4	1	2	184 #	2.2	Early Mature	Moderate	Fair	C	2	10+	Multi stem stool Ivy smothered Poor form; hazel & thorn (unsurveyed) near base-all on eastern side of ditch
6	Aspen	19	8	8	8	7	4.5	1240	14.9	Mature	Normal	Good	B	2	20+	Broken branches Ivy clad Minor deadwood ; tagged 279; trifurcation @ 1.89m; cut back to S & SE

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter	Protection Radius	Age Class	Growth Vitality	Structural Condition	B.S. Cat	Sub Cat	Useful Life	Comments
			N	S	E	W										
7	Hawthorn, Common	4	4	2.5	3	2	2.5	269	3.2	Mature	Moderate	Fair	C	2	10+	Ivy smothered
8	Hazel, Common	4.5	3	1.5	1	4	2.5	349 #	4.2	Early Mature	Moderate	Fair	C	2	10+	Ivy clad Multiple stem stool Stands on eastern face of ditch
9	Hazel, Common	4.5	4	2	2	3	2.5	260 #	3.1	Early Mature	Moderate	Fair	C	2	10+	Ivy clad Multiple stem stool
10	Dogwood	3	1.5	1.5	1.5	1.5	0.5	185 #	2.2	Early Mature	Normal	Good	C	2	20+	One element of boundary screen on western & southern edge of ditch
H11	Mixed Broadleaves	2-3	.75	.75	.75	.75	0	159 #	1.9	Early Mature	Moderate	Fair	C	2		Mixed species screen along northern boundary of site-beside ditch
G12	Hawthorn, Common	2.75 -4.5	1.5	1.5	1.5	2	0.5	211 #	2.5	Early Mature	Moderate	Fair	C	2	10+	Ivy smothered Remote survey [RS] Bases obscured in boundary screen; 2 free standing young elm on edge of hard standing
G13	Hawthorn, Common	4.5	1.5	1.5	1.5	2	0.5	211 #	2.5	Early Mature	Moderate	Fair	C	2	10+	Ivy smothered Remote survey [RS] Base obscured in boundary screen

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter	Protection Radius	Age Class	Growth Vitality	Structural Condition	B.S. Cat	Sub Cat	Useful Life	Comments
			N	S	E	W										
14a	Hawthorn, Common	3.5	1	1.5	1.5	1.5	2	147 #	1.8	Semi-mature	Moderate	Fair	C	2	10+	Ivy smothered RS
14	Hawthorn, Common	5.5	2	2	3.5	4.5	2.5	260 #	3.1	Early Mature	Moderate	Fair	C	2	10+	Ivy smothered RS
15	Cedar, Blue Atlantic	11	1	4.5	3	3	3	370	4.4	Early Mature	Normal	Good	B	2	20+	Asymmetry (major) Ivy clad
16	Lime spp	10.5	4	3	4	6.5	3	528	6.3	Early Mature	Normal	Good	B	2	20+	Bifurcates @ 1m
17	Cherry, Wild (Gean)	9.5	2	6	5	5	3	350	4.2	Early Mature	Normal	Fair	C	2	10+	Unbalanced to SSE
18	Lime, Common	15	7	6	7	8	2.5	686 #	8.2	Mature	Normal	Good	B	2	20+	Suckering from base Ivy clad
18a	Maple, Field	4	2	6	1.5	3	3	255 #	3.1	Early Mature	Normal	Poor	C	2	10+	Very poor form Ivy clad Interfering with T19; arguably 'U' category

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter	Protection Radius	Age Class	Growth Vitality	Structural Condition	B.S. Cat	Sub Cat	Useful Life	Comments
			N	S	E	W										
19	Cherry, Wild (Gean)	12	2	5	2.5	6	4	370	4.4	Early Mature	Normal	Fair	C	2	20+	Ivy clad
20	Elm spp	6	1.5	1.5	0	3	2.5	130	1.6	Semi-mature	Normal	Fair	C	2	10+	Asymmetry (major) Vulnerable to DED
21	Hawthorn, Common	4	1.5	1	1.5	1.5	1	204 #	2.4	Semi-mature	Normal	Fair	C	2	10+	Ivy smothered
22	Hawthorn, Common	5	2	1.5	.5	2.75	2	238 #	2.9	Early Mature	Normal	Fair	C	2	10+	Ivy smothered
23	Hawthorn, Common	5	3	1.75	1.5	1.5	2	245 #	2.9	Early Mature	Normal	Fair	C	2	10+	Ivy smothered
24	Hazel, Common	4	2	1	1.5	1.5	0.5	156 #	1.9	Semi-mature	Normal	Good	C	2	20+	Multi stem stool
25	Hawthorn, Common	5.5	3	2	2.75	3	2.5	433 #	5.2	Early Mature	Normal	Good	C	2	20+	Ivy smothered Growing with young elm

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter		Protection Radius	Age Class	Growth Vitality	Structural Condition	B.S. Cat	Sub Cat	Useful Life	Comments
			N	S	E	W											
26	Hawthorn, Common	4	2.75	1.75	2.75	1.5	0	173	#	2.1	Early Mature	Normal	Good	C	2	20+	Ivy smothered Growing with young elm Brambles around base; RS
27	Hawthorn, Common	4	2	1.5	2	2	1.5	200	#	2.4	Early Mature	Moderate	Fair	C	2	10+	Ivy smothered Minor deadwood
28	Hawthorn, Common	3	.5	.5	1	1	2	150	#	1.8	Semi-mature	Poor	Fair	C	2	10+	Ivy clad
29	Ash, Common	12	4	4	7	5	3	574	#	6.9	Early Mature	Moderate	Fair	C	2	10+	Ivy clad RS Vulnerable to chalara
33	Hazel, Common	4	1.5	2	3	3	1	350	#	4.2	Early Mature	Normal	Good	C	2	20+	RS Multiple stem stool
34	Hazel, Common	3.5	1.5	1.75	3	1.5	1	250	#	3.0	Early Mature	Normal	Fair	C	2	10+	RS Dying back (lead stem /centre) Multiple stem stool
35	Hawthorn, Common	3	.2	2	1	1	0.5	184	#	2.2	Early Mature	Normal	Fair	C	2	10+	Ivy clad Asymmetry (major)

Site: Blackland Lakes Calne
Date: 17th November 2025

Appendix B
BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd
07986 122074
Surveyor(s): James Bell
Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter	Protection Radius	Age Class	Growth Vitality	Structural Condition	B.S. Cat	Sub Cat	Useful Life	Comments
			N	S	E	W										
36	Dogwood	3.5	1.5	1.5	2	1.5	0.5	122 #	1.5	Semi-mature	Normal	Good	C	2	10+	
37	Elder	2.5	1.5	1.5	1	1	0	208 #	2.5	Semi-mature	Moderate	Fair	C	2	10+	Smothered in dog rose
38	Hawthorn, Common	6	2.5	3	3	3	3	270	3.2	Early Mature	Normal	Good	C	2	20+	Ivy clad Blackthorn @ base
38a	Blackthorn	2.5	1	1	1	1	1.5	106 #	1.3	Semi-mature	Normal	Fair	C	2	10+	Ivy smothered Growing with an elder
G38b	Mixed Broadleaves	3	1.5	1.5	1.5	1.5	0	93 #	1.1	Early Mature	Normal	Good	C	2	10+	Willow, blackthorn & hawthorn with bramble
G39	Hawthorn, Common	2.5	.75	.75	.75	.75	0.5	180 #	2.2	Early Mature	Normal	Fair	C	2	10+	Ivy smothered Elements within G38b
41	Cherry, Wild (Gean)	7.5	3.5	0	0	4	2.5	280	3.4	Early Mature	Moderate	Fair	C	2	10+	Ivy clad Very poor form

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter	Protection Radius	Age Class	Growth Vitality	Structural Condition	B.S. Cat	Sub Cat	Useful Life	Comments
			N	S	E	W										
42	Lime, Common	12	6	3	2.75	5	1	700	8.4	Mature	Normal	Good	B	2	20+	Ivy clad Trunk separation to 4 @ 1.5m
43	Maple, Field	2.75	1.5	1	2	2	0.5	270	3.2	Early Mature	Normal	Fair	C	2	10+	Ivy clad Crown removed off power lines
44	Maple, Field	2.75	1.5	2.5	1	1	0.5	306 #	3.7	Early Mature	Normal	Fair	C	2	10+	Ivy clad Crown removed off power lines
45	Maple, Field	13	3	3	6	4	2.5	482	5.8	Early Mature	Normal	Good	C	2	20+	Asymmetry (major)
46	Sycamore	11	4	7	5	7	2.5	560	6.7	Early Mature	Normal	Fair	C	2	20+	Co-dominant stems Included bark in main stem unions
47	Maple, Field	10	2	6	4.5	2	1.5	250	3.0	Early Mature	Normal	Good	C	2	20+	Asymmetry (major)
48	Maple, Field	10	3	3	4	2	1.5	399	4.8	Early Mature	Normal	Good	C	2	20+	

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter		Protection Radius	Age Class	Growth Vitality	Structural Condition	B.S. Cat	Sub Cat	Useful Life	Comments
			N	S	E	W											
G49	Mixed Broadleaves	4	2	2	2	2	0.5	180	#	2.2	Early Mature	Normal	Fair	C	2	20+	Dogwood, laurel & plum
G50	Mixed Broadleaves	4	2	2	2	2	0.5	180	#	2.2	Early Mature	Normal	Fair	C	2	20+	Contiguous with G49 Dogwood, laurel & plum
51	Willow, Goat	5	4	2.5	3.5	3.5	2.5	300		3.6	Early Mature	Normal	Fair	C	2	20+	Ivy smothered base
G52	Mixed Species	4.5	2	2	2	2	0	150	#	1.8	Semi-mature	Normal	Good	C	2	20+	Yew, elder, hazel, Portuguese laurel & Thuja with ash & cherry saplings
53	Hazel, Common	5.5	2	2	2.5	2	1	441	#	5.3	Early Mature	Normal	Good	C	2	20+	Ivy clad
54	Cypress, Lawson variety	4.5	1.5	1.5	1.5	1.5	0.5	180	#	2.2	Semi-mature	Normal	Good	C	2	20+	Ivy smothered
55	Oak, English	5.5	4	3	2	4	2.5	370		4.4	Early Mature	Normal	Fair	C	2	20+	Ivy clad Bifurcation @ 1.5m One element within group/screen

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

BS5837:2012 Tree Survey Schedule

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Crown Spread				Ground Clearance	Stem Diameter	Protection Radius	Age Class	Growth Vitality	Structural Condition	B.S. Cat	Sub Cat	Useful Life	Comments
			N	S	E	W										
56	Cypress, Lawson	7.5	1.25	1.25	1.25	1.25	2.5	300	3.6	Early Mature	Normal	Fair	C	2	20+	Ivy clad Bifurcation @ 1.75m
57	Spruce spp	8	2	2	2.5	2.5	0	280	3.4	Early Mature	Normal	Good	C	2	20+	
58	Birch, Downy	13	3	3.5	4	4.5	2	290	3.5	Early Mature	Normal	Good	C	2	20+	Ivy clad Unsure re species.
59	Willow, Weeping	9.5	4	4	7	7	3	460	5.5	Early Mature	Normal	Good	C	2	20+	Garden ornamental Base obscured in laurel
60	Birch, Silver	8	3.5	3	3	3	1.5	310	3.7	Semi-mature	Normal	Good	C	2	20+	Bifurcation @ 1.5m
61	Birch, Silver	7	3.5	1.5	2	2	1.5	200	2.4	Semi-mature	Normal	Good	C	2	20+	Swept stem to NE
G30 -32	Hawthorn, Common	3.5	1.5	1.5	1.5	1.5	0	150 #	1.8	Semi-mature	Moderate	Fair	C	2	10+	Ivy smothered Brambles obscure bases

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

Recommended Tree Works

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/ATAAMS



Tree No.	English Name	Height	Stem Diameter	Crown Spread				BS Cat	Sub Cat	Recommended Works	Comments / Reasons
				N	S	E	W				
1	Willow, Weeping	8	340	4	3	3	4	C	2	Remove	Garden ornamental Ivy clad Hazel, dogwood, fog rise, thorn in hedge @ base To permit development
4	Hawthorn, Common	4	252	2	2	1.5	1.5	U		Fell	Multi stem stool Ivy smothered Recommended husbandry 2
5	Hawthorn, Common	4	184	1	1	4	1	C	2	Fell	Multi stem stool Ivy smothered Poor form; hazel & thorn (unsurveyed) near base-all on eastern side of ditch Recommended husbandry 2
6	Aspen	19	1240	8	8	8	7	B	2	CCL	Broken branches Ivy clad Minor deadwood ; tagged 279; trifurcation @ 1.89m; cut back to S & SE Recommended husbandry 2
H11	Mixed Broadleaves	2-3	159	.75	.75	.75	.75	C	2	Remove (partial)	Mixed species screen along northern boundary of site-beside ditch To permit development

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

Recommended Tree Works

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Stem Diameter	Crown Spread				BS Cat	Sub Cat	Recommended Works	Comments / Reasons
				N	S	E	W				
17	Cherry, Wild (Gean)	9.5	350	2	6	5	5	C	2	Remove	Unbalanced to SSE To permit development
18	Lime, Common	15	686	7	6	7	8	B	2	Cut back for clearance off building if necessary	Suckering from base Ivy clad To facilitate development
19	Cherry, Wild (Gean)	12	370	2	5	2.5	6	C	2	Remove	Ivy clad To facilitate development
20	Elm spp	6	130	1.5	1.5	0	3	C	2	Remove	Asymmetry (major) Vulnerable to DED To facilitate development
21	Hawthorn, Common	4	204	1.5	1	1.5	1.5	C	2	Remove	Ivy smothered To permit development

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B Recommended Tree Works

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/ATAAMS



Tree No.	English Name	Height	Stem Diameter	Crown Spread				BS Cat	Sub Cat	Recommended Works	Comments / Reasons
				N	S	E	W				
23	Hawthorn, Common	5	245	3	1.75	1.5	1.5	C	2	Remove	Ivy smothered To permit development
25	Hawthorn, Common	5.5	433	3	2	2.75	3	C	2	Remove	Ivy smothered Growing with young elm To permit development
26	Hawthorn, Common	4	173	2.75	1.75	2.75	1.5	C	2	Cut back for clearance off building if necessary	Ivy smothered Growing with young elm Brambles around base; RS To facilitate development
27	Hawthorn, Common	4	200	2	1.5	2	2	C	2	Remove	Ivy smothered Minor deadwood To facilitate development
28	Hawthorn, Common	3	150	.5	.5	1	1	C	2	Cut back for clearance off building if necessary	Ivy clad To facilitate development

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

Recommended Tree Works

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/ATAAMS



Tree No.	English Name	Height	Stem Diameter	Crown Spread				BS Cat	Sub Cat	Recommended Works	Comments / Reasons
				N	S	E	W				
29	Ash, Common	12	574	4	4	7	5	C	2	Remove	Ivy clad RS Vulnerable to chalara To permit development
33	Hazel, Common	4	350	1.5	2	3	3	C	2	Cut back for clearance off building if necessary	RS Multiple stem stool To facilitate development
34	Hazel, Common	3.5	250	1.5	1.75	3	1.5	C	2	Cut back for clearance off building if necessary	RS Dying back (lead stem /centre) Multiple stem stool To facilitate development
35	Hawthorn, Common	3	184	.2	2	1	1	C	2	Cut back for clearance off building if necessary	Ivy clad Asymmetry (major) To facilitate development
36	Dogwood	3.5	122	1.5	1.5	2	1.5	C	2	Cut back for clearance off building if necessary	To facilitate development

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B

Recommended Tree Works

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Stem Diameter	Crown Spread				BS Cat	Sub Cat	Recommended Works	Comments / Reasons
				N	S	E	W				
37	Elder	2.5	208	1.5	1.5	1	1	C	2	Remove	Smothered in dog rose To facilitate development
38	Hawthorn, Common	6	270	2.5	3	3	3	C	2	Remove	Ivy clad Blackthorn @ base To permit development
46	Sycamore	11	560	4	7	5	7	C	2	Cut back for clearance off building if necessary	Co-dominant stems Included bark in main stem unions To facilitate development
45	Maple, Field	13	482	3	3	6	4	C	2	Cut back for clearance off building if necessary	Asymmetry (major) To facilitate development
47	Maple, Field	10	250	2	6	4.5	2	C	2	Remove	Asymmetry (major) To permit development

Site: Blackland Lakes Calne

Date: 17th November 2025

Appendix B Recommended Tree Works

Arbortrack Systems Ltd

07986 122074

Surveyor(s): James Bell

Ref: jwmb/rpt1/blacklandlakes/ATAAMS



Tree No.	English Name	Height	Stem Diameter	Crown Spread				BS Cat	Sub Cat	Recommended Works	Comments / Reasons
				N	S	E	W				
48	Maple, Field	10	399	3	3	4	2	C	2	Remove	To permit development
G49	Mixed Broadleaves	4	180	2	2	2	2	C	2	Remove (partial)	Dogwood, laurel & plum To permit development
51	Willow, Goat	5	300	4	2.5	3.5	3.5	C	2	Cut back northern crown for clearance off building if necessary	Ivy smothered base To facilitate development
G52	Mixed Species	4.5	150	2	2	2	2	C	2	Remove (partial)	Yew, elder, hazel, Portuguese laurel & Thuja with ash & cherry saplings To permit development
54	Cypress, Lawson variety	4.5	180	1.5	1.5	1.5	1.5	C	2	Remove	Ivy smothered To permit development

Site: Blackland Lakes Calne
Date: 17th November 2025

Appendix B
Recommended Tree Works

Arbortrack Systems Ltd
07986 122074
Surveyor(s): James Bell
Ref: jwmb/rpt1/blacklandlakes/AIAAMS



Tree No.	English Name	Height	Stem Diameter	Crown Spread				BS Cat	Sub Cat	Recommended Works	Comments / Reasons
				N	S	E	W				
55	Oak, English	5.5	370	4	3	2	4	C	2	Cut back for clearance off building if necessary	Ivy clad Bifurcation @ 1.5m One element within group/screen To facilitate development

Appendix B

Notes on Tree Survey Schedule:

- **Height** describes the approximate height of the tree measured in metres from ground level.
- The **Crown Spread** refers to the crown radius in metres from the stem centre and is expressed as an average of **NSEW** aspect if symmetrical.
- **Ground Clearance** is the height in metres of crown clearance above adjacent ground level.
- **Clear Stem Height** is the distance between trunk base and first branch separation measured in metres.
- **Stem Diameter** is the diameter of the stem measured in millimetres at 1.5m from ground level for single-stemmed trees. See section 4.6 of BS5837:2012 for details of treatment for multistems.
- **Protection Radius** is a radial distance in metres measured from the trunk centre.
- **Growth Vitality** - **Normal** growth, **Moderate** (below normal), **Poor** (sparse/weak), **Dead** (dead or dying tree).
- **Structural Condition** - **Good** (no or only minor defects), **Fair** (remediable defects), **Poor** - Major defects present.
- **B.S. Category** refers to (British Standard 5837:2012 Table 1) and refers to tree/group quality and value; '**A**' - High, '**B**' - Moderate, '**C**' - Low, '**U**' - Unsuitable for Retention.
- **Sub Cat** refers to the retention criteria values where **1** is mainly **arboricultural** qualities, **2** is mainly **landscape** qualities and **3** is mainly **cultural** values including conservation.
- **Useful Life** is the tree's estimated remaining contribution in years.
- **First Significant Branch (FSB)** is the height of the first significant branch above ground level taken at the trunk separation point.

Notes on Recommended Tree Works:

- **Recommended husbandry 1, 2 & 3:**

- 1** Urgent (ASAP)
- 2** Standard (6-12 months)
- 3** Non-Urgent (2-3 years)

- **CB** Cut back to boundary/clear from structure
- **CL#** Crown lift to given height in meters
- **CT#%** Crown Thinning by identified %
- **CCL** Crown clean (remove deadwood/crossing & hazardous branches & stubs)
- **CR#%** Crown Reduce by given maximum percentage (of outermost branch & twig length)
- **DWD** Remove deadwood
- **Fell** Fell to ground level
- **FInv** Further Investigation (generally with decay detection equipment)
- **Pol** Pollard or re-pollard
- **Mon** Monitor ongoing condition (annually by staff/owners & every 2-3 years by consultant). Svr Ivy/Clr Bs Sever Ivy/clear base and re-inspect base/stem for concealed defects

APPENDIX C

Appendix C Tree Protective Fencing Detail (from BS5837:2012)

Figure 2 Default specification for protective barrier


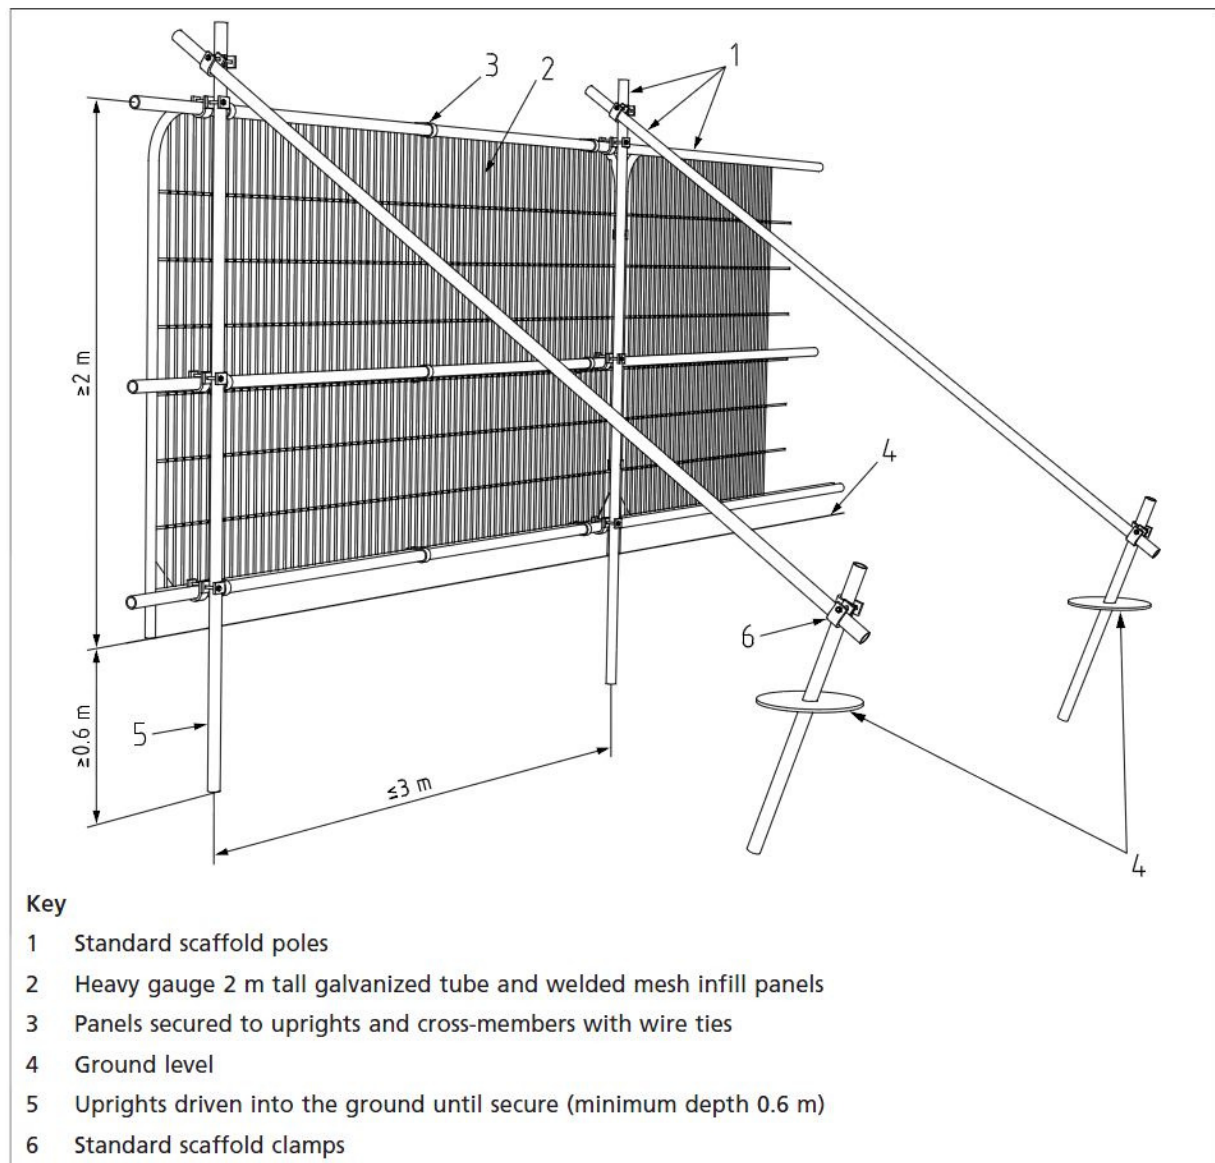


Figure 3 Examples of above-ground stabilizing systems

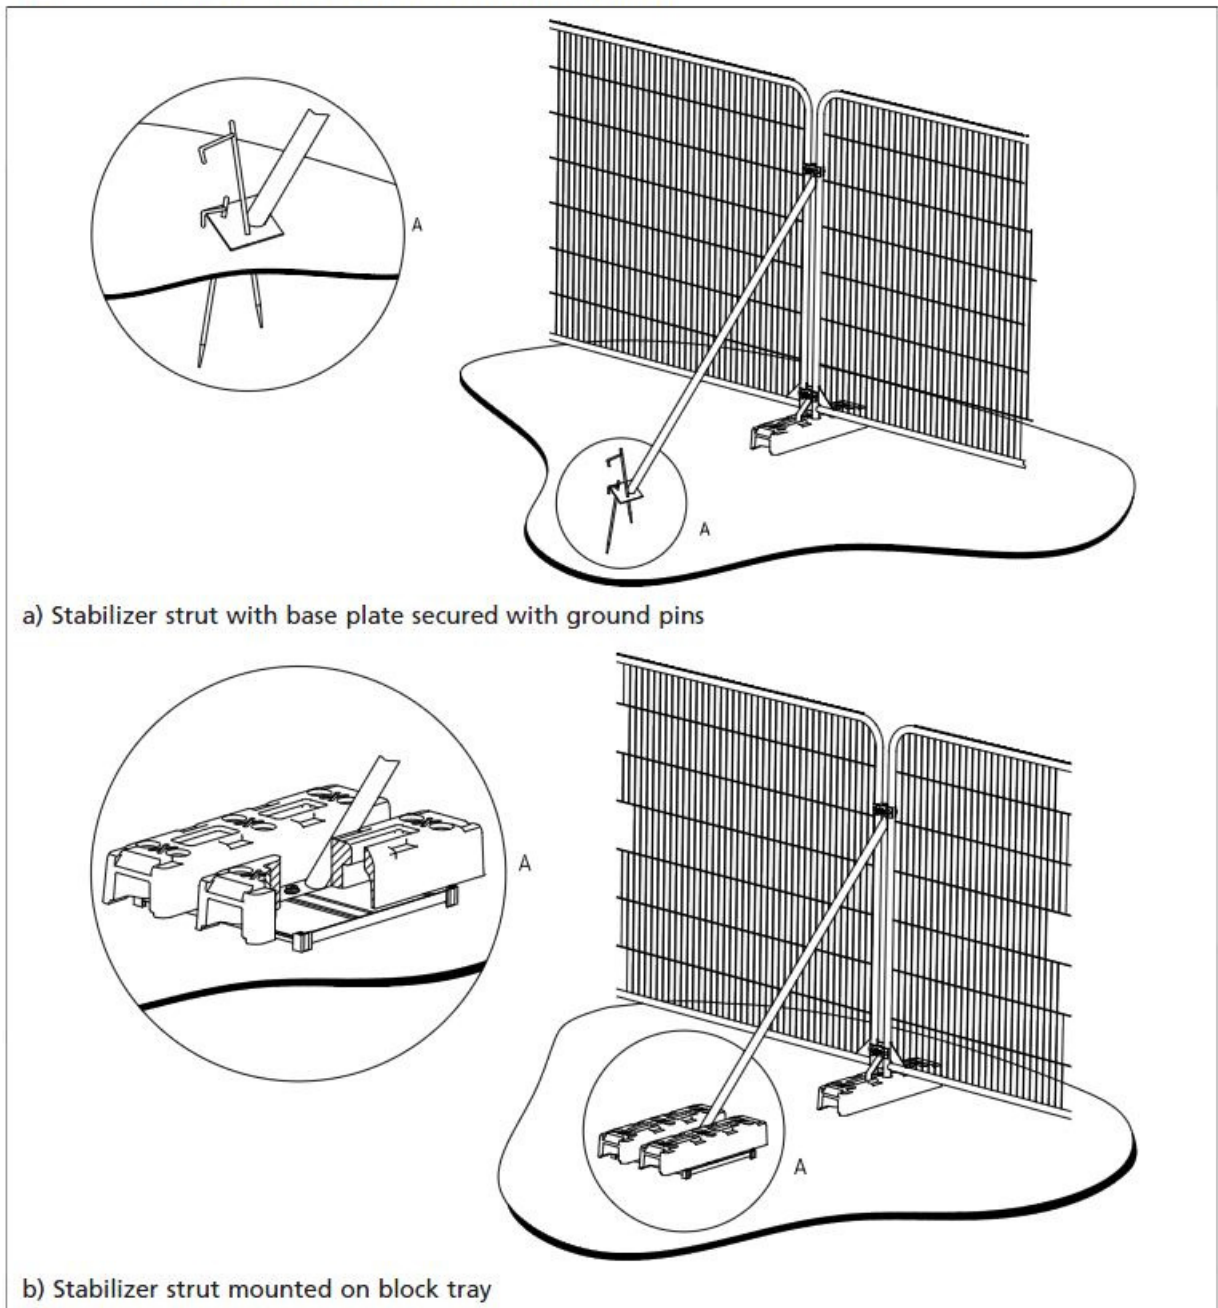

a) Stabilizer strut with base plate secured with ground pins

b) Stabilizer strut mounted on block tray

APPENDIX D

Appendix D


1.0 Glossary of Terms

Canker	Disease damaged area of a tree, usually caused by fungus or bacteria.
Co-dominant Stem	A stem which has grown in direct competition to the main stem and which has formed a substantial size influencing the appearance of the tree.
Crown Lift	The removal of the lowest branches, usually to a given height. It allows more residual light and greater clearance underneath for vehicles etc.
Crown reduce	The reduction of a tree's height or spread while preserving its natural shape.
Crown thin	The removal of some of the density of a tree's crown, usually 5-25% allowing more light through its canopy and reducing wind resistance.
Deadwood	The removal of all dead, dying and diseased branches from a tree. Also, wood which is dead.
Dieback	Where branches are beginning to show signs of death usually at the tips in the crown.
Epicormic shoots	Small branches that grow in uncharacteristic clusters around the base or the stem of a tree, usually as a result of bad pruning or some other stress factor.
Formative pruning	The trimming of a tree to remove weaknesses and irregularities which may lead to problems. The formative pruning operation is aimed at reducing the potential for future weaknesses or problems within the tree's crown.
Included bark	Where the bark on two adjoining branches or stems is growing tightly together, forming a joint with limited physical strength.
Pollarding	A method of tree management in which the main trunk of the tree is cut at about 4m, and the resulting branches are then cropped on a regular basis.
Remedial pruning	The removal of old stubs, deadwood, epicormic growth, rubbing or crossing branches and other unwanted items from the tree's crown. Sometimes referred to as crown cleaning.
Topping	Topping is a form of pruning that removes terminal growth leaving a 'stub' cut end. Topping causes serious health problems to a tree.

2.0 General Guidelines

- 2.1 All work must be to BS 3998:2010 – Tree work - Recommendations
- 2.2 Staff carrying out the work must be qualified, experienced and ideally be Arboricultural Association approved contractors, and should be covered by adequate public liability insurance.
- 2.3 Any defects seen by a contractor or the client that were not apparent to the consultant must be brought to the consultant's attention immediately.
- 2.4 No liability can be accepted by the consultant in respect of the trees unless the recommendations of this method statement are carried out under the supervision of the designated arboriculturist.
- 2.5 It is advisable to have trees inspected by designated arboriculturist regularly.

APPENDIX E

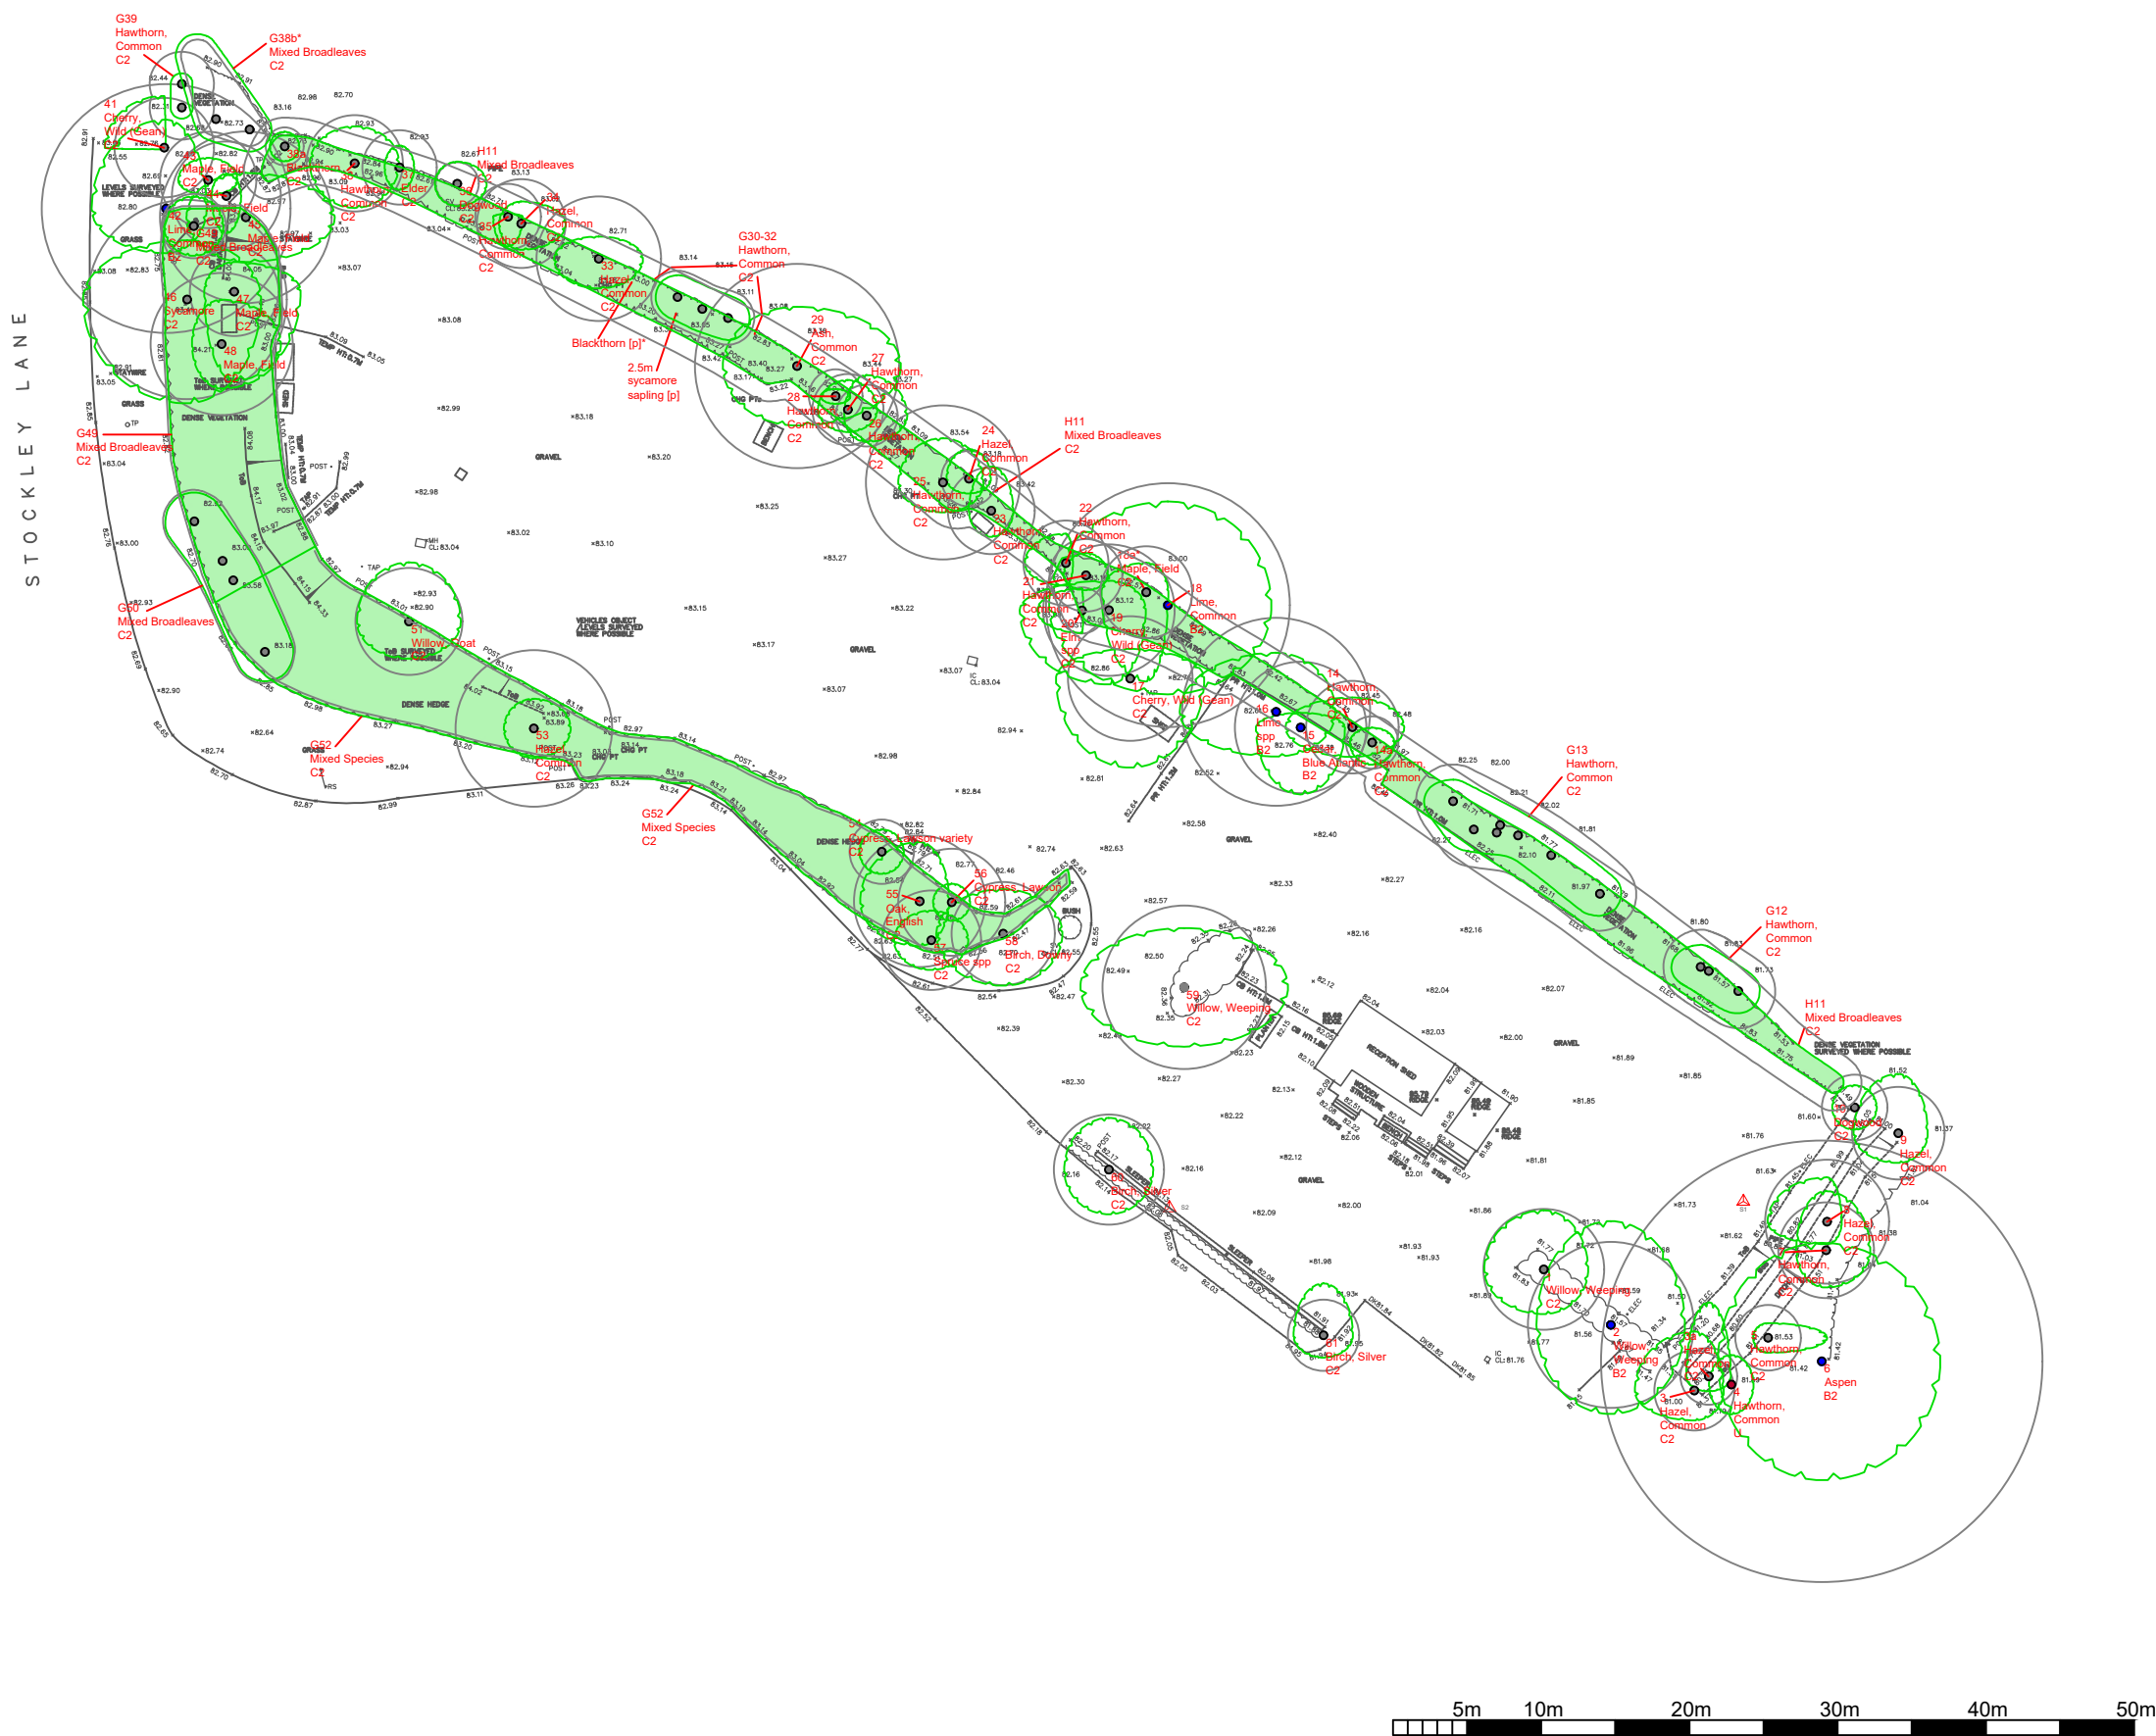

Arbortrack Systems Ltd

The Granary Studio, Crewe Lane, Kenilworth, CV8 2LA
07986 122074 / james@arbortrackservices.com

Site: Blackland Lakes, Calne

Drawing Title: Tree Constraints Plan


1:500@A3

Appendix: A

Rev A,
Nov 2025

Key:

- Category A
- Category B
- Category C
- Category U



NOTE: Tree/group numbers marked with an * have approximate locations.

Do not scale from this drawing. Please check all dimensions on site and notify us of any discrepancies.
This drawing was produced in colour. Do not rely on monochrome copies or those reduced in size.
This drawing is copyright [Arbortrack Systems Ltd] and may not be used or changed without the written consent of Arbortrack Systems Ltd.
