



SJ Stephens Associates

ARBORICULTURAL, LANDSCAPE &
MANAGEMENT CONSULTANTS

Savernake Barn
Stokke Common
Great Bedwyn
Marlborough
Wiltshire SN8 3LL
Tel: 01672 871 862
www.sjstephens.co.uk
e: info@sjstephens.co.uk

Arboricultural Impact Assessment

- Tree Survey
- Tree Protection Plan
- Arboricultural Method Statement

For:-

Four New Houses

At:-

Land adj Filands farm
Filands
Malmesbury
SN16 9JN

On behalf of:-

Mick Smith,
Northmoor Cottage,
Northmoor Lane,
South Cerney,
Cirencester,
GL7 5QD

Prepared by:

Simon Stephens MA Oxon, Dip
Arb(RFS), MArborA, C Env. MICFor
Email: simon@sjstephens.co.uk

Survey Date: 6th October 2025
Report Date: 11th December 2025
Project no: 2516

CONTENTS

- 1 BACKGROUND**
- 2 SURVEY DETAILS AND SCOPE**
- 3 SURVEY LIMITATIONS**
- 4 LEGAL PROTECTION OF TREES**
- 5 ARBORICULTURAL METHOD STATEMENT**
- 6 ARBORICULTURAL IMPACT ASSESSMENT**
- 7 REFERENCES**

Appendices

- A Tree Protection Plan: drawing no: 2516-02**
- B Tree Schedule**
- C BS 5837:2012 - Trees in relation to design, demolition and construction, Table 1**
- D Tree Protection Fencing Detail**
- E Site photos**
- F Proposed Site Plan**

1 BACKGROUND

- 1.1** This Arboricultural Impact Assessment has been instructed by Mick Smith to specify tree protection measures and assess the arboricultural impact of the proposed demolition of agricultural buildings and replacement with four new houses on land adjacent to Filands Farm.
- 1.2** Trees were surveyed, with findings shown in the Tree Schedule in Appendix B and plotted on the Tree Protection Plan in Appendix A. This also shows tree protection measures, which are specified in the Arboricultural Method Statement in section 5 below. The arboricultural impact is assessed in section 6, which assumes that these measures are followed.
- 1.3** The tree survey was undertaken, and this report has been prepared, by Simon Stephens MA Oxon, Dip Arb (RFS), MArborA, C Env, MICFor a Registered Consultant with the Arboricultural Association, with over 20 years relevant experience.
- 1.4** This survey and report have been prepared in accordance with the recommendations of BS 5837:2012, Trees in relation to design, demolition and construction - Recommendations.
- 1.5** Documentation supplied:
 - Topographical Survey
 - SJ Stephens Associates, Tree Constraints Plan, drawing 2516-02
 - Coombes Everitt Architects Ltd, Proposed Site Layout Plan: drawing no 25.20.010PL004

2 SURVEY DETAILS AND SCOPE

- 2.1 The site survey included trees and shrubs, within and immediately adjacent to the red line boundary, with a stem diameter over 75mm at 1.5m height, as shown located on the Tree Protection Plan, included as Appendix A.
- 2.2 Tree inspection took place from ground level with the use of binoculars, sounding hammer and metal probe using the Visual Tree Assessment method (Mattheck & Breloer 1994). The presence and condition of bark and stem wounds, cavities, decay, fungal fruiting bodies and any structural defects that could increase the risk of structural failure were noted.
- 2.3 Tree diameters were measured using a girthing tape and tree heights were measured using a hypsometer. Where use of a tape was restricted by site factors, diameters were estimated, with the diameter recorded in the tree schedule as eg "est 300".
- 2.4 At the time of the survey, the weather was fine with no restrictions to visibility. Broadleaf trees were in leaf. In places, dense undergrowth restricted access/dense ivy restricted visibility of tree stems.
- 2.5 Tree details are shown on the Tree Protection Plan included as Appendix A. Tree locations have been taken from the topographical survey provided. Where not included on the topographical survey, they have been determined by measuring distances from features shown on the plan, using a laser measuring device. The following information was recorded for each tree, and is shown in the Tree Schedule included as Appendix B:
 - **Number:** an identity number for each tree, prefixed with a "T", which cross references locations shown on the plan with the schedule in Appendix B. Where a number of trees are located close together and are similar in character and management requirements, they have been treated as a Group under a single number, prefixed with a "G".
 - **Species:** common name.
 - **Tree height:** approximate height in metres.
 - **Stem diameter:** diameter in millimetres, taken at 1.5m above ground. Where there are a number of stems, stem diameters are recorded in the condition column.
 - **Branch spread:** approximate spread in metres to N,S,E and W of the trunk. The approximate branch spread is drawn on the plan.
 - **Canopy clearance:** approximate height of the canopy above ground. Where a significant, low lateral branch is present, its height and direction of growth is included in the Condition column.
 - **Age class:** Young, Semi-mature, Early mature, Mature, Over-mature, Veteran.
 - **Condition:** features that affect the safe useful life expectancy and amenity of the tree, including the presence of decay or any physical defect.
 - **Management Recommendations:** recommendations to ensure the health and safety of the tree, within the future development.
 - **Estimated Remaining Contribution:** <10 years, 5-15 years, 10-20 years, 15-30 years, 20-40 years, >40 years.

- **Category grading:** tree classification taken from BS 5837:2012, Trees in relation to design, demolition and construction (see Appendix C for details), as follows:
 - Category U: Unsuitable for retention, trees with less than 10 years life expectancy, normally recommended for removal (Red)
 - Category A: high quality trees, able to make a substantial contribution for at least 40 years, normally retained unless there is an over-riding reason for removal and appropriate mitigation. (Green)
 - Category B: moderate quality trees, able to make a significant contribution for at least 20 years, normally retained. (Blue)
 - Category B/C: an intermediate category between categories B and C (not specifically described in BS5837). Trees, which should be retained wherever possible, providing retention does not unreasonably constrain the layout. (Blue)
 - Category C: low quality, in adequate condition to remain for at least 10 years, or young trees <150mm stem diameter. Trees which can be removed to allow the desired layout or new planting. (Grey)

For category A, B and C trees, a subcategory has been allocated, providing information on the reasons for selection of a specific category, as follows:

- Subcategory 1: mainly arboricultural values.
 - Subcategory 2: mainly landscape values.
 - Subcategory 3: mainly cultural values, including conservation.
- Trees have been classified irrespective of the possible proximity to future construction. The BS 5837 category is colour coded, as indicated above, on the plan included as Appendix A.
- **Protection Distance:** the protection distance in metres required to provide the Root Protection Area recommended in BS 5837, assuming a circular area centred on the tree.
- **Root Protection Area (RPA):** the area in m², as recommended in BS 5837, to provide sufficient rooting area to ensure tree survival and which, in most situations, should be fenced off to prevent root damage from construction activities.

3 SURVEY LIMITATIONS

- 3.1 No internal decay devices, or other invasive tools to assess tree condition, were used.
- 3.2 No soil excavation or root inspection was carried out.
- 3.3 This survey has not considered the effect that trees or vegetation may have on the structural integrity of future building through subsidence or heave.

- 3.4 The tree survey has been undertaken for planning purposes. Although any obvious structural defects have been noted, a Tree Hazard Assessment has not been carried out. Mature trees close to highly populated areas or public highways should normally be checked for safety annually, by a suitably qualified person.

4 LEGAL PROTECTION OF TREES

- 4.1 The Wiltshire Council website was viewed on 14-10-2025, showing that the site does not contain any Tree Preservation Orders, nor does it fall within a Conservation Area. The presence of Planning Conditions currently attached to the site, was not checked.

5 ARBORICULTURAL METHOD STATEMENT

5.1 Site Overview

- 5.1.1 The proposal is for the demolition of agricultural buildings and replacement with four new houses on land adjacent to Filands Farm. The proposed site plan is included as Appendix F and details have been added to the survey drawing, along with tree details, to create the Tree Protection Plan attached as Appendix A.
- 5.1.2 There are hedgerows along the western and southern site boundaries. The western hedgerow contains occasional birch growing through a dense thicket of thorn, damson, dying elm and damson. The southern hedgerow contains many dead elm and an early mature ash (T1) at the eastern corner, which is beginning to succumb to the ash dieback disease.

5.2 Tree Work

- 5.2.1 Details of proposed tree works are included in the Tree Schedule included as Appendix B.
- 5.2.2 Two trees and two tree groups are proposed for removal, as detailed in section 6.1 below.
- 5.2.3 All tree work must be undertaken to the standards set out in BS 3998:2010 Tree work – Recommendations.

5.3 Root Protection Areas

- 5.3.1 Root Protection Areas are shown for all trees in the tree schedule included as Appendix B. They are also shown for all retained trees, as circular areas centred on the trunk, on the Tree Protection Plan included as Appendix A. Where there are physical obstructions to root growth the Root Protection Area should be shown as an equivalent area that is more likely to reflect actual root growth. The Root Protection Area shows the area around a tree in which all

construction activity must normally be excluded, unless appropriate protection measures are implemented.

5.4 Tree Protection Fencing

5.4.1 Tree Protection Fencing must be erected where shown on the Tree Protection Plan, included as Appendix A. This will provide full protection of the Root Protection Areas of all retained trees within the site, other than for:

- areas hatched in blue on the Tree Protection Plan, where No-Dig Construction must be used, as described in section 5.5 below, to protect underlying roots.
- areas shaded cyan on the Tree Protection Plan, indicating Ground Protection Areas, where roots must be protected, as described in section 5.6 below.

5.4.2 Tree works can be completed before Tree Protection Fencing is erected, however no contractors plant or vehicles must be allowed to track within the Root Protection Areas unless ground protection panels are laid.

5.4.3 Tree Protection Fencing must be from weldmesh panels, at least 2m high, securely fixed, with wire or scaffold clamps, to a rigid framework. This framework must be constructed from scaffold tubes with vertical tubes, at a maximum interval of 3m and driven into the ground at least 0.6m. The structure must be well braced to resist impacts, constructed as per Figure 2 of BS5837:2012, which is reproduced in Appendix D.

5.4.4 After erection of Tree Protection Fencing and installation of ground protection, 2 days notice must be given to the Local Planning Authority before demolition or construction, including any ground work, starts on site.

5.4.5 Tree Protection Fencing must be maintained and retained for the duration of the works, or until such time as agreed in writing with the Local Planning Authority.

5.4.6 Weatherproof notices must be fixed to the Tree Protection Fencing, and maintained, stating:-

TREE PROTECTION AREA KEEP OUT

TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY PLANNING CONDITIONS
CONTRAVENTION MAY LEAD TO CRIMINAL PROSECUTION
THE FOLLOWING MUST BE OBSERVED BY ALL PERSONS:

- The Protection Fence must not be moved
- No person or machine must enter the area
- No materials or spoil must be deposited
- No excavation must be permitted

ANY INCURSION INTO THE PROTECTED AREA MUST BE WITH THE WRITTEN
PERMISSION OF THE LOCAL PLANNING AUTHORITY

5.5 No-Dig Construction Areas

- 5.5.1 The No-Dig areas, shown hatched blue on the Tree Protection Plan included as Appendix A, must be constructed without excavation apart from the removal of turf/organic matter, which must be carried out by hand. Excavators, dumpers and other site traffic must not be allowed to track on the No-Dig areas until roots are protected by the No-Dig surfacing or ground protection panels.
- 5.5.2 Engineering details must avoid localised compaction, using both a two dimensional geogrid, and a three dimensional cellular confinement system as integral components of the sub-base. A typical section is shown on the Tree Protection Plan included as Appendix A. As well as being fit for purpose, the design and methodology must protect tree roots, by ensuring the following:-
- topsoil/turf can be removed carefully by hand to a maximum of 75mm, but less if roots are found nearer the surface.
 - following leveling with soil or sand, a permeable, non-woven geotextile membrane, must be laid.
 - a suitable two dimensional geogrid, such the TriAx Geogrid supplied by Tensar International (www.tensar.co.uk), or the Biaxial Geogrid supplied by Geosynthetics Ltd (www.geosyn.co.uk), must be laid over the entire area and underneath the edging.
 - pressure treated timber edging boards, supported by driven stakes must be used.
 - a suitable cellular confinement system must then be laid to manufacturers instructions on top of the geogrid. Products that might be considered include Geoweb, supplied by Greenfix (www.greenfix.co.uk) or Cellweb, supplied by Geosynthetics Ltd (www.geosyn.co.uk). The depth of the system must be adequate to take the maximum axle weight, as per manufacturers guidance.
 - the cellular confinement system must be filled with clean (no fines), washed angular, 20/40mm, stone to provide load support, while allowing air and moisture to permeate to the root zone.
 - a further permeable, non-woven geotextile membrane, such as TreetexT300, or an alternative approved product which has similar oil trapping qualities, must be laid over the cellular confinement system.
 - a porous, surfacing material, free from contaminants, must then be laid. Either sand bedding and block paving, gravel or permeable tarmac would be suitable.
 - removed turf/topsoil can be used to grade surrounding ground levels.
- 5.5.3 Site traffic, including pedestrians, must not be allowed on the No-Dig areas unless roots are protected by existing hard surfacing, new No-Dig surfacing or unless suitable ground protection panels are laid. Either Maxitrack mats, as supplied by the Marwood Group, (www.marwoodgroup.co.uk) or Euro Mat or Pro Mat panels, from Ground Guards (www.ground-guards.co.uk), or a similar approved product, must be used, laid on top of a compressible layer of sand or woodchips, laid onto a geotextile.

- 5.5.4 Alternatively, the build up for the new No-Dig permeable surface can be used for construction traffic providing an adequate depth of cellular confinement system is used for the loads anticipated. In this case, the same section detail shown on the Tree Protection Plan must be used but with the sand and porous paving surface replaced with clean stone. This can then be removed together with the underlying geotextile at the end of the construction period and a new geotextile laid and final surface laid.
- 5.5.5 No-Dig construction will result in an increase in levels. This must be fully taken account of in all other aspects of the design.

5.6 Ground Protection Areas

- 5.6.1 The Ground Protection Areas, which are shaded cyan on the Tree Protection Plan, contain soft areas where ground protection must be laid to protect any underlying roots.
- 5.6.2 Maxitrack mats, as supplied by the Marwood Group, (www.marwoodgroup.co.uk) or Euro Mat or Pro Mat panels, from Ground Guards (www.ground-guards.co.uk), or a similar approved recycled product, must be used, laid on a compressible layer of sand or woodchips, laid onto a geotextile, with adjacent panels held together with connectors.
- 5.6.3 Ground protection must be laid before any construction starts on site and must be maintained in good condition until all construction operations have been completed. Ground protection must be fit for purpose and be replaced with an alternative product if panels start to move or any sign of ground compaction is seen.

5.7 General measures

- 5.7.1 No construction activity whatsoever, including routing of underground services, storage of materials or on-site parking, must be allowed within Root Protection Areas, other than that specifically described above.
- 5.7.2 No mixing or storage of cement, concrete, oil, fuel, bitumen or other chemicals must be permitted within 10m of the trunk of any retained trees, nor in any position where the slope of the ground could lead to contamination of the Root Protection Area.
- 5.7.3 Fires must not be lit in a position where their flames could extend to within 10m of foliage, branches or trunk.
- 5.7.4 Landscape works carried out within Root Protection Areas must be undertaken with great care so as not to damage shallow roots. Rotovators or other heavy mechanical cultivation must not be used within the Root Protection Areas.

- 5.7.5 If any tree shown for retention is removed, uprooted or destroyed, another tree must be planted in the same location, at a size and species to be agreed in writing with the Local Planning Authority.
- 5.7.6 A copy of this report and the Tree Protection Plan must be kept on site and must be fully understood by the Site Agent.

5.8 Bat roosts

- 5.8.1 The current legislation makes it a criminal offence to disturb, damage or destroy any bat roost or hibernation area. Contractors must be reminded of their responsibilities and should contact the relevant authorities if any signs of bats are found.

5.9 Birds

- 5.9.1 The current legislation makes it a criminal offence to disturb nesting birds. The nesting season is generally assumed to be from 1st March to 31st July, however this can vary depending on species and location. During these months a careful inspection must be made before work commences and works must be postponed if active nests are found.

6 ARBORICULTURAL IMPACT ASSESSMENT

- 6.1 The following trees / tree groups, categorized as per BS 5837 (see Appendix C for details), are proposed for removal:
- Category U – unsuitable for retention: two trees, T7 and T15 and one group of dead elm, G8.
 - Category B/C – between categories B and C:
 - G2 – a dense hedgerow, but from which only dead elm are being removed.
- 6.2 No trees need to be removed to facilitate the development, with only dead trees proposed for removal for safety.
- 6.3 Protection measures have been specified to protect the Root Protection Area of all retained trees.
- 6.4 Although preservation of Root Protection Areas is deemed to protect tree roots, in some cases buildings may need to be set further back to ensure the future sustainability of trees. If buildings are too close to trees, future occupiers may be likely to seek the reduction, or removal of trees, if they are cutting out excessive sunlight or providing a claustrophobic or threatening environment.

- 6.5** Section 5.2.2 of BS 5837:2012 states that “an indication of potential direct obstruction of sunlight can be illustrated by plotting a segment with a radius from the centre of the stem equal to the height of the tree, drawn from due North West to due East, indicating the shadow pattern through the main part of the day.” Shading patterns for key trees have been shown on the plan. This shows that new dwellings are outside potential shading areas apart from Unit 2, where there will be shading of part of the house in the late afternoons from the Birch, T13. However, since the house will not be shaded from the south, this is unlikely to be an issue.
- 6.6** Provided the recommendations in this report are followed, the arboricultural impact of this development on existing tree cover is likely to be negligible. No trees have to be removed and new tree planting is proposed as indicated on the proposed site plan.

7 REFERENCES


- *BS5837:2012 Trees in relation to design, demolition and construction – Recommendations.*
- *BS3998:2010 Tree Work. Recommendations.*
- *Common sense risk management of trees (FCMS024). Published by the National Tree Safety Group (www.ntsgroup.org.uk)*
- *The use of Cellular Confinement systems near Trees: a guide to good practice Arboricultural Association Guidance Note 12.*

BS 5837: TREE CATEGORY GUIDE

- Category U: Unsuitable for retention, trees with less than 10 years life expectancy.
- Category A: high quality trees, able to make a substantial contribution for at least 40 years, normally retained unless there is an over-riding reason for removal and appropriate mitigation.
- Category B: moderate quality trees, able to make a significant contribution for at least 20 years, normally retained.
- Category B/C: an intermediate category between categories B and C (not specifically described in BS5837). Trees, which should be retained wherever possible, providing retention does not significantly constrain the layout.
- Category C: low quality, in adequate condition to remain for at least 10 years, or young trees <150mm stem diameter. Trees which can be removed to allow the desired layout or new planting.

BS58837 Shade Area - area in which shading of living accommodation may affect sustainability of trees. Keep living accommodation out of these areas.

Wiltshire Council website shows there are no Tree Preservation Orders or Conservation Areas protecting trees (as at 14-10-2025).

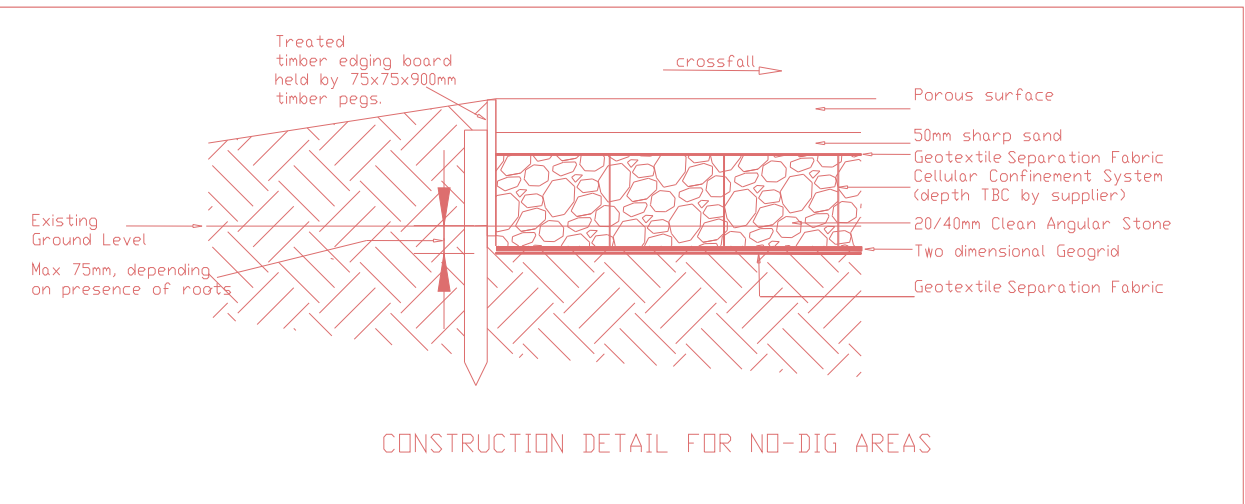

Land adjacent to Finland's Farm

Appendix B
BS 5837: 2012 Tree Schedule

Tree/ Group No.	Species	Height (m)	Stem Diam. at 1.5m (mm)	Branch Spread (m)				Canopy Clearance (m)	Age Class	Observations	Management Recommendations	Estimated Remaining Contribution (years)	BS 5837 Category Grading	Protect- ion Distance (m)	Root Protect. Area (m2)
				N	S	E	W								
T1	Ash	10	est 650	6	5	4	6	1.6	Early mature	Bifurcates at 1.5m - tight fork. Ash dieback beginning with 15% canopy dead. Basal stem (260mm) leaning to south west.		5-15	C2	7.8	191
G2	Hedge	3.5/11	50 - 125/ 100 - 200					0.0	Mature	Thorn/ blackthorn hedge with approx 14 dead elm, which are likely to fall on power line/ road. Hedge providing good screening.	Fell dead elm.	15-30	B-C2	2.4	18
G3	Thorn hedge	3.5 - 7	75 - 150					0.0	Mature	Good screening.		15-30	B-C2	1.8	10
G4	Leyland cypress	2.6	100 - 180					0.6	Early mature	Connifer hedge - recently topped.		10-20	C2	2.2	15
T5	Birch	15	est 420	6	6	4	5	3.5	Mature	Attractive tree growing in adjacent site - base not inspected.		20-40	B2	5.0	80
G6	Hedgerow	3 - 7	50 - 150					0	Mature	Unmanaged hedgerow including thorn, damson, elm, bramble.		15-30	B-C2	1.8	10
T7	Elm	7	110	3	3	3	3	1.6	Semi mature	Dead.	Remove.	<10	U	2.2	15
G8	3 no. Elm	8.5	70 - 180					2	Semi mature	Dead.	Remove.	<10	U	1.3	5
G11	3 no. Grey willow	1.8 - 3.2	est 120					0	Semi mature	3 multistem trees forming a clump.		20-40	C2	1.4	7
T12	Oak	2.5	20	0.5	0.5	0.5	0.5	0.6	Young	Good potential.		>40	C2	0.2	0
T13	Birch	14	est 260	3.5	3.5	3.5	3.5	2.5	Early mature	Growing in adjacent site - base not inspected.		20-40	B2	3.1	31
T14	Golden rain tree	6	est 400	4	3	8	2	1.5	Mature	Growing in adjacent site - base not inspected. Heavily reduced but good vigour.		20-40	B2	4.8	72
T15	Elm	7.5	130	1	1	1	1	1.3	Semi mature	Dead tree.	Remove.	<10	U	1.6	8
G16	Hedgerow	3 - 6.5	50-125					0	Mature	Dense hedgerow including field maple and blackthorn.		15-30	B-C2	1.5	7


BS 5837:2012, Table 1 Cascade chart for tree quality assessment

Category and definition	Criteria (including subcategories where appropriate)			Identification on plan
Trees unsuitable for retention (see Note)				
Category U Those in such a condition that they cannot realistically be retained as living trees in the context of the current land use for longer than 10 years	- Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other category U trees (e.g. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning) - Trees that are dead or are showing signs of significant, immediate, and irreversible overall decline - Trees infected with pathogens of significance to the health and/or safety of other trees nearby, or very low quality trees suppressing adjacent trees of better quality <i>NOTE Category U trees can have existing or potential conservation value which it might be desirable to preserve; see 4.5.7.</i>			See Table 2
	1 Mainly arboricultural qualities	2 Mainly landscape qualities	3 Mainly cultural values, including conservation	
Trees to be considered for retention				
Category A Trees of high quality with an estimated remaining life expectancy of at least 40 years	Trees that are particularly good examples of their species, especially if rare or unusual; or those that are essential components of groups or formal or semi-formal arboricultural features (e.g. the dominant and/or principal trees within an avenue)	Trees, groups or woodlands of particular visual importance as arboricultural and/or landscape features	Trees, groups or woodlands of significant conservation, historical, commemorative or other value (e.g. veteran trees or wood-pasture)	See Table 2
Category B Trees of moderate quality with an estimated remaining life expectancy of at least 20 years	Trees that might be included in category A, but are downgraded because of impaired condition (e.g. presence of significant though remediable defects, including unsympathetic past management and storm damage), such that they are unlikely to be suitable for retention for beyond 40 years; or trees lacking the special quality necessary to merit the category A designation	Trees present in numbers, usually growing as groups or woodlands, such that they attract a higher collective rating than they might as individuals; or trees occurring as collectives but situated so as to make little visual contribution to the wider locality	Trees with material conservation or other cultural value	See Table 2
Category C Trees of low quality with an estimated remaining life expectancy of at least 10 years, or young trees with a stem diameter below 150 mm	Unremarkable trees of very limited merit or such impaired condition that they do not qualify in higher categories	Trees present in groups or woodlands, but without this conferring on them significantly greater collective landscape value; and/or trees offering low or only temporary/transient landscape benefits	Trees with no material conservation or other cultural value	See Table 2

Figure 2

Key

- 1 Standard scaffold poles
- 2 Heavy gauge 2 m galvanised tube and welded mesh infill panels
- 3 Panels secured to uprights and cross-members with wire ties
- 4 Ground level
- 5 Uprights driven into the ground until secure (minimum depth 0.6 m)
- 6 Standard scaffold clamps

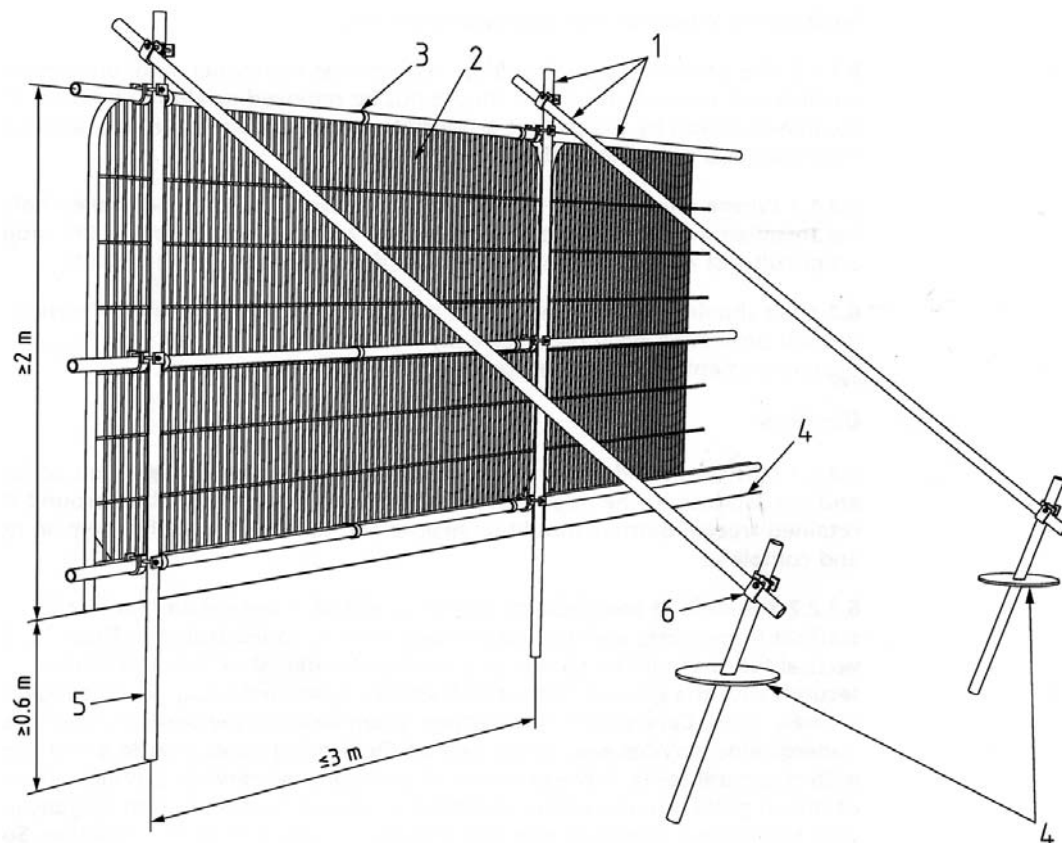

Examples of above-ground stabilising systems

Figure 3a

Stabiliser strut with base plate secured with ground pins





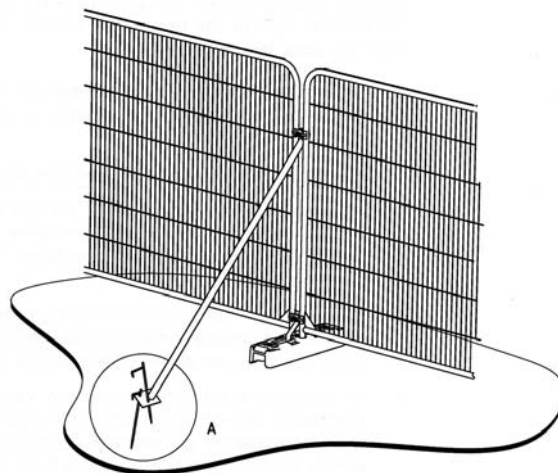


Figure 3b


Stabiliser strut mounted on block tray

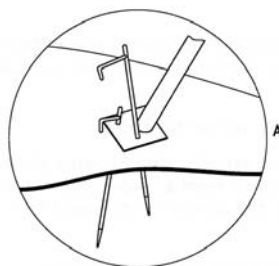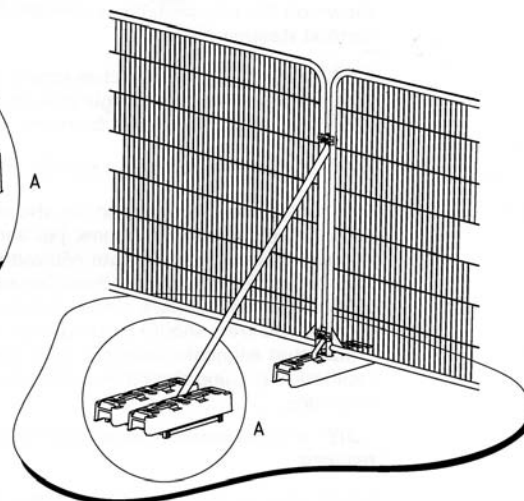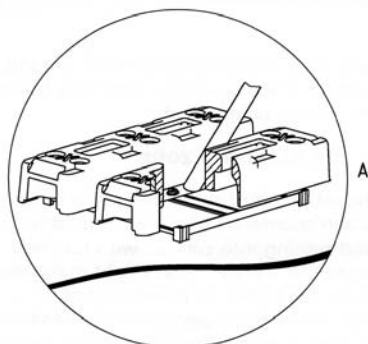

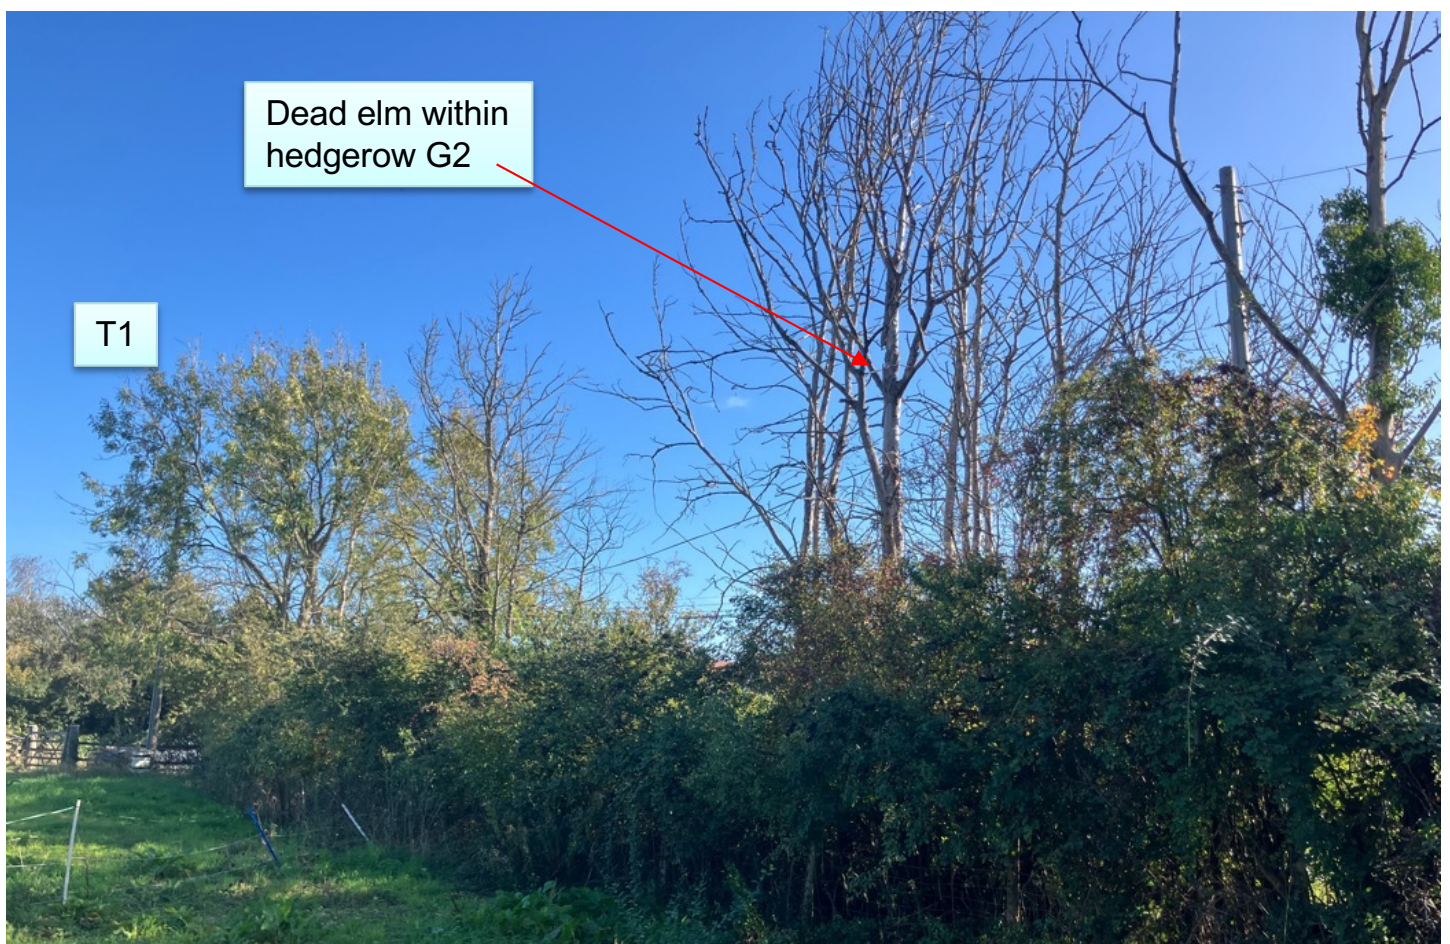

Proposed Residential Development , Land adj.
Filands Farm

1. This drawing and content is copyright © of coombes : everitt architects limited and should not be copied without their prior written consent.
2. For construction purposes only, do not scale drawing. All dimensions to be checked on site prior to construction and any discrepancies reported to contract administrator.
3. Do not use this drawing for setting out unless drawing specifically indicates setting out points.
4. Engineering information is indicative only and should be taken from structural engineers design.

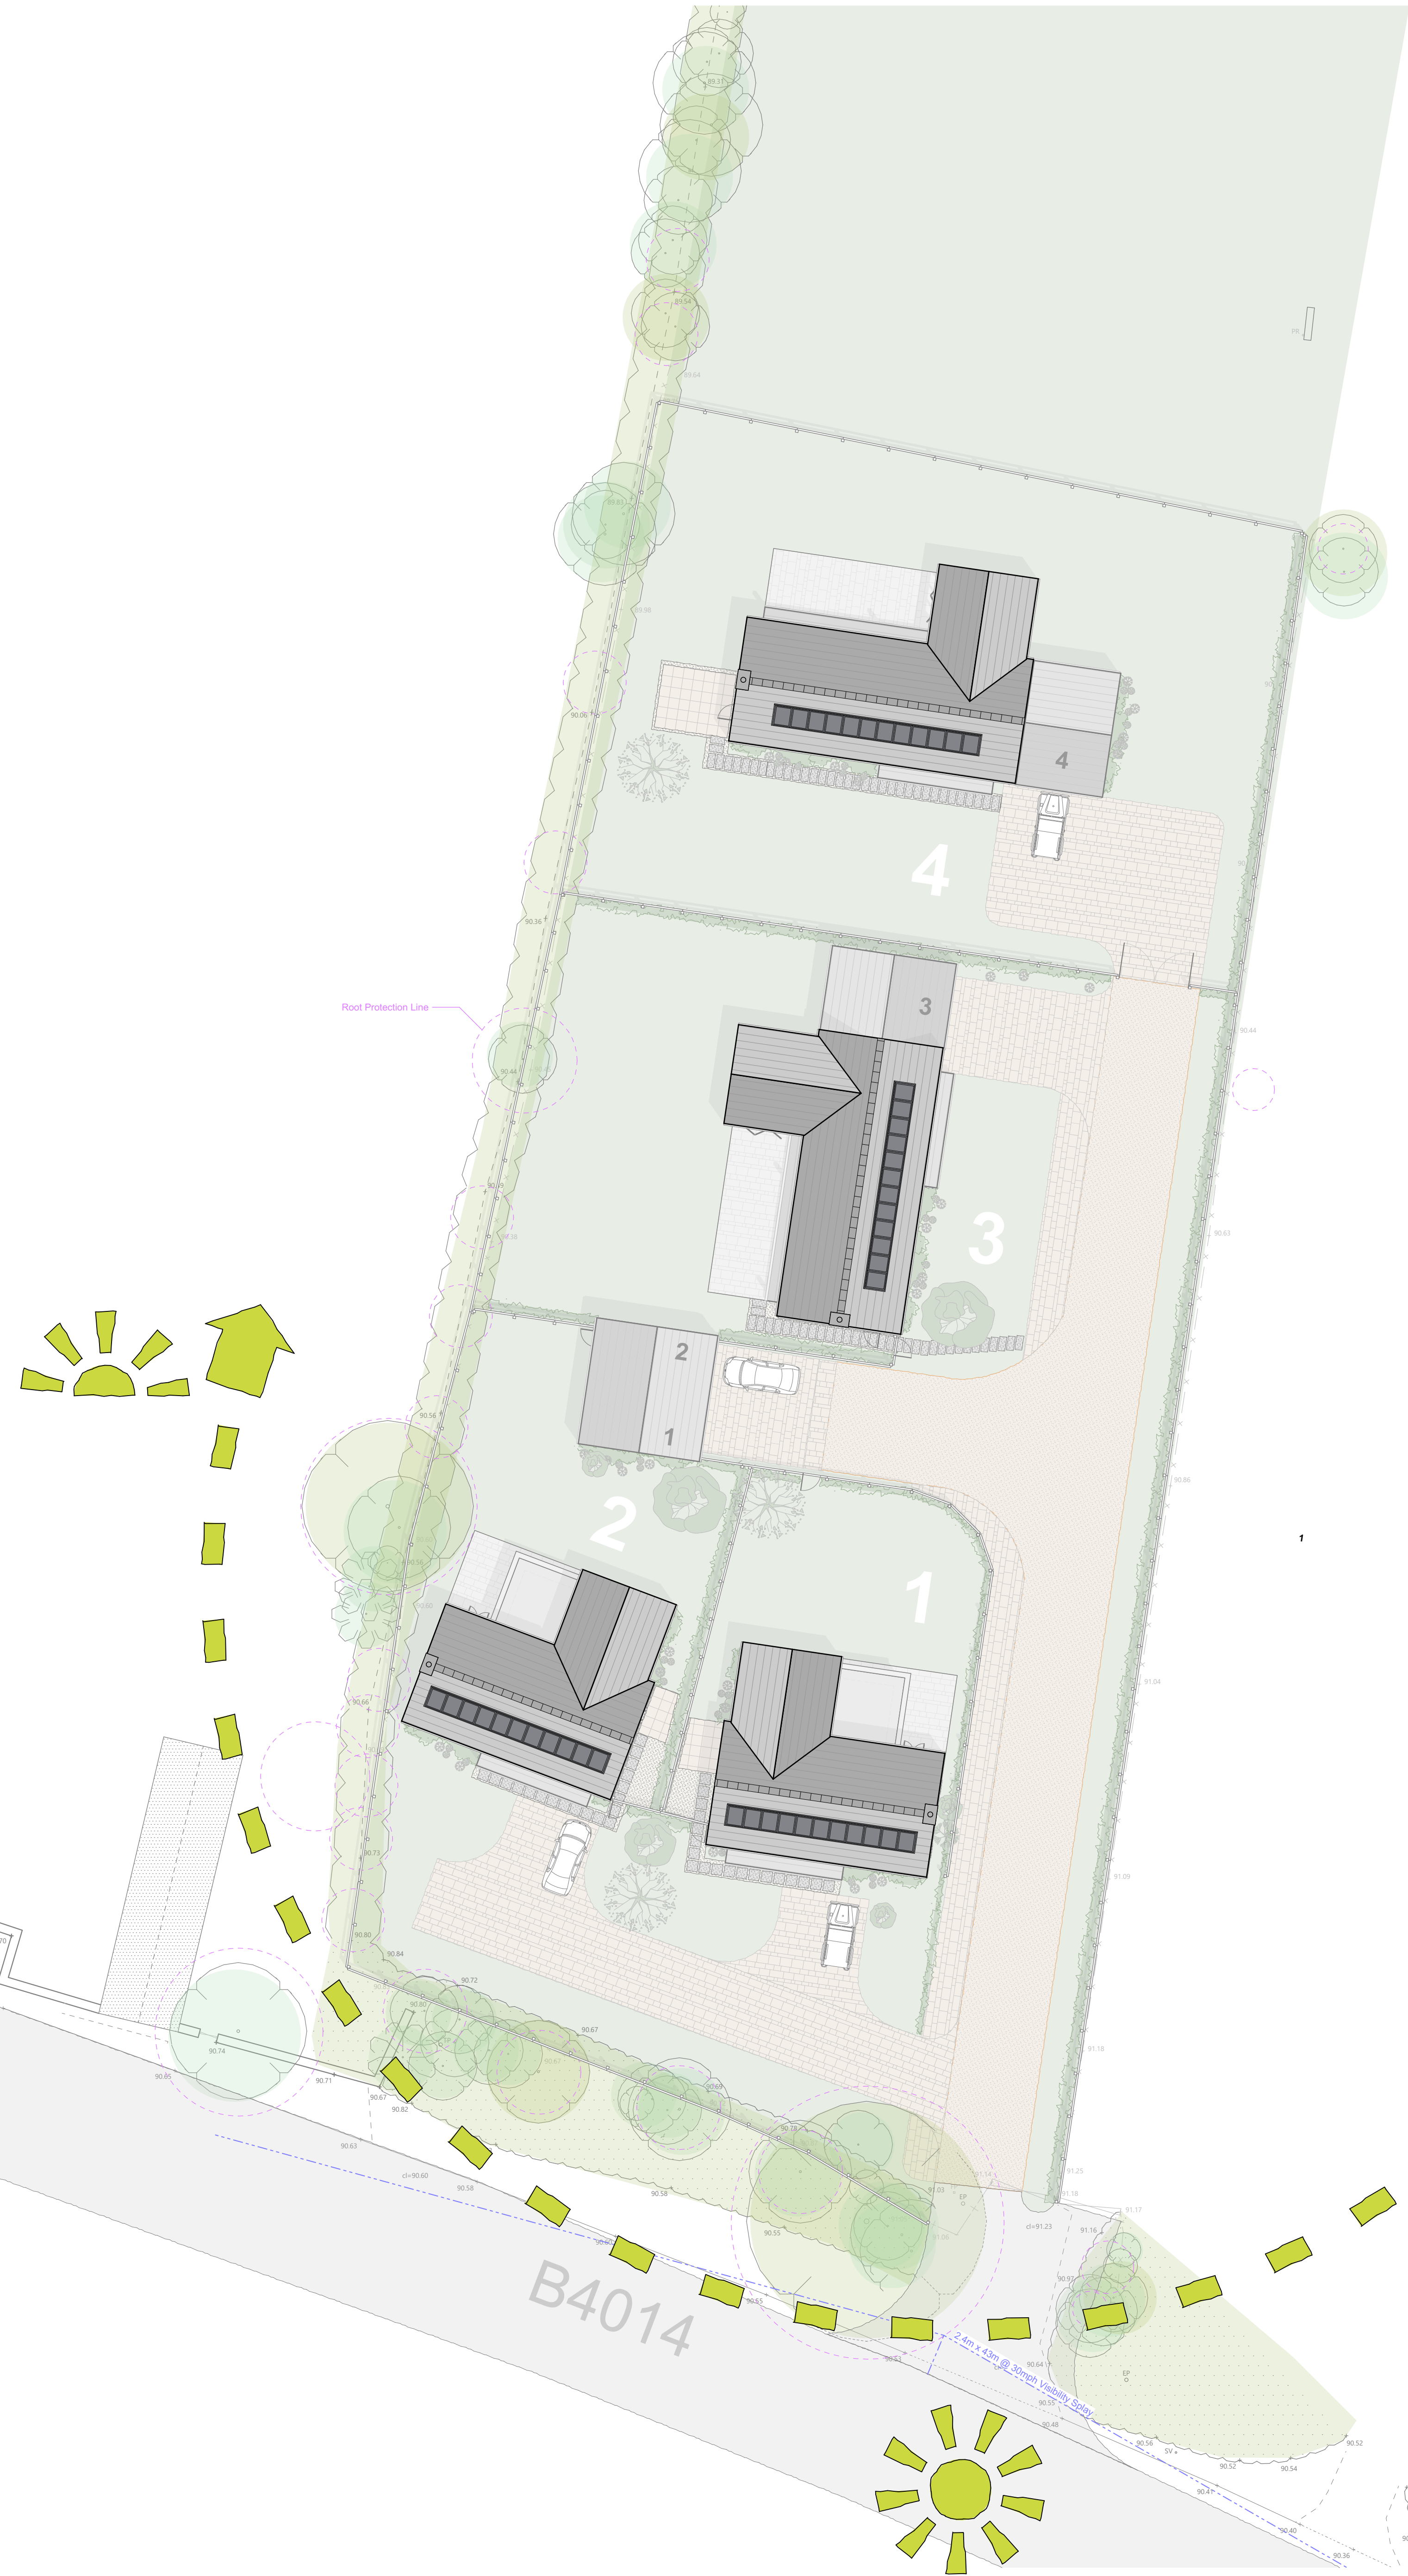

G I F A
Development Area:
Dwellings - 874m²
Garages - 92m²
Total - 966m²

Rev	Initial	Description / Amendment	Date
Drawing title:		Proposed Site Layout Plan	
Project:		Proposed Residential Development Land adj. Filands Farm, Filands, Malmesbury, SN16 9JN	
Scale:		As Shown: 1:200 @ A1	
Date:		28.11.2025	
Client:		Mr M Smith	
Drawn by:		LN	
Drawing No:		25.20.010.PL004	

coombes : everitt architects limited
105-107
Bath Road
Cheltenham
Gloucestershire
GL53 7LE
t: 01242 807727
e: info@ce-architects.co.uk
www.ce-architects.co.uk
Chartered Practice
coombes : everitt architects
