

Tree Protection Areas - Construction Exclusion Zones

INSTALLING PROTECTION Protective barriers and ground protection (as approved), must be installed before any materials or machinery are brought onto the site and before the commencement of any demolition, general site clearance, ground or construction works of any description.


RETENTION OF PROTECTION All protective measures must remain fully intact, vertical (in the case of barriers), in their approved locations, from the outset of the development and maintained, at all times, until all works have been completed on site, including any earthworks and associated soft landscaping works. Any approved phasing of protective measures must be fully observed and complied with.

RESTRICTIONS Tree Protection Areas/Construction Exclusion Zones are to remain completely undisturbed for the duration of all development works. No construction activity of any description including but not limited to the following must occur within these areas at any time:

- No excavation of any description.
- No storage, disposal of soil, rubble or materials of any other description.
- No alterations to existing levels or ground conditions.
- No vehicular access, parking or use of any tracked or wheeled machinery of any description.
- No tree works, without the written consent of the Council's Tree Service.
- No erection of temporary structures of any description.
- No fires.
- No storage disposal handling or use of any Chemicals including cement wastings.
- No fixtures or fittings of any description, security lighting, signage etc shall be attached to any part of a tree.
- No trees shall be left within 10 metres of the canopies of any tree or spread of any hedge.
- No chemicals, fuel, liquids/waste residues of any other description to be stored or disposed of within close proximity to or drained towards/into protection areas.

PROTECTION AREA SIGNAGE All weather notices as below or similar to be fixed to protective barriers at regular intervals (maximum spacing 50m) throughout site and maintained until completion of all development works.

PLANNING COMPLIANCE The protective measures detailed on this drawing are a legal requirement. Failure to protect the trees/hedges in full accordance with the approved scheme may lead to enforcement action being taken by the Local Authority.

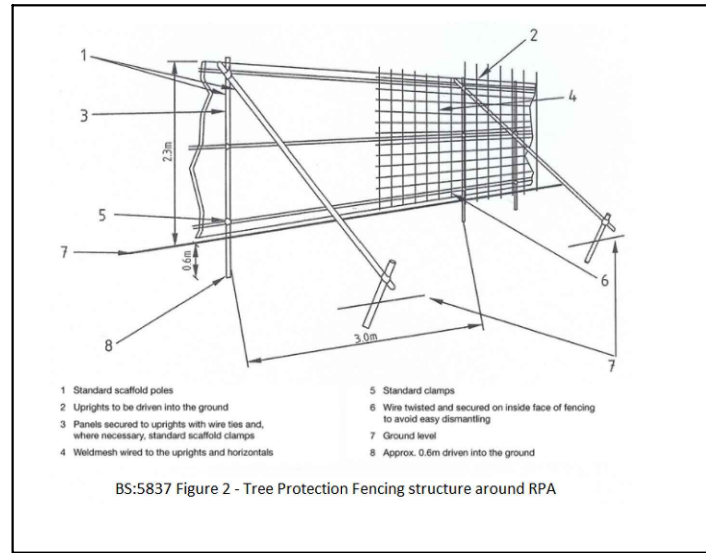

SECTION OF EXISTING RETAINING WALL TO BE REMOVED TO ALLOW AMENDMENT TO ACCESS

EXISTING AND/OR AMENDED ACCESS TO BE USED FOR CONSTRUCTION.



KEY - TREES

- T001 HIGH-GRADE CATEGORY 'A' TREE
- T002 MEDIUM-GRADE CATEGORY 'B' TREE
- T003 LOW-GRADE CATEGORY 'C' TREE
- T004 CATEGORY 'U' POOR QUALITY TREE -
- BS:5837 ROOT PROTECTION AREA (RPA)
- T005 TREE TO BE REMOVED TO FACILITATE THE BUILD
- TEMPORARY GROUND PROTECTION (PEDESTRIAN)
- POROUS DRIVEWAY EXTENSION
- TEMPORARY GROUND PROTECTION (VEHICULAR)
- NO-DIG POROUS COURT SURFACE WITHIN RPA OF ADJACENT TPO TREES
- HAND-DIG FOOTINGS WITHIN THE RPA OF RETAINED TREES
- TEMPORARY TREE PROTECTION FENCING
- CONSTRUCTION EXCLUSION ZONE - KEEP OUT!

BS5837 TREE PROTECTION PLAN

Client:
MR. J. SPENCER-JONES

Site:
THE OLD MANOR
THE SQUARE
ALDBOURNE
WILTSHIRE
SN8 2DU

The location of the trees within the Tree Protection Plan has been taken from a topographical survey provided by the client. Trees not shown on the survey have been plotted by eye by the Tree Surveyor.

The position of trees should not therefore be taken as exact but this plan is considered to be a good representation of tree locations in relation to the Old Manor and the proposed building works.

Survey by Sarah Duckworth
Arboricultural Consultant

sarahduckworth@hotmail.com
M:07810 440546

Scale 1:200 @ A1
Date: JANUARY 2026

Ref: THE OLD MANOR TPP 06898 2026 0.2
