

Landscape and Ecological Management Plan

Land at Spitfire Road, Calne

17 April 2026

Ecology
Arboriculture
Land Management



Report Details

Report Title	Landscape and Ecological Management Plan
Report Reference	3130-LEMP-LO

Quality Assurance & Revision Record

Revision	Date	Author	Checked By	Approver	Summary of Changes
V5	17 April 2026	Harry Dyer BSc	Nick Hargreaves BSc MSc MCIEEM	Nick Hargreaves BSc MSc MCIEEM	Minor figure amendments.
V4	10 April 2026	Luke Owen BSc	Chris Merrick BSc ACIEEM	Chris Merrick BSc ACIEEM	Minor text and figure amendments.
V3	22 December 2025	Luke Owen BSc	Chris Merrick BSc ACIEEM	Chris Merrick BSc ACIEEM	Minor figure amendments.
V2	08 December 2025	Luke Owen BSc	Chris Merrick BSc ACIEEM	Chris Merrick BSc ACIEEM	Minor figure amendments.
V1	28 November 2025	Luke Owen BSc	Chris Merrick BSc ACIEEM	Chris Merrick BSc ACIEEM	

Disclosure

The content of this report that has been provided by GE Consulting is true, and has been prepared and submitted in accordance with the Chartered Institute of Ecology and Environmental Management's Code of Professional Conduct. Its contents are compliant with British Standard BS42020: 2013 Biodiversity Code of Practice for Planning and Development.

This report has been prepared for the exclusive use of the stated client and unless otherwise agreed in writing by GE Consulting, no other party may use, make use of or rely on the contents of the report. No liability is accepted by GE Consulting for any use of this report, other than for the purposes for which it was originally prepared and provided.

GE Consulting has exercised due care in preparing this report. It has not, unless specifically stated, independently verified information provided by others. No other warranty, express or implied, is made in relation to the content of this report and GE Consulting assumes no liability for any loss resulting from errors, omissions or misrepresentation made by others.

Any recommendation, opinion or finding stated in this report is based on circumstances and facts as they existed at the time that GE Consulting undertook the work. Nothing in this report constitutes legal opinion. If legal opinion is required the advice of a qualified legal professional should be secured.

© Copyright GE Consulting Services (UK) Limited 2025

Site Details

Site Name and Location	Land at Spitfire Road, Calne
Central OS Grid Reference	SU 00897 71534
Client	Allison Homes

Boundary



Contents

1	Introduction	1
1.1	Background	1
1.2	Site Description	2
1.3	Aims of LEMP	2
2	Description of Habitats To Be Managed	2
3	Additional Features.....	3
4	Management Mechanism.....	5
4.1	Managing Agent	5
4.2	Funding	5
4.3	Management Constraints	6
4.4	Management and Maintenance Responsibilities.....	6
5	Management Schedule	6
6	Monitoring.....	14
6.1	Plan Review	14

Figures

- 1: Enhancements and Mitigation Plan

Appendices

Appendix 1 – Landscape Strategy Plan.....	16
Appendix 2 – On Plot Planting Plans Plan	17

1 Introduction

This Landscape and Ecological Management Plan (LEMP) has been produced by GE Consulting on behalf of Allison Homes in relation to a residential development at Land at Spitfire Road, Calne.

The area within the application boundary is hereafter referred to as the 'Site'.

This document accompanies a Reserved Matters Application and is to be used to guide management of the Site.

This LEMP serves a period of 5-years following commencement of development. It will be reviewed and updated at the end of this period when new habitats have established, however is capable of being rolled out over the lifetime of the development.

1.1 Background

The Site was granted outline planning permission at appeal in February 2025 (planning ref: PL/2022/07893) for 'residential development for up to 90 dwellings, associated works including infrastructure, ancillary facilities, play area and open space and landscaping. Construction of a new vehicular access off Spitfire Road and demolition of existing structures.

This document has been prepared to provide sufficient information to satisfy Condition 14 of the outline consent and to accompany a Reserved Matters Application. Condition 14 states:

"Landscape and Ecology Management Plan: Prior to the commencement of works, a Landscape and Ecology Management Plan (LEMP) shall be submitted to and approved in writing by the Local Planning Authority. The LEMP will include:

- a) long term objectives and targets for retained, created and enhanced habitats;*
- b) management responsibilities and maintenance schedules for each ecological feature within the development;*
- c) the mechanism for monitoring success of the management prescriptions; and*
- d) a procedure for review and necessary adaptive management in order to attain targets.*

The LEMP shall be implemented in full and for the lifetime of the development in accordance with the approved details."

In addition, the report will discharge Condition 17, outlined in **Section 3** and **Figure 1**:

"Wildlife features: Prior to the commencement of any works, including vegetation removal and demolition, a scheme (based on a site plan/technical elevations drawing) showing details of the number, design and locations of features for bats, birds, reptiles and invertebrates, as well as a timetable for implementation, shall be submitted to and approved in writing by the Local Planning Authority.

The approved details shall be implemented before occupation of the final works. These features shall continue to be available for the target species for the lifetime of the development."

The document will also be compliant with Condition 13:

"Ecology: The development shall be carried out in accordance with the following documents:

- a) Ecological Assessment. Ref: 10185.EcoAss.vf2. Ecology Solutions; and*
- b) Ecological Parameters Plan. Rev C. December 2023."*

1.2 Site Description

The Site is situated in the east of Calne and comprises four semi-improved grassland fields with boundary hedgerows/scrub, trees, a pond and a single corrugated metal building and an area of hardstanding.

1.3 Aims of LEMP

The aims of this document are to:

- 🐾 Provide details on habitat creation and enhancement measures, which will ensure a net gain in biodiversity;
- 🐾 Provide sufficient detail on management operations to ensure that retained and new habitats are managed and maintained in the long-term;
- 🐾 Provide a timetable for the implementation of the LEMP; and
- 🐾 Provide a monitoring framework to ensure that appropriate refinements and/ or revision of the plan can be made, in order to promote any objectives/ targets of the LEMP.

This LEMP should be read in conjunction with the Landscape Strategy Plan (13642-XX-XX-DR-L-0001-P11) in **Appendix 1** which sets out the specification for planting.

2 Description of Habitats To Be Managed

Table 1 below provides a summary of the features that the Site supports or are to be created. These features will be managed for the lifetime of the development.


Table 1: Features to be Managed

Feature	Details
Retained trees	🐾 Retained trees throughout the Site.
Retained hedgerows	🐾 Retained hedgerows around the Site boundaries and within the centre of the Site.
New native tree planting	🐾 Proposed native tree planting throughout the Site.
New native species-rich hedgerows	🐾 New native hedgerows planted throughout the Site.
New amenity grassland and turf	🐾 New amenity grassland in areas throughout Site including POS and adjacent to hedgerows.
New meadow grassland	🐾 New meadow grassland planting around Site along the eastern and northern edges within retained reptile habitat.
New native bulb planting	🐾 New native bulb planting throughout the Site.
New street tree planting	🐾 New street tree planting throughout the Site.
New main street ornamental planting	🐾 New ornamental planting throughout the Site.
New main street hedge	🐾 New hedgerow planted throughout the Site.
New main street feature shrub	🐾 New shrub planting throughout the Site.
New housing core ornamental planting	🐾 New ornamental planting throughout the Site.
New housing core side hedge	🐾 New hedgerow planted throughout the Site.
New housing core feature shrub	🐾 New shrub planting throughout the Site.


3 Additional Features

The Site will be enhanced for nesting birds, roosting bats, reptiles, invertebrates and hedgehogs in line with Wiltshire Design Guide 2024¹ as detailed in **Table 2** below and illustrated on **Figure 1**.

Table 2: Additional Features

Quantity & Type	Illustrations	Description & Installation
Integrated bird nest box (ratio of one per dwelling)	 WoodStone Build-in Swift Nest Box Deep (nhbs.com)  Installation – integral nestbox installed in outer leaf of brickwork in a traditional cavity wall construction	- Density: one box per dwelling, to be clustered in groups of three boxes. - Fully integrated boxes to be built into the fabric of the building. These are more secure and eliminate future maintenance requirements. - Suitable models include the PRO UK Rendered Build-in Swift Box or the WoodStone Build-in Swift Nest Box Deep which can be chosen to suit the finishing of the building. Suppliers include www.nhbs.com and www.wildcare.co.uk. - Swift boxes are recommended as they are considered a universal box suitable not only for swifts but also for house sparrows and other small birds (CIEEM, 2021). - Install at the highest point of the building, ideally at least 5m above ground level. - To be sited under the shelter of eaves or overhanging roofs where possible, avoiding locating above doors and windows. - Entrance out of direct sun and the prevailing weather and away from perches/ledges where birds are at risk from predators. - Ensure a clear flyway of ideally at least 5m, avoiding obstructions such as trees. - See swift-conservation.org for additional advice.
Integrated bat boxes (ratio of one per dwelling)		- Density: one box per dwelling, to be clustered in groups of two. - Fully integrated boxes to be built into the fabric of the building. Install within the cavity of house walls. The entrance hole can sit flush to a course of bricks. - Suitable models include the Vivaro Pro Build-in Woodstone Bat Tube, Habibat

¹https://www.wiltshire.gov.uk/media/13006/Wiltshire-Design-Guide-2024/pdf/8320_WiltshireDesignGuide_Consultation_Accessible.pdf?m=1711382742703

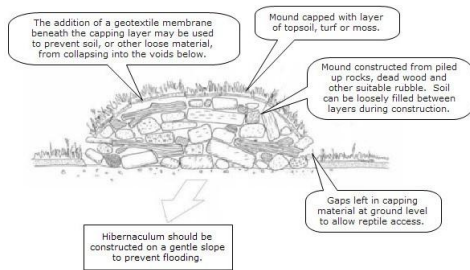Quantity & Type	Illustrations	Description & Installation
	Vivaro Pro Build-in Woodstone Bat Box and Habibat Bat Box  Installation	Bat Box or similar approved which can be chosen to suit the finishing of the building. Suppliers include www.nhbs.com and www.wildcare.co.uk. - Position a minimum of 3m above the ground. - Locate where there is a clear, unlit flight path for bats to linear vegetation (e.g. hedgerows) and away from windows. - Install away from any lighting.
Four hibernaculum/ habitat/ log piles	 Example hibernacula design	- Provide hibernacula/ resting places for fauna such as reptiles, mammals and invertebrates. - Constructed from dead wood and rubble, topped with loose soil and turf. Dimensions to be a minimum of 2m length x 1m width x 1m height. - Located in suitable locations such as within the northern, eastern and southwest boundaries in relatively undisturbed marginal areas of the Site.
Five bee bricks located on suitable south-facing walls	Green&Blue Bee Brick 	- Ideally located within suitable south-facing walls. - Should be located at least 1m off the ground and unobstructed by vegetation and located close to nectar and pollen sources.
Three hedgehog domes	Schwegler Hedgehog Dome 	Dome should be placed in sheltered areas outside in areas of dense vegetation and outside of direct sunlight.

Quantity & Type	Illustrations	Description & Installation
Hedgehog holes		- Include 13cm x 13cm cut out through close-boarded fences (or equivalent gaps under fences) to allow hedgehog movement throughout Site. - These can be holes created during fence construction, or purpose made products such as the Durapost Hedgehog Hole and Hedgehog Gravel Boards (or similar) available from suppliers including www.jacksonsfencing.co.uk or www.wickes.co.uk. - To reduce the risk of these being blocked by future residents, a small 'Hedgehog Highway Sign' should be attached. Available from www.nhbs.com. - Further information is available at: https://www.hedgehogstreet.org/help-hedgehogs/link-your-garden/

4 Management Mechanism

This section describes how the LEMP will be implemented, who will fund it and who will be responsible for its delivery.

4.1 Managing Agent

The Managing Agent will be the organisation responsible for the delivery of the LEMP. In the long-term it is anticipated that the POS and other features included within this LEMP will be managed by a Management Company which will be briefed on the requirements set by the LEMP to ensure features are maintained over the course of the LEMP.

Until occupation of the last dwelling, the Managing Agent will be **Allison Homes** or successors in title. This is a holding arrangement during which time the developer is responsible for implementing the landscape proposals, and for any maintenance accruing during that time.

After the occupation of the last dwelling, it is anticipated that a Residents' Funded Management Company (RFMC) will be established for the Site. The RFMC will be responsible for the maintenance of POS and landscaping, in line with this LEMP for the lifetime of the development.

The Managing Agent or RFMC will appoint an Approved Contractor to undertake the works specified in the LEMP. The Approved Contractor will be a suitably qualified and experienced contractor, capable of delivering the ongoing management works in line with the LEMP.

4.2 Funding

Allison Homes will fund the costs of compliance with the LEMP until practical completion of the development.

Following occupation of the final dwelling, the ongoing maintenance will be funded by the RFMC with costs distributed amongst residents. It is anticipated that each household will be charged an annual management fee (precise sums to be agreed prior to sale and based pro rata on the number of bedrooms in each dwelling). The RFMC shall use the funds for the purposes of delivering the LEMP, together with other Site maintenance and insurance matters.

4.3 Management Constraints

The Site is known to support 'low' populations of common reptiles (slow worm and grass snake). Therefore, grassland in the retained habitat and green corridors should be mown in a manner sympathetic to reptiles (see Management Schedule).

The Site is likely to support nesting birds and supports foraging and commuting bats. Management of native hedgerows and trees should be undertaken between November and February inclusive.

4.4 Management and Maintenance Responsibilities

As outlined within the On Plot Planting Plans Plan (13642-XX-XX-DR-L-0002-0007) in **Appendix 2**, for the first 12 months following practical completion of the landscaping works, maintenance of landscaped areas will be the responsibility of the landscape contractor which undertook the implementation. Regular maintenance visits will be undertaken by the landscape contractor following planting to maintain all areas in a weed and litter free condition, as outlined below, and to ensure the healthy establishment of all planting stock (including through watering). Any litter collected will be disposed of at a licenced waste disposal centre and any arisings will be recycled at a licensed composting site.

Throughout this initial maintenance period, the landscape contractor will be responsible for sourcing and supplying all water required to meet the watering regime. Watering will be undertaken using targeted and efficient methods (e.g. bowser watering or low-flow systems) directed at the root zone to minimise evaporation losses and avoid unnecessary water use. Watering will be undertaken as necessary, taking account of prevailing weather conditions, to support healthy establishment of all stock. On completion of the 12-month maintenance period, the responsibility for maintaining all stock in a healthy condition (including watering) will be passed to the appointed management company and will follow the Management Schedule outlined in **Table 3**.

5 Management Schedule

Table 3 below provides a timetable for the establishment of the proposed mitigation measures as well as a maintenance specification for a period of 5 years post-completion. Following the end of the initial 5-year period under which this LEMP covers, it will be reviewed and updated when new habitats have been established. In the absence of this however, this LEMP is capable of being rolled out over 5-year cycles for the lifetime of the development. Locations of each habitat are shown on the Landscape Strategy Plan (13642-XX-XX-DR-L-0001-P11) in **Appendix 1**. Detailed prescriptions are provided in **Table 3**.

Table 3: Management Schedule

Ecological Feature	Objective/ Target	Prescription/ Action	Year Post Commencement					Month											
			1	2	3	4	5	J	F	M	A	M	J	J	A	S	O	N	D
Retained trees	🌳 Maintain/improve structure	Conduct annual inspections of trees to assess health of trees and to consider public health and safety. Carry out pruning to encourage good structure and form and undertake remedial action if there are health and safety concerns.	✓	✓	✓	✓	✓	✓	✓	If required for health and safety, but nesting bird check required.						✓	✓	✓	✓
Retained hedgerows	🌳 Enhance species diversity	Coppice or hedge laying of leggy hedgerows.	✓	-	-	-	-	✓	✓	-	-	-	-	-	-	-	-	✓	✓
	🌳 Maintain/improve structure	Plant up gaps with native hedge mix as per the native species rich hedgerow mix outlined on the Landscape Strategy Plan.	-	✓	-	-	-	✓	✓	✓	-	-	-	-	-	-	-	-	✓
		Following planting, water new hedgerow whips in periods of extreme drought (two weeks or more without rainfall), trees that have not yet established (not healthy, not in full leaf, suppressed growth) need to be watered where their tolerance to drought is deemed to be insufficient.	✓	✓	✓	-	-	-	-	-	✓	✓	✓	✓	✓	✓	-	-	-
		Prune any diseased or rotten wood back to sound wood. Remove all cut material from Site.	-	✓	✓	✓	✓	✓	✓	-	-	-	-	-	-	-	-	✓	✓
		Replace any dead, diseased or damaged stock. Regularly remove litter and fallen leaves to maintain a neat appearance.	✓	✓	✓	✓	✓	✓	✓	✓	-	-	-	-	-	-	-	-	-
New native tree planting	🌳 Ensure new trees are well established	Plant in accordance with the Landscape Strategy Plan.	✓	-	-	-	-	✓	✓	✓	-	-	-	-	-	-	✓	✓	✓
		Regularly check ties and stakes adjusting as needed. Remove stakes and ties after two years. Examine all guards and replace or adjust as appropriate. Remove guards once trees are established.	✓	✓	-	-	-	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓

Ecological Feature	Objective/ Target	Prescription/ Action	Year Post Commencement					Month											
			1	2	3	4	5	J	F	M	A	M	J	J	A	S	O	N	D
		Spraying, strimming or hand removal of weeds within a 1m diameter circle (mulched) around each tree to reduce competition and aid establishment. Once established the sward can be allowed to grow up to the trunk, although tall weeds, bramble and ivy will be removed from around the trees. Care will be taken when using strimmers or mowers to avoid damaging trees. Weeds and grass within 100mm of the trunks will be removed by hand. Regularly remove litter and fallen leaves to maintain a neat appearance.	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓	✓	✓	✓	✓	-	-
		Replace failed specimens on a like-for-like basis. Top up mulch to a depth of 75mm where necessary.	✓	✓	✓	✓	✓	✓	✓	✓	-	-	-	-	-	-	✓	✓	✓
		Where periods of extreme drought occur (two weeks or more without rainfall), trees that have not yet established (not healthy, not in full leaf, suppressed growth) need to be watered where their tolerance to drought is deemed to be insufficient.	✓	✓	✓	-	-	-	-	-	✓	✓	✓	✓	✓	✓	-	-	-
		Conduct annual inspections of trees to assess health of trees and to consider public health and safety. Carry out pruning to encourage good structure and form and undertake remedial action if there are health and safety concerns.	✓	✓	✓	✓	✓	✓	✓	If required for health and safety, but nesting bird check required.						✓	✓	✓	✓
New native species-rich hedgerow	 Ensure new hedgerows are well established	Plant in accordance with Landscape Strategy Plan.	✓	-	-	-	-	✓	✓	✓	-	-	-	-	-	-	✓	✓	✓
		Water hedgerows in periods of extreme drought (two weeks or more without	✓	✓	✓	-	-	-	-	-	✓	✓	✓	✓	✓	✓	-	-	-

Ecological Feature	Objective/ Target	Prescription/ Action	Year Post Commencement					Month											
			1	2	3	4	5	J	F	M	A	M	J	J	A	S	O	N	D
		rainfall), trees that have not yet established (not healthy, not in full leaf, suppressed growth) need to be watered where their tolerance to drought is deemed to be insufficient.																	
		Replace failed specimens on a like-for-like basis. Remove dead/ diseased specimens. Regularly remove litter and fallen leaves to maintain a neat appearance.	✓	✓	✓	-	-	✓	✓	✓	-	-	-	-	-	-	✓	✓	✓
		Examine all guards and replace or adjust as appropriate. Remove guards once hedgerows established.	✓	✓	✓	-	-	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓
		Spraying or strimming of weeds to reduce competition and aid establishment. Not required if weed suppression matting used.	✓	✓	✓	-	-	-	-	-	-	-	-	✓	✓	-	-	-	-
		Hedgerows to be pruned to 45-60cm above ground level to encourage dense growth in second year. Side trimming of new hedgerows to promote healthy hedgerow base. Top up mulch as required. Remove cut material from Site. Maintain temporary fence until well-established.	-	✓	-	-	-	✓	✓	-	-	-	-	-	-	-	-	✓	✓
		Allow hedgerow to grow to desired height with incremental cutting. Starting in year 4 after planting new hedgerows will be cut along one side annually, alternating between the two sides of the hedgerow each year.	-	-	-	✓	✓	✓	✓	-	-	-	-	-	-	-	-	✓	✓

Ecological Feature	Objective/ Target	Prescription/ Action	Year Post Commencement					Month											
			1	2	3	4	5	J	F	M	A	M	J	J	A	S	O	N	D
New amenity grassland and turf	 Ensure new amenity grassland establishes	Seed/ turf amenity areas in line with the Landscape Strategy Plan. The Contractor will protect newly seeded areas where appropriate to prevent seedling destruction by pedestrians and water as required to aid establishment. Reseed/ repair as needed.	✓	-	-	-	-	-	-	✓	✓	✓	✓	✓	✓	✓	✓	-	-
		During initial establishment of new grassland (for 6-8 weeks after germination) it will be mown every 7 – 10 days to a height of 40-60mm.	✓	-	-	-	-	-	-	✓	✓	✓	✓	✓	✓	✓	✓	-	-
		Once established, grass will be mown every two weeks during the growing season to 25 – 40mm to maintain a neat appearance. From late June, relax mowing to every 4 – 8 weeks i.e. when the sward becomes untidy. Regularly remove litter and fallen leaves to maintain a neat appearance.	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓	-	✓	-	✓	-	-
New meadow grassland	 Ensure new meadow grassland establishes	Seed areas as per the Landscape Strategy Plan.	✓	-	-	-	-	-	-	✓	✓	-	-	-	-	✓	✓	-	-
		During initial establishment of new grassland, resist cutting until early August following sowing to remove annual weeds. Cut and remove arisings. Mow regularly when conditions allow through autumn until the end of March. Regularly remove litter and fallen leaves to maintain a neat appearance. Dig out any residual perennial weeds such as docks.	✓	✓	-	-	-	✓	✓	✓	-	-	-	-	✓	✓	✓	✓	✓
		The best results are usually obtained by traditional meadow management based	-	✓	✓	✓	✓	-	-	✓	-	-	-	-	✓	✓	✓	✓	✓

Ecological Feature	Objective/ Target	Prescription/ Action	Year Post Commencement					Month											
			1	2	3	4	5	J	F	M	A	M	J	J	A	S	O	N	D
		around a main summer hay cut in combination with autumn and possibly spring mowing. After flowering in July or August take a 'hay cut': cut back with a scythe, petrol strimmer or tractor mower to c 50mm. Leave the 'hay' to dry and shed seed for 1-7 days then remove from Site. Mow the re-growth through to late autumn/winter to c 50mm and again in spring if needed. 25% of grassland will be left unmown over the winter months allowing invertebrates to overwinter, to be rotated.																	
		Outside of mowing regime, maintain a long sward (over 200mm) to support reptiles.	✓	✓	✓	✓	✓	✓	✓	-	✓	✓	✓	✓	-	-	-	-	-
New native bulb planting	🦋 Ensure new native bulbs are well established	Plant in line with Landscape Strategy Plan.	✓	-	-	-	-	-	-	-	-	-	-	-	-	✓	✓	✓	-
		Bulbs to be watered in periods of extreme drought (two weeks or more without substantial rainfall).	✓	✓	✓	-	-	-	-	-	✓	✓	✓	✓	✓	✓	-	-	-
		Remove weed growth by hand and top up mulch levels as necessary. Deadhead after flowering. Prune back and remove spent stems and dead leaves of grass. Regularly remove litter to maintain a neat appearance.	✓	✓	✓	✓	✓	-	-	✓	✓	✓	✓	✓	✓	✓	✓	-	-
		Replace any dead, diseased or damaged stock on a like-for-like basis in the next appropriate season i.e. not in the summer months and not in frost conditions. Set firm any shrubs that have become	✓	✓	✓	-	-	✓	✓	✓	-	-	-	-	-	-	✓	✓	✓

Ecological Feature	Objective/ Target	Prescription/ Action	Year Post Commencement					Month											
			1	2	3	4	5	J	F	M	A	M	J	J	A	S	O	N	D
		loosened up. Top up mulch where necessary.																	
New street tree planting	 Ensure new trees are well established	Plant in line with Landscape Strategy Plan.	✓	-	-	-	-	✓	✓	✓	-	-	-	-	-	-	✓	✓	✓
		Manage in line with new native tree planting.	As above.					As above.											
New main street ornamental planting	 Ensure new ornamental planting is well established	Plant in line with Landscape Strategy Plan.	✓	-	-	-	-	-	-	-	-	-	-	-	-	✓	✓	✓	-
		Manage in line with new native bulb planting.	As above.					As above.											
New main street hedge	 Ensure new hedgerows are well established	Plant in line with Landscape Strategy Plan.	✓	-	-	-	-	✓	✓	✓	-	-	-	-	-	-	-	✓	✓
		Manage in line with new native species-rich hedgerow.	As above.					As above.											
New main street feature shrub	 Ensure new shrub is well established	Plant in line with Landscape Strategy Plan.	✓	-	-	-	-	-	-	-	-	-	-	-	-	✓	✓	✓	-
		Shrubs to be watered in periods of extreme drought (two weeks or more without substantial rainfall).	✓	✓	✓	✓	✓	-	-	-	✓	✓	✓	✓	✓	✓	-	-	-
		Prune back shrubs (no more than one third of woody growth) during October to March. Trim shrubs back from paths etc. Trim topiary shrubs to the desired shape.	✓	✓	✓	✓	✓	✓	✓	✓	-	-	-	-	-	-	✓	✓	✓
		Remove weed growth by hand and top up mulch levels as necessary. Deadhead after flowering. Prune back and remove spent stems and dead leaves of grass conditions. Set firm any shrubs that have	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓	✓

Ecological Feature	Objective/ Target	Prescription/ Action	Year Post Commencement					Month											
			1	2	3	4	5	J	F	M	A	M	J	J	A	S	O	N	D
		become loosened up. Top up mulch where necessary. Regularly remove litter to maintain a neat appearance.																	
		Replace any dead, diseased or damaged stock on a like-for-like basis in the next appropriate season i.e. not in the summer months and not in frost conditions. Set firm any shrubs that have become loosened up. Top up mulch where necessary.	✓	✓	✓	-	-	✓	✓	✓	-	-	-	-	-	-	✓	✓	✓
New housing core ornamental planting	🌱 Ensure new ornamental planting is well established	Plant in line with Landscape Strategy Plan.	✓	-	-	-	-	-	-	-	-	-	-	-	-	✓	✓	✓	-
		Manage in line with new native bulb planting.	As above.					As above.											
New housing core side hedge	🌱 Ensure new hedgerows are well established	Plant in line with Landscape Strategy Plan.	✓	-	-	-	-	✓	✓	✓	-	-	-	-	-	-	-	✓	✓
		Manage in line with new native species-rich hedgerow.	As above.					As above.											
New housing core feature shrub	🌱 Ensure new shrub is well established	Plant in line with Landscape Strategy Plan.	✓	-	-	-	-	-	-	-	-	-	-	-	-	✓	✓	✓	-
		Manage in line with new main street feature shrub.	As above.					As above.											

6 Monitoring

Monitoring is fundamental to the success of this management plan and is required to assess biodiversity changes compared to the baseline and identify potential issues. This will not only enable the effectiveness of mitigation or compensation to be identified but will also inform future revisions of the management plan to be produced.

Monitoring will be undertaken by a competent ecologist in Years 2, 5, 10, 15, 20 and 30 following completion of initial habitat works, as follows:

-  Site walkover to confirm presence and health of habitats;
-  Habitats assessed against the objectives in **Table 3** to measure progress; and
-  Report produced detailing results and any rectifying measures.

6.1 Plan Review

An adaptive management approach should be adopted whereby the results of monitoring feed back into the appropriate management of the Site and the management plan updated accordingly. The Managing Agent will be responsible for implementing any remedial actions recommended by the ecologist.

Management will be undertaken for the lifetime of the development following each revised management plan.

Include 13cm x 13cm 'cut outs' through close-boarded fences (or equivalent gaps under fences) to allow hedgehog movement throughout the site, avoiding areas leading hedgehogs out onto roads.

These holes can be created during fence construction, or purpose made products such as the Durapost Hedgehog Hole and Hedgehog Gravel Boards (or similar).

To reduce the risk of these being blocked by future residents, a small 'Hedgehog Highway Sign' should be attached.

Schwegler Hedgehog Dome (or similar) to be installed in suitable sheltered habitat within boundary features.

Vivara Pro Build-in Woodstone Bat Box (or similar) to be installed on south-western to south-eastern elevations at a minimum height of 3m above the ground. Boxes to be installed at a ratio of one box per residential unit, each symbol represents two bat boxes.

'Green&Blue' Bee Brick (or similar) to be installed on southern elevations at a minimum height of 1m above the ground.

Woodstone Build-in Swift Nest Box Deep (or similar) to be installed on northern and eastern elevations at a minimum height of 5m above the ground. Boxes to be installed at a ratio of one box per residential unit, each symbol represents three bird boxes.

Habitat Piles will be installed as per the details included within the LEMP.

Key:

- 5no. 'Green&Blue' Bee Brick (or similar)
- 4no. Habitat Piles
- Gaps at Fence Bases For Hedgehogs
- 90no. Vivara Pro Build-in Woodstone Bat Box (or similar)
- 90no. Woodstone Build-in Swi/ Nest Box Deep (or similar)
- 3no. Schwegler Hedgehog Dome (or similar)

Scale @A4: 1:1550

Imagery ©2026 CNES / Airbus, Getmapping plc, Infoterra Ltd & Bluesky, Maxar Technologies. Map data ©2026 Google

Figure 1:
Enhancements and Mitigation Plan

Project:
Land at Spitfire Road, Calne


Client:
Allison Homes

Date:
17/4/2026

Ref:
3130-LEMP-F1

Drawn:
LO

Revision:
REV4





Appendix 1 – Landscape Strategy Plan



- This drawing is the property of FPCR Environment and Design Ltd and is issued on the condition it is not reproduced, retained or disclosed to any unauthorised person, either wholly or in part without written consent of FPCR Environment and Design Ltd.
- 0 10 20 30m
1. All drawing dimensions to be checked and verified prior to construction.
 2. Drawings are design intent and for Planning purposes only.
 3. Drawings to be checked and verified by the project Architect, Engineer, M&E Engineer, Lighting consultant.
 4. Specification/Depth/location of root barriers to the project engineer's design.
 5. All services and drainage easements are to be checked and verified by the project engineers.
 6. The landscape contractors shall make themselves aware of all service locations, hedges and safety and risk assessments prior to commencing planting operations.
 7. It is the responsibility of the project engineer to design foundations to accommodate all proposed and existing tree and shrub planting, with reference made to BS5836: Part 2, 2014 (Building near Trees).
 8. All planting work to be carried out in accordance with BS428:1989 Code of Practice for General Landscaping Operations.
 9. All levels to be checked and verified by the project engineers prior to construction.
 10. All works in and around existing retained trees are subject to an Arboricultural Method Statement.
 11. All steps, structures, paving and fencing are by others unless otherwise stated.
 12. For setting out see the project engineer's drawings.
 13. Please refer to the L&SMP for specification & management prescriptions.
 14. Please see Landscape Strategy Plan on drawing 13462-FPCR-XX-XX-DR-L-0001 for an overview of the landscape proposals.

	Application Boundary
	Existing Trees & Hedgerows See Arboricultural Survey for Full Details
	Proposed Native Tree Planting Species Stem Size Root
	<i>Acer campestre</i> Clear-stem 12/14cm RB
	<i>Betula pendula</i> Clear-stem 12/14cm RB
	<i>Corylus avellana</i> Clear-stem 12/14cm RB
	<i>Fagus sylvatica</i> Clear-stem 12/14cm RB
	Native Species Rich Hedgerow Species Density Size Root %
	<i>Acer campestre</i> 5/Lm DSR 60-80cm Whip 10
	<i>Cornus sanguinea</i> 5/Lm DSR 60-80cm Whip 10
	<i>Corylus avellana</i> 5/Lm DSR 60-80cm Whip 10
	<i>Crataegus monogyna</i> 5/Lm DSR 60-80cm Whip 25
	<i>Euonymus europaeus</i> 5/Lm DSR 60-80cm Whip 5
	<i>Ilex verticillata</i> 5/Lm DSR 60-80cm Whip 5
	<i>Prunus spinosa</i> 5/Lm DSR 60-80cm Whip 25
	<i>Quercus robur</i> 5/Lm DSR 60-80cm Whip 5
	<i>Viburnum lantana</i> 5/Lm DSR 60-80cm Whip 5
	Native Species Scrub Species Density Size Root %
	<i>Acer campestre</i> 5/Lm DSR 60-80cm Whip 10
	<i>Cornus sanguinea</i> 5/Lm DSR 60-80cm Whip 10
	<i>Corylus avellana</i> 5/Lm DSR 60-80cm Whip 10
	<i>Crataegus monogyna</i> 5/Lm DSR 60-80cm Whip 20
	<i>Euonymus europaeus</i> 5/Lm DSR 60-80cm Whip 10
	<i>Ligustrum vulgare</i> 5/Lm DSR 60-80cm Whip 15
	<i>Rosa canina</i> 5/Lm DSR 60-80cm Whip 15
	Amenity Grassland Emergate EL1 - Flowering Lawn Mixture
	Meadow Grassland Gerrnall RE1 - Traditional Hay Meadow
	Native Bulb Planting Species Density %
	<i>Eranthis ciliata</i> 100/sq m 25
	<i>Galanthus nivalis</i> 100/sq m 25
	<i>Hyacinthoides non-scripta</i> 100/sq m 25
	<i>Narcissus pseudonarcissus</i> 100/sq m 25
	Equipped Play Area Detailed by Others
	Street Tree Planting Species Stem Size Root
	<i>Aesculus h</i> Clear-stem 12/14cm RB
	<i>Cornus RW</i> Clear-stem 12/14cm RB
	<i>Liriodendron f</i> Clear-stem 12/14cm RB
	<i>Malus sylvestris</i> Clear-stem 12/14cm RB
	Main Street Ornamental Planting Species Centres Size Root %
	<i>Brachyglottis Sunshine</i> 60cm 7.5L C 25
	<i>Camellia f var. repens</i> 60cm 7.5L C 25
	<i>Euonymus f 'E' G</i> 60cm 7.5L C 25
	<i>Viburnum tinus</i> 60cm 7.5L C 25
	Main Street Hedge Species Density Size Root %
	<i>Elaeagnus x ebbingei</i> Gilt Edge 2/Lm 10L C 100
	Main Street Feature Shrub Species Size Root %
	<i>Corylia avellana</i> 20L C 100
	Housing Core Ornamental Planting Species Centres Size Root %
	<i>Fatsia japonica</i> 60cm 7.5L C 25
	<i>Hebe x exoniensis</i> 60cm 7.5L C 25
	<i>Phormium tenax</i> 60cm 7.5L C 25
	<i>Prunus laurocerasus</i> 60cm 7.5L C 25
	Housing Core Side Hedge Species Density Size Root %
	<i>Prunella x fraseri</i> Red Robin 2/Lm 7.5L C 100
	Housing Core Feature Shrub Species Size Root %
	<i>Hemocallis x intermedia</i> 7 20L C 100
	Turf Contact Grade

P11	16/04/2026	Existing tree in ne corner shown as removed	JUB/JIT
P10	16/04/2026	Updated to comments re planting at plot12	JUB/JIT
P09	15/04/2026	Update with new layout and comments	JUB/JIT
P08	09/04/2026	Update Following Comment	RW/JIT
P07	02/04/2026	Tree Update	RW/JIT
rev	date	description	dm / chk

client
Allison Homes

project
**Spitfire Road
Calne**

scale
1:500 @A0

number
13642-FPCR-XX-XX-DR-L-0001

status
53

rev
P11

N

title
LANDSCAPE STRATEGY PLAN



Appendix 2 – On Plot Planting Plans Plan

13462-FPCR-XX-XX-DR-L-0003

13462-FPCR-XX-XX-DR-L-0004

13462-FPCR-XX-XX-DR-L-0005

13462-FPCR-XX-XX-DR-L-0006

P08	16/04/2026	Existing tree in ne corner shown as removed	JUB/JIT
P07	16/04/2026	Updated to comments re planting at plot12	JUB/JIT
P06	15/04/2026	Update with new layout and comments	JUB/JIT
P05	09/04/2026	Update Following Comment	RW/JIT
P04	02/04/2026	Tree Update	RW/JIT
rev	date	description	dm / chk


client
Allison Homes

project
**Spitfire Road
Calne**

title	scale
SHEET LAYOUT PLAN	1:500
number	status
13642-FPCR-XX-XX-D-L-0002	53
	rev
	P08



For General Arrangement Plan, please refer to 13462-FPCR-XX-XX-DR-L-0001-0002



drwn/chkd	scale	date
JUB / JJT	1:250	16.04.26
number		status rev
13642-FPCR-XX-XX-DR-L-0004		S3 P08

0510101520

0510101520

0510101520

0510101520

0510101520

client
Allison Homes

project
**Spitfire Road
Calne**

title
ON PLOT PLANTING PLAN (SHEET 2 OF 4)

Drawing is based on (layout 0841-X- Layout.DWG) produced by Focus Design Partnership LTD

For on-plot planting details, plant schedules and seeding mixes, please refer to
13462-FPCR-XX-XX-DR-L-0003-0007

For General Arrangement Plan, please refer to 13462-FPCR-XX-XX-DR-L-0001-0002

Application Boundary

Existing Trees & Hedgerows

See Arboricultural Survey for Full Details

Proposed Native Tree Planting

Species	Stem	Size	Root
<i>Green Infrastructure</i>			
<i>Acer campestre</i>	Clear-stem	12/14cm	RB
<i>Betula pendula</i>	Clear-stem	12/14cm	RB
<i>Carpinus betulus</i>	Clear-stem	12/14cm	RB
<i>Fagus sylvatica</i>	Clear-stem	12/14cm	RB

Native Species Rich Hedgerow

Species	Density	Size	Root	%
<i>Acer campestre</i>	5/Lm DSR	60-80cm Whip	10	
<i>Cornus sanguinea</i>	5/Lm DSR	60-80cm Whip	10	
<i>Corylus avellana</i>	5/Lm DSR	60-80cm Whip	10	
<i>Crataegus monogyna</i>	5/Lm DSR	60-80cm Whip	25	
<i>Euonymus europaeus</i>	5/Lm DSR	60-80cm Whip	5	
<i>Ilex aquifolium</i>	5/Lm DSR	60-80cm Whip	5	
<i>Prunus spinosa</i>	5/Lm DSR	60-80cm Whip	25	
<i>Quercus robur</i>	5/Lm DSR	60-80cm Whip	5	
<i>Viburnum lantana</i>	5/Lm DSR	60-80cm Whip	5	

Native Species Scrub

Species	Density	Size	Root	%
<i>Acer campestre</i>	5/Lm DSR	60-80cm Whip	10	
<i>Cornus sanguinea</i>	5/Lm DSR	60-80cm Whip	20	
<i>Corylus avellana</i>	5/Lm DSR	60-80cm Whip	10	
<i>Crataegus monogyna</i>	5/Lm DSR	60-80cm Whip	10	
<i>Euonymus europaeus</i>	5/Lm DSR	60-80cm Whip	10	
<i>Ligustrum vulgare</i>	5/Lm DSR	60-80cm Whip	15	
<i>Rosa canina</i>	5/Lm DSR	60-80cm Whip	15	

Amenity Grassland

Emorsgate EL1 - Flowering Lawn Mixture

Meadow Grassland

Germinal RE1 - Traditional Hay Meadow

Native Bulb Planting

Species	Density	%
<i>Eranthis ciliata</i>	10P/sq m	25
<i>Galanthus nivalis</i>	10P/sq m	25
<i>Hyacinthoides non-scripta</i>	10P/sq m	25
<i>Narcissus pseudonarcissus</i>	10P/sq m	25

Equipped Play Area

Detailed by Others

Street Tree Planting

Species	Stem	Size	Root
<i>On-Plot Landscape</i>			
<i>Amelanchier l</i>	Clear-stem	12/14cm	RB
<i>Cornus 'EWW'</i>	Clear-stem	12/14cm	RB
<i>Liriodendron t 'F'</i>	Clear-stem	12/14cm	RB
<i>Malus sylvestris</i>	Clear-stem	12/14cm	RB

Main Street Ornamental Planting

Species	Centres	Size	Root	%
<i>On-Plot Link Road</i>				
<i>Brachyglottis 'Sunshine'</i>	60cm	7.5L	C	25
<i>Ceanothus t var. repens</i>	60cm	7.5L	C	25
<i>Euonymus f 'E'n 'G'</i>	60cm	7.5L	C	25
<i>Viburnum tinus</i>	60cm	7.5L	C	25

Main Street Hedge

Species	Density	Size	Root	%
<i>On-Plot Link Road</i>				
<i>Eleagnus x ebbingei</i>	2/Lm	10L	C	100

Main Street Feature Shrub

Species	Size	Root	%
<i>On-Plot Green Edge</i>			
<i>Garrya elliptica</i>	20L	C	100

Housing Core Ornamental Planting

Species	Centres	Size	Root	%
<i>On-Plot Side Street</i>				
<i>Fatsia japonica</i>	60cm	7.5L	C	25
<i>Hebe rakaiensis</i>	60cm	7.5L	C	25
<i>Phormium 'Jester'</i>	60cm	7.5L	C	25
<i>Prunus laurocerasus 'OL'</i>	60cm	7.5L	C	25

Housing Core Side Hedge

Species	Density	Size	Root	%
<i>On-Plot Side Street</i>				
<i>Photinia x fraseri</i>	2/Lm	7.5L	C	100

Housing Core Feature Shrub

Species	Size	Root	%
<i>On-Plot Green Edge</i>			
<i>Hamamelis x intermedia 'J'</i>	20L	C	100

Turf

Contact Grade



This drawing is the property of FPCR Environment and Design Ltd and is issued on the condition it is not reproduced, retained or disclosed to any unauthorised person, either wholly or in part without written consent of FPCR Environment and Design Ltd.

Ordnance Survey Mastermap - Crown Copyright. All rights reserved. License Number: 100019980 (Centremapslive.com).

Application Boundary

Existing Trees & Hedgerows

See Arboricultural Survey for Full Details

Proposed Native Tree Planting

Species	Stem	Size	Root
Green Infrastructure			
Acer campestre	Clear-stem	12/14cm	RB
Betula pendula	Clear-stem	12/14cm	RB
Carpinus betulus	Clear-stem	12/14cm	RB
Fagus sylvatica	Clear-stem	12/14cm	RB

Native Species Rich Hedgerow

Species	Density	Size	Root	%
Acer campestre	5/Lm DSR	60-80cm Whip	10	
Cornus sanguinea	5/Lm DSR	60-80cm Whip	10	
Corylus avellana	5/Lm DSR	60-80cm Whip	10	
Crataegus monogyna	5/Lm DSR	60-80cm Whip	25	
Euonymus europaeus	5/Lm DSR	60-80cm Whip	5	
Ilex aquifolium	5/Lm DSR	60-80cm Whip	5	
Prunus spinosa	5/Lm DSR	60-80cm Whip	25	
Quercus robur	5/Lm DSR	60-80cm Whip	5	
Viburnum lantana	5/Lm DSR	60-80cm Whip	5	

Native Species Scrub

Species	Density	Size	Root	%
Acer campestre	5/Lm DSR	60-80cm Whip	10	
Cornus sanguinea	5/Lm DSR	60-80cm Whip	20	
Corylus avellana	5/Lm DSR	60-80cm Whip	10	
Crataegus monogyna	5/Lm DSR	60-80cm Whip	20	
Euonymus europaeus	5/Lm DSR	60-80cm Whip	10	
Ligustrum vulgare	5/Lm DSR	60-80cm Whip	15	
Rosa canina	5/Lm DSR	60-80cm Whip	15	

Amenity Grassland

Emorsgate EL1 - Flowering Lawn Mixture

Meadow Grassland

Germinal RE1 - Traditional Hay Meadow

Native Bulb Planting

Species	Density	%
Eranthis ciliata	10P/sq m	25
Galanthus nivalis	10P/sq m	25
Hyacinthoides non-scripta	10P/sq m	25
Narcissus pseudonarcissus	10P/sq m	25

Equipped Play Area

Detailed by Others

Street Tree Planting

Species	Stem	Size	Root
On-Plot Landscape			
Amelanchier l	Clear-stem	12/14cm	RB
Cornus 'EWW'	Clear-stem	12/14cm	RB
Liriodendron t 'F	Clear-stem	12/14cm	RB
Malus sylvestris	Clear-stem	12/14cm	RB

Main Street Ornamental Planting

Species	Centres	Size	Root	%
On-Plot Link Road				
Brachyglottis 'Sunshine'	60cm	7.5L	C	25
Ceanothus t var. repens	60cm	7.5L	C	25
Euonymus f 'E'n 'G	60cm	7.5L	C	25
Viburnum tinus	60cm	7.5L	C	25

Main Street Hedge

Species	Density	Size	Root	%
On-Plot Link Road				
Eleagnus x ebbingei	2/Lm	10L	C	100

Main Street Feature Shrub

Species	Size	Root	%
On-Plot Green Edge			
Garrya elliptica	20L	C	100

Housing Core Ornamental Planting

Species	Centres	Size	Root	%
On-Plot Side Street				
Fatsia japonica	60cm	7.5L	C	25
Hebe rakaiensis	60cm	7.5L	C	25
Phormium 'Jester'	60cm	7.5L	C	25
Prunus laurocerasus 'OL'	60cm	7.5L	C	25

Housing Core Side Hedge

Species	Density	Size	Root	%
On-Plot Side Street				
Photinia x fraseri 'Red Robin'	2/Lm	7.5L	C	100

Housing Core Feature Shrub

Species	Size	Root	%
On-Plot Green Edge			
Hamamelis x intermedia 'J'	20L	C	100

Turf


Contact Grade

Drawing is based on (layout 0841-X- Layout.DWG) produced by Focus Design Partnership LTD

For on-plot planting details, plant schedules and seeding mixes, please refer to 13462-FPCR-XX-XX-DR-L-0003-0007

For General Arrangement Plan, please refer to 13462-FPCR-XX-XX-DR-L-0001-0002

This drawing is the property of FPCR Environment and Design Ltd and is issued on the condition it is not reproduced, retained or disclosed to any unauthorised person, either wholly or in part without written consent of FPCR Environment and Design Ltd.



drawn/chkd	scale	date
JUB / JIT	1:250	16.04.26
number	status	rev
13642-FPCR-XX-XX-DR-L-0005	S3	P08

0

5

10

15m

client
Allison Homes

project
Spitfire Road
Calne

title
ON PLOT PLANTING PLAN (SHEET 3 OF 4)

FPCR | environment & design

L:\13600\13642\LANDS\Drawings\13642-XX-XX-DR-L-0001\Landscape Strategy Plan.rvt
t: 01509 672772 e: mail@fpcr.co.uk w: www.fpcr.co.uk



This drawing is the property of FPCR Environment and Design Ltd and is issued on the condition it is not reproduced, retained or disclosed to any unauthorised person, either wholly or in part without written consent of FPCR Environment and Design Ltd.

Ordnance Survey Mastermap - Crown Copyright. All rights reserved. License Number: 100019980 (Centremapslive.com).

Application Boundary

Existing Trees & Hedgerows

See Arboricultural Survey for Full Details

Proposed Native Tree Planting

Species	Stem	Size	Root
Green Infrastructure			
<i>Acer campestre</i>	Clear-stem	12/14cm	RB
<i>Betula pendula</i>	Clear-stem	12/14cm	RB
<i>Corylus avellana</i>	Clear-stem	12/14cm	RB
<i>Fagus sylvatica</i>	Clear-stem	12/14cm	RB

Native Species Rich Hedgerow

Species	Density	Size	Root	%
<i>Acer campestre</i>	5/Lm DSR	60-80cm Whip	10	
<i>Cornus sanguinea</i>	5/Lm DSR	60-80cm Whip	10	
<i>Corylus avellana</i>	5/Lm DSR	60-80cm Whip	10	
<i>Crataegus monogyna</i>	5/Lm DSR	60-80cm Whip	25	
<i>Euonymus europaeus</i>	5/Lm DSR	60-80cm Whip	5	
<i>Ilex aquifolium</i>	5/Lm DSR	60-80cm Whip	5	
<i>Prunus spinosa</i>	5/Lm DSR	60-80cm Whip	25	
<i>Quercus robur</i>	5/Lm DSR	60-80cm Whip	5	
<i>Viburnum lantana</i>	5/Lm DSR	60-80cm Whip	5	

Native Species Scrub

Species	Density	Size	Root	%
<i>Acer campestre</i>	5/Lm DSR	60-80cm Whip	10	
<i>Cornus sanguinea</i>	5/Lm DSR	60-80cm Whip	20	
<i>Corylus avellana</i>	5/Lm DSR	60-80cm Whip	10	
<i>Crataegus monogyna</i>	5/Lm DSR	60-80cm Whip	20	
<i>Euonymus europaeus</i>	5/Lm DSR	60-80cm Whip	10	
<i>Ligustrum vulgare</i>	5/Lm DSR	60-80cm Whip	15	
<i>Rosa canina</i>	5/Lm DSR	60-80cm Whip	15	

Amenity Grassland

Emorsgate EL1 - Flowering Lawn Mixture

Meadow Grassland

Germinal RE1 - Traditional Hay Meadow

Native Bulb Planting

Species	Density	%
<i>Eranthis ciliata</i>	10P/sq m	25
<i>Galanthus nivalis</i>	10P/sq m	25
<i>Hyacinthoides non-scripta</i>	10P/sq m	25
<i>Narcissus pseudonarcissus</i>	10P/sq m	25

Equipped Play Area

Detailed by Others

Street Tree Planting

Species	Stem	Size	Root
On-Plot Landscape			
<i>Amelanchier l</i>	Clear-stem	12/14cm	RB
<i>Cornus 'EWW'</i>	Clear-stem	12/14cm	RB
<i>Liriodendron t 'F'</i>	Clear-stem	12/14cm	RB
<i>Malus sylvestris</i>	Clear-stem	12/14cm	RB

Main Street Ornamental Planting

Species	Centres	Size	Root	%
On-Plot Link Road				
<i>Brachyglottis 'Sunshine'</i>	60cm	7.5L	C	25
<i>Ceanothus t var. repens</i>	60cm	7.5L	C	25
<i>Euonymus f 'E'n 'G'</i>	60cm	7.5L	C	25
<i>Viburnum tinus</i>	60cm	7.5L	C	25

Main Street Hedge

Species	Density	Size	Root	%
On-Plot Link Road				
<i>Eleagnus x ebbingei</i> 'Gilt Edge'	2/Lm	10L	C	100

Main Street Feature Shrub

Species	Size	Root	%
On-Plot Green Edge			
<i>Garrya elliptica</i>	20L	C	100

Housing Core Ornamental Planting

Species	Centres	Size	Root	%
On-Plot Side Street				
<i>Fatsia japonica</i>	60cm	7.5L	C	25
<i>Hebe rakaiensis</i>	60cm	7.5L	C	25
<i>Phormium 'Jester'</i>	60cm	7.5L	C	25
<i>Prunus laurocerasus</i> 'OL'	60cm	7.5L	C	25

Housing Core Side Hedge

Species	Density	Size	Root	%
On-Plot Side Street				
<i>Photinia x fraseri</i> 'Red Robin'	2/Lm	7.5L	C	100

Housing Core Feature Shrub

Species	Size	Root	%
On-Plot Green Edge			
<i>Hamamelis x intermedia 'J'</i>	20L	C	100

Turf

Contact Grade

This drawing is the property of FPCR Environment and Design Ltd and is issued on the condition it is not reproduced, retained or disclosed to any unauthorised person, either wholly or in part without written consent of FPCR Environment and Design Ltd.

L:\13600\13642\LANDS\Drawings\13642-XX-XX-DR-L-0001Landscape Strategy Plan.rvt
t: 01509 672772 e: mail@fpcr.co.uk w: www.fpcr.co.uk

N

drawn/checked
JUB/ JJT

scale
1:250

date
16.04.26

number
13642-FPCR-XX-XX-DR-L-0006

status
S3

rev
P08

0

5

10

15m

client
Allison Homes
project
Spitfire Road Calne

title
ON PLOT PLANTING PLAN (SHEET 4 OF 4)

Drawing is based on (layout 0841-X- Layout.DWG) produced by Focus Design Partnership LTD
For on-plot planting details, plant schedules and seeding mixes, please refer to 13462-FPCR-XX-XX-DR-L-0003-0007
For General Arrangement Plan, please refer to 13462-FPCR-XX-XX-DR-L-0001-0002

FPCR | environment & design

Planting Schedule - On Plot

INDIVIDUAL TREES

Qty	Latin Name	Abbreviation	Height	Form	Root Condition	Minimum Clear Stem	Girth
19	Acer campestre	Acer camp.	350-400cm	Heavy Standard	RB	Min. 200cm	12-14cm
15	Amelanchier lamarckii	Amel. l	350-400cm	Heavy Standard	RB	Min 200cm	12-14cm
20	Betula pendula	Betu. pen.	350-400cm	Heavy Standard	RB	Min 200cm	12-14cm
12	Carpinus betulus	Carp. bet.	350-400cm	Heavy Standard	RB	Min 200cm	12-14cm
9	Cornus 'Eddie's White Wonder'	Cornus EWW	400-450cm	Extra Heavy Standard	RB	Min 200cm	14-16cm
1	Fagus sylvatica	Fagus syl.	500-550cm	Heavy Standard	RB	Min 200cm	12-14cm
13	Garrya elliptica	Garrya e	125-150cm	20L	C	N/A	N/A
8	Hamamelis x intermedia 'Jelena'	Ham x i 'J'	125-150cm	20L	C	N/A	N/A
14	Liriodendron tulipifera'Fastigiata'	Lirioden. tul. F	350-400cm	Heavy Standard	RB	Min 200cm	12-14cm
9	Malus sylvestris	Malus syl	400-450cm	Extra Heavy Standard	RB	Min 200cm	14-16cm

HEDGEROWS (planted in a single row, 5 plants lin/m)

Qty	Latin Name	Abbreviation	Height	Form	Root Condition
54	Acer campestre	Acer c	60-80cm	Whip	BR
26	Cornus sanguinea	Cornus s	60-80cm	Whip	BR
54	Corylus avellana	Corylus a	60-80cm	Whip	BR
131	Crataegus monogyna	Cratae m	60-80cm	Whip	BR
26	Euonymus europaeus	Euony e	60-80cm	Whip	BR
26	Ilex aquifolium	Ilex a	60-80cm	Whip	BR
26	Ligustrum vulgare	Ligus v	60-80cm	Whip	BR
131	Prunus spinosa	Prun s	60-80cm	Whip	BR
26	Quercus robur	Quercus r	80-100cm	Whip	BR
26	Viburnum lantana	Vib l	80-100cm	Whip	BR

BULB PLANTING

Qty	Latin Name	Abbreviation	Rate/Plants m²
898	Eranthis cilicica	Eranthis cil.	10
898	Galanthus nivalis	Galanthus niv.	10
898	Hyacinthoides non-scripta	Hyacinthoides ns.	10
898	Narcissus pseudonarcissus	Narcissus pseu.	10

ON PLOT PLANTING

Qty	Latin Name	Abbreviation	Rate/Plants m²	Root Condition
155	Viburnum tinus	Vib t	2	C
235	Euonymus fortunei 'Emerald n Gold'	Euony f 'EG'	3	C
235	Brachyglottis 'Sunshine'	Brachy 'S'	3	C
155	Ceanothus thyrsiflorus 'Repens'	Ceano t 'R'	2	C
342	Fatsia japonica	Fatsia j	3	C
342	Phormium 'Jester'	Phor J	3	C
342	Prunus laurocerasus 'Otto Luyken'	Prun l 'OL'	3	C
342	Hebe rakaiensis	Hebe r	3	C

This drawing is the property of FPCR Environment and Design Ltd and is issued on the condition it is not reproduced, retained or disclosed to any unauthorised person, either wholly or in part without written consent of FPCR Environment and Design Ltd.

Ordnance Survey Mastermap - Crown Copyright. All rights reserved. License Number: 100019980 (Centremapslive.com).

PLANTING NOTES Public Open Space

- Drawing is based on (layout 0841-X- Layout.DWG) produced by Focus Design Partnership LTD
- For on-plot planting details, plant schedules and seeding mixes, please refer to 13462-FPCR-XX-XX-DR-L-0003-0007
- For General Arrangement Plan, please refer to 13462-FPCR-XX-XX-DR-L-0001-0002

GENERAL

- All planting and seeding to be undertaken within the first planting season following the completion of construction of the development.
- The landscape contractor will make themselves aware of the service locations prior to commencing operations and no tree will be planted closer than 4.5m to any adoptable cable and 3m to any private cable.
- All plants to be of British Provenance and in accordance with the National Plant Specification.

PLANTING

- All Standard trees to be secured with a single stake and adjustable tie with spacer. All Heavy and Extra Heavy Standard trees to be double staked using wooden crossbar and adjustable tie with spacer. Stake to be positioned in the windward side of the tree. Semi-mature trees and Heavy Standard and Extra Heavy Standard trees in highly visible locations to be secured using underground anchoring system.
- All trees to be protected against rabbit/ deer damage using appropriate spiral guards.
- All native woodland/ native shrub planting to be protected with appropriate biodegradable shrub shelters.
- Native hedgerow planting to be protected using appropriate biodegradable spiral guards/ shrub shelters and canes.
- Native woodland/ native shrub planting to be planted in groups of 5-11 species groups randomly distributed and planted at density specified in the schedule.
- Native hedgerows to be planted in double staggered row at 5 plants per linear metre Drawn at 1.25m width /and a triple staggered row at 7 plants per linear metre if drawn at 2m width. All hedgerows to be secured with post and wire fence until established.
- Ornamental planting to be set out in species groups of 3-5 plants, with taller species towards the centre/ back of the bed and lower plants closer to the edges. Beds to be mulched with 50mm layer of well-composted bark mulch.
- Meadow seed mixes to be sown onto prepared subsoils to reduce fertility and enable successful establishment.

MAINTENANCE

- Regular maintenance visits shall be undertaken following planting to maintain all areas in a weed and litter free condition and to ensure the healthy establishment of all planting stock.
- For the first 12 months following practical completion the maintenance is the responsibility of the landscape contractor who undertook the implementation. Any failures to be replaced during the next planting season.
- During the maintenance period all areas of planting shall be watered dependant on prevailing weather conditions, to ensure healthy establishment of all stock.
- Areas of amenity grass to be regularly cut throughout the growing season to maintain a neat and tidy appearance, the arisings removed. In drought or wet conditions, mowing will be suspended.
- Wildflower areas to be trimmed as per seed provider guidance. Arisings should be removed and composted.
- In addition to mowing and watering, all planting shall be maintained/ inspected a minimum of 4 times annually to aid establishment and appearance.
- Maintenance operations shall include: weed removal by spot treatment with contact herbicide or hand weeding; pruning of dead wood, epicormic growth or suckers from stems, with all prunings removed from site; stakes and ties will be check and adjusted accordingly to prevent growth restriction; pruning of shrubs will be kept to minimum at appropriate time for each species and in line with good horticultural practice, with plants maintaining a neat and tidy appearance; footpaths will be kept obstruction and waste free.
- On completion of the 12-month maintenance period, a site inspection shall be undertaken by the landscape contractor, landscape architect and a representative of the appointed management company as necessary, to ascertain that all areas of landscaping associated with the development are om a satisfactory condition for handover to the management company. Any necessary works shall then be carried out to the satisfaction of the landscape architect/ client to enable the works to be handed over to the appointed management company or Local Authority as appropriate.

ONGOING MAINTENANCE AND MANAGEMENT

- The appointed management company should continue to undertake all necessary operations in line with the above notes, to ensure that the grounds are maintained in a neat and tidy appearance in line with good horticultural practice and to maintain the ecological habitats in good condition.
- Long term management of all communal areas of soft landscape shall be based on the above notes, however these notes are not definitive, and any works required to maintain the areas in healthy condition should be carried out on a regular basis throughout subsequent years.

On Plot

GENERAL

- All planting and seeding to be undertaken within the first planting season following the completion of construction of the development.
- The landscape contractor will make themselves aware of the service locations prior to commencing operations and no tree will be planted closer than 4.5m to any adoptable cable and 3m to any private cable.
- All plants to be of British Provenance and in accordance with the National Plant Specification.

PLANTING

- All Standard trees to be secured with a single stake and adjustable tie with spacer. All Heavy and Extra Heavy Standard trees to be double staked using wooden crossbar and adjustable tie with spacer. Stakes to be positioned in the windward side of the tree. Semi-mature trees and Heavy Standard and Extra Heavy Standard trees in highly visible locations to be secured using underground anchoring system.
- All trees to be protected against rabbit/ deer damage using appropriate spiral guards.
- Ornamental planting to be set out in species groups of 3-5 plants, with taller species towards the centre/ back of the bed and lower plants closer to the edges. Beds to be mulched with 50mm layer of well-composted bark mulch.
- All single species hedgerows to be planted in a single row at 3/4/5 plants per linear metre (delete unnecessary). Hedgerows to be supported by post and wire fence until established.
- Non-self-supporting climbers proposed along boundary walls to be supported by tensioned wires attached to vine eyes secured to walls. Self-supporting climbers to be planted at a slight angle towards the wall, with supporting canes leaning against the wall.
- All front garden grassed areas to be turfed.

Website: www.ge-consulting.co.uk
Phone: 01647 253652
Email: info@ge-consulting.co.uk

GE Consulting is a trading name for
GE Consulting Services (UK) Ltd
registered number 08435536

Registered office: Unit 11A, Gidleys
Meadow Business Park, Christow,
Devon, EX6 7QB.
VAT Number 160595992

Ecology
Arboriculture
Land Management

