


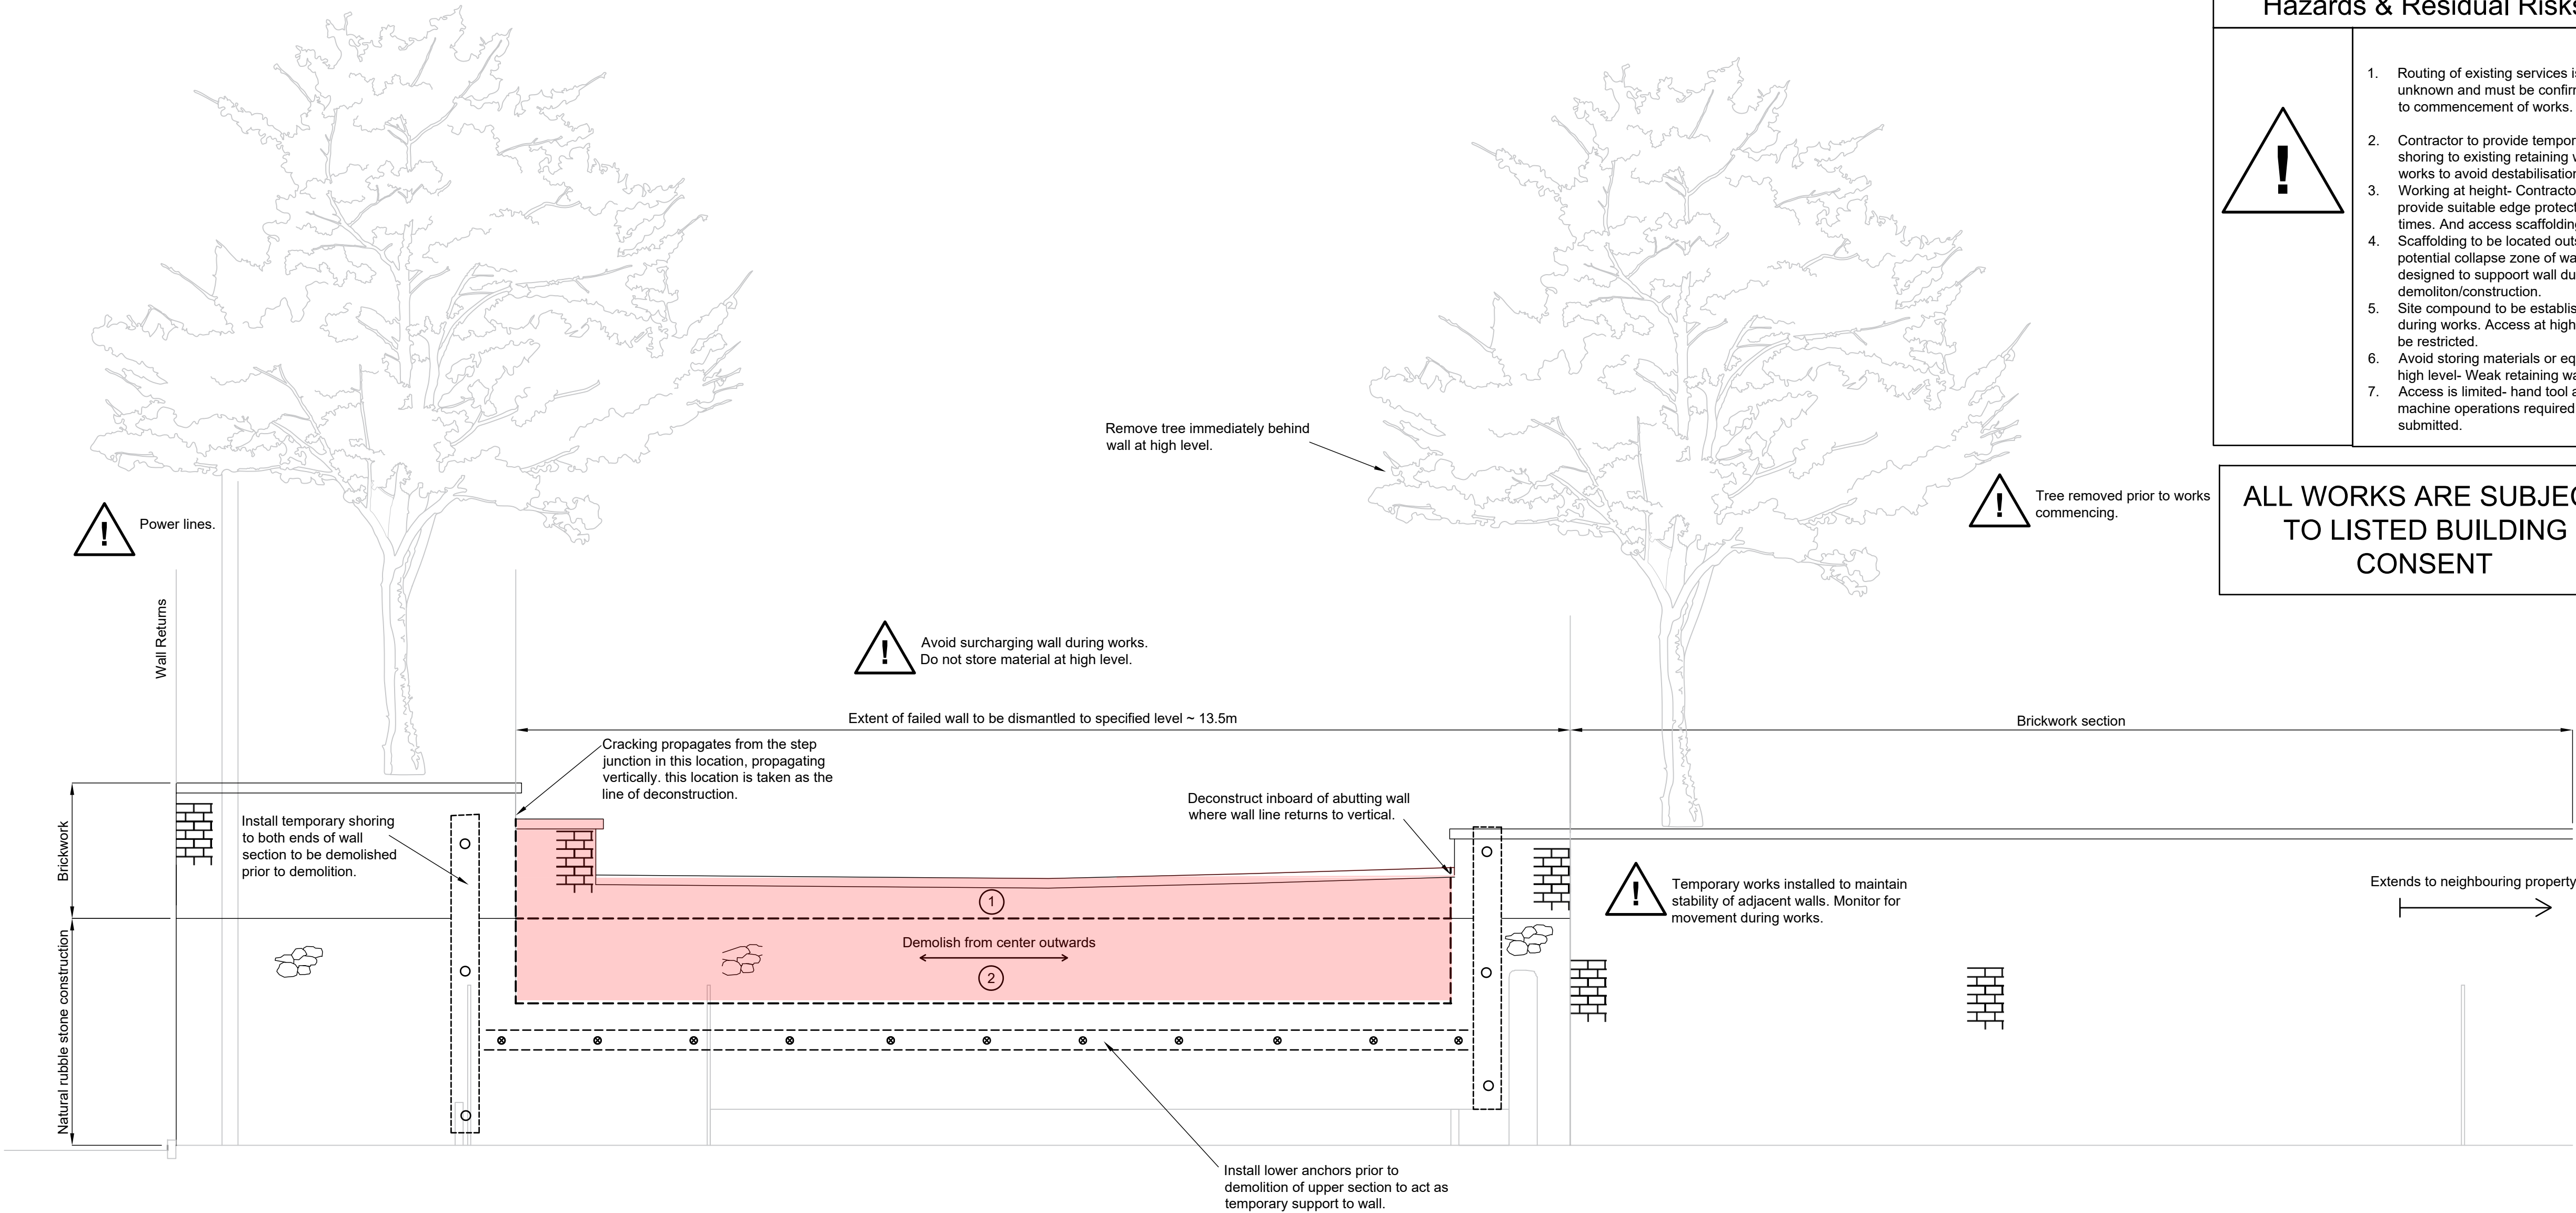

Existing Wall Elevation
1:50

DEMOLITION SEQUENCE:
1. Install temporary works either side of wall. Carefully demolish free standing brickwork section of the wall indicated as Bay 1. Retaining all bricks for re-use when re-building wall.
2. Excavate material behind wall to depth indicated on section A-A, banking back soil to a 1:2 slope or shallower if retained material is unstable. Excavation to take place by long reach excavator positioned away from wall to avoid surcharge or by hand digging. Exclude lower area of retaining wall during excavation.
3. Install lower level Heli-Pile anchors through existing wall one levels have been reduced. If upper section of wall is unstable install temporary works in line with contractors details. If in doubt consult engineer.
4. Demolish upper section of retaining wall indicated as bay 2, taking down to a level horizontal bed joint. Retain all stone for re-construction.
Note: deviation from the proposal to be agreed by MESH engineering. Demolition to take place one all formal agreements are in place (Party Wall Act, Listed Building Consent). Temporary works to be installed prior to undertaking any works.

CDM 2015 Hazards & Residual Risks	
	- Routing of existing services is unknown and must be confirmed prior to commencement of works. - Contractor to provide temporary shoring to existing retaining wall during works to avoid destabilisation. - Working at height- Contractor to provide suitable edge protection at all times. And access scaffolding. - Scaffolding to be located outside the potential collapse zone of wall or designed to support wall during demolition/construction. - Site compound to be established during works. Access at high level to be restricted. - Avoid storing materials or equipment at high level- Weak retaining wall. - Access is limited- hand tool and machine operations required. RAMS submitted.
ALL WORKS ARE SUBJECT TO LISTED BUILDING CONSENT	

Notes
1. All works are to comply with current Building Regulations and relevant codes of practice
2. This drawing is to be read in conjunction with all relevant Architect's drawings and Engineer's detailed specifications.
3. This drawing is not to be scaled
4. The contractor shall be responsible for the design, fabrication, erection and removal of all temporary works and shall provide all temporary bracings and back-propping necessary to maintain structural stability during construction
5. Care should be taken to ensure that existing structures e.g. foundation, road, boundary walls and buildings are not undermined. Temporary works to contractors details and method statement.
6. For full set of notes refer to Structural Specification
7. Mesh Engineering is not appointed as the Principal Designer under CDM Regulations and these duties are assumed to be carried out by the Principal Contractor

CDM Residual Risks & Hazards
See project specific Mesh Engineering Ltd Specification document for CDM residual risks and hazards.
Project specific hazards are indicated on this drawing by an exclamation mark within a triangle adjacent box notes.

General notes :-
See notes above.

Preliminary Issue	P1	SL	06.07.26
Revisions	Ref	Initial	Date

meshengineers.co.uk | Measured thinking when it matters most

www.meshengineering.co.uk

Client
IVO STOURTON

Description
Proposed Demolition Sequence

Project
Bratton House Bratton Wiltshire, BA13 4RN

Drawing status PRELIMINARY		Reinf. Schedule No.s NA	
Scale at A1 As shown	Scale at A3 1/2 Shown	Drawn by SL	Checked by MJ
Date JULY 26	Project number 26-082	Drawing No. X03	Rev. P1
