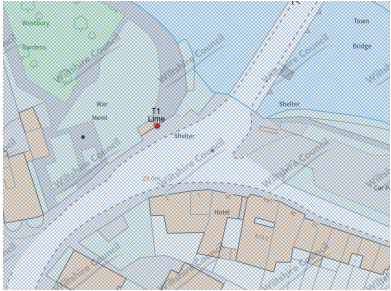


Job Sheet & SSRA

Job	TREE WORKS REQUEST FORM - Bridge Street, Bradford on Avon, bus stop opposite ravello - Lewis Neate
Date / Time of inspection	12/11/2025 09:54
Manager	Craig Lane
Enquiry Description	Please inspect tree reported by passenger transport as to be interfering with bus drivers. Told by tree officer that the tree need to be pruned so can we inspect with a view to do this.
Client	Wiltshire Council
Contact	
Site Address	Town Bridge, Bradford-on-Avon BA15 1DE, UK
Contact number	
Inspected by	Jac Morgan
W3W And Or (Ash Die Back Ref): ///norms.restrict.delighted	
Is a Site Safety Induction required prior to works starting?: No	

Job description

Work				
T No	Species	Work required	Photos	Tree Location
T1	Lime (Tillia cordata) Within HB Priority 3	Physiologically good Structurally good Small mature, historically pollarded lime tree with canopy over bus shelter, footway and encroaching on bus stop. Recommend re-pollard to previous pruning points. Road speed 20mph Traffic high Phone signal good	   	///norms. restrict.d elighted

Work				
T No	Species	Work required	Photos	Tree Location
				

SITE MAP

Site Considerations:

Disposal of Arisings	All arisings removed from site
----------------------	---------------------------------------

Replant
Required?:
No

Replant Species Required:

Planning/Environmental Constrains

TPO/Conservation Area	Yes
Permission granted?	N/A
Environmental Designation	SAC (Special Area of Conservation)

Protected Wildlife Assessment

Protected Species Present Or Suspected?	No
---	-----------

Identified Species:	
Is Ecological Supervision Required To Facilitate Works	

COSHH

Hazardous Plants Identified?:
No

What species have been identified?:

Is it reasonably foreseeable that Asbestos could be found on site:

no

Work at height assessment

(Refer to ICOP)

Can work be safely carried out from ground?	No
Can a MEWP be used to complete the task?	Yes
How is the work going to be completed?: Climbed with competent and qualified climber and areal rescuer	

Overhead and underground services

Are overhead services present? (In or near the work site)	No
---	-----------

Photos of the overhead services

Can the work be carried out safely?	
If yes, what control measures are required? (i.e Physical barriers & Blue electrical cones to create exclusion zone)	

If no, contact network operator for shrouding or temporary power isolation to be arranged?

Are Underground Services present? (Within or near the work site)	Unknown
Can the work be carried out safely?	Yes
Details: If yes, ensure cable avoidance tools are used to help identify the location of under ground services. Request service plans and where possible avoid breaking ground. Consider BT, Fibre, foul, electricity, water, gas & manhole covers.	

If no, contact service provider.

Biosecurity Risk Assessment

Is a P&D present or suspected on or adjacent to the site?	No
Details: If yes, how does this affect your work and what biosecurity control measures are required? Refer to FC guidance. Is a Statutory Plant Health Notice in place? Always take routine biosecurity control measures.	

Additional Equipment Required -

in addition to standard issue

Is there any additional equipment required?	No
Additonal Equipment	
Attachments or Other:	

Welfare

Nearest Welfare Facility. Local services/Site facilities (Enter WTW of welfare): Public WC at w3w ///wins.lyricism.haunt
--

Emergency contingencies / planning

Nearest A&E (inc. postcode)	Royal United Hospital, Bath (BA1 3NG)
Site Access: Consider 4x4/helicopter/road access	

Site-Specific Risk Assessment

List here the specific hazards/considerations of the site that pose a risk which needs to be controlled/ managed and then say how this will be achieved? (example below)

Hazard: *EXAMPLE passing pedestrians entering worksite being injured by falling branches / equipment etc.*

Controls: *EXAMPLE Worksite signed, coned & barriered to form exclusion zone. Ground staff to act as banks-man / lookouts.*

Hazards/Controls	
Hazard	Controls
Noise/using machinery. GRA Ref 4.3c	Ensure full PPE is being worn by all operatives. Be aware of close proximity to pedestrians/third parties/site staff etc. Only qualified staff to use machinery., Maintain high levels of communication between team., Erect sufficient Chapter 8, adhering to regulations., Secure the worksite where possible to prevent access by third parties., Complete Vehicle and Machinery checks (PUWER), Operatives Competent for task with appropriate training and experience, Rescue Plan in place

Hazards/Controls	
Hazard	Controls
Falling timber/rigging operations. GRA Ref: 5.1-5.6	Ensure full PPE is being worn by all operatives. Be aware of close proximity to pedestrians/third parties/site staff etc. Only qualified staff to use machinery., Maintain high levels of communication between team., Erect sufficient Chapter 8, adhering to regulations., Secure the worksite where possible to prevent access by third parties., Operatives Competent for task with appropriate training and experience, Rescue Plan in place
Roadside Operations. GRA Ref: GRA Ref 2.5	Ensure full PPE is being worn by all operatives. Be aware of close proximity to pedestrians/third parties/site staff etc. Only qualified staff to use machinery., Maintain high levels of communication between team., Erect sufficient Chapter 8, adhering to regulations., Secure the worksite where possible to prevent access by third parties., Operatives Competent for task with appropriate training and experience, Rescue Plan in place
Working at Height. GRA Ref: 5.1-6.8	Ensure full PPE is being worn by all operatives. Be aware of close proximity to pedestrians/third parties/site staff etc. Only qualified staff to use machinery., Maintain high levels of communication between team., Erect sufficient Chapter 8, adhering to regulations., Secure the worksite where possible to prevent access by third parties., Complete Vehicle and Machinery checks (PUWER), Operatives Competent for task with appropriate training and experience, Prestart LOLER & PUWER checks complete, Work Restraint Harness and Lanyard worn and fitted correctly, Rescue Plan in place, Work Positioning Harness worn with personal fall protection system consisting of 2 independent anchor points and systems
Pedestrians/Public access/Footpaths. GRA Ref: 2.6/4.3c/2.5	Ensure full PPE is being worn by all operatives. Be aware of close proximity to pedestrians/third parties/site staff etc. Only qualified staff to use machinery., Maintain high levels of communication between team., Erect sufficient Chapter 8, adhering to regulations., Secure the worksite where possible to prevent access by third parties., Operatives Competent for task with appropriate training and experience, Rescue Plan in place

Select Appropriate Generic Risk Assessments	1.1 Staff & Other Personnel., 2.1a Works Vehicles., 2.1b Theft of work Equipment, 2.1c Use of Hand Tools, 2.1d Access Equipment/Ladders/Temporary Platforms, 2.1e Powered Tools and Machinery, 2.1f Manual Handling., 2.1g Extreme Weather., 2.1j Sting & Bites., 2.1o Dog and Cat Faeces Toxicara., 2.1q Zoonotic infections Avian flu & Others., 2.4 Buildings & Obstructions, 2.5 Working near Roads/Footpaths/Public areas., 2.6 Working in sensitive/Emotionally charged locality., 3.3 Excessive Noise., 3.4 Spread of Tree Pests & Diseases During work activities Felling/Pruning., 4.1a Fuelling., 4.2b Maintenance of chain and saw bar., 4.3c Noise., 4.4d Vibration., 4.5e Poor Handling., 4.6f Contact with moving Chain/kickback., 4.7g Contact with moving Chain/kickback. Environmental factors., 5.2 Equipment Failure., 5.3 Fall from Height., 5.4 Poor Climbing technique., 5.5 Falling Objects/Equipment/Tools., 5.6 Awkward movements when working in the tree., 6.1 Top handle chainsaw use by climber., 6.2 Passing saw to/from climber., 6.4 Branch removal., 7.1 Brushwood Chippers., 8.2 Noise, 9.1 covid, 10.1 Driving & Associated Hazards.
Select Appropriate Safety Guide	TG1 (AA Technical Guide 1 Tree Climbing and Aerial Rescue), TG2 (AA Technical Guide 2 Use of Tools in the Tree), TG3 (AA Technical Guide 3 Rigging and Dismantling), FISA 806 Welfare, FISA 805 Training and certification, FISA 802 Emergency Planning, FISA 604 Wood chippers, FISA 304 Chainsaw cross-cutting and manual stacking, FISA 301 Using petrol-driven chainsaws, Safety Guide 1: Tree Climbing and Aerial Rescue, Safety Guide 2: Use of Tools in the Tree, Safety Guide 3: Rigging and Dismantling

Risk Assessment Completed By

Signature
 Jac Morgan 12/11/2025 10:27:59

Re-assign to:	
---------------	--
