


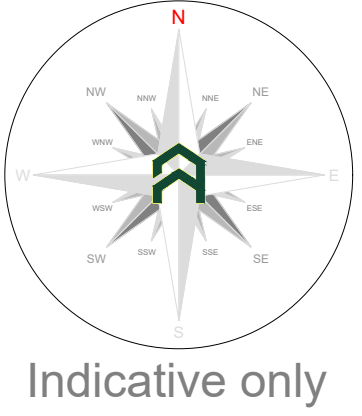

Arboricultural Impacts			
Impacts			Nos. of trees
Trees to be removed			
Groups / Hedges to be removed (Partial removal of groups)			0 (0)
Trees with proposed incursions into RPA's			0
Groups / Hedges with proposed incursions into RPA's			1
Trees that will require pruning			0
Groups / Hedges that will require pruning			2
Trees to be transplanted			0
Groups / Hedges to be transplanted			0
No.	Species	Proposed structure	Incursion
G1	Various	Hard surfacing	RPA / Canopy
Tree Work Schedule			
No.	Species	Works	Category
2	Various	Fell to ground level, remove stump	C
G1	Various	Partial removal - Fell to ground level, ground not stumped Crown lift - lift crown to 3.5m above hard surfacing	B
G2	Various	Partial removal - Fell to ground level, ground not stumped Crown reduction - reduce 50% canopy to provide 3m clearance from existing building	C
All tree work is to be undertaken in accordance with British Standard BS 3888:2010 Tree work - Recommendations. All arising are to be removed and the site to be left as found. Care is to be taken of the ground around retained trees to make sure that it does not become compacted as a result of tree surgery operations. No equipment or vehicles such as timber trailers, tractors, excavators or cranes shall be parked or driven beneath the crowns of any retained trees, to prevent subsequent compaction and root death.			
No. of individual trees to be removed			
U	A	B	C
0	0	0	1
No. of groups / hedges to be removed			
U	A	B	C
0 (0)	0 (0)	0 (1)	0 (1)
1 (1) - Partial removal of a group			
Arboricultural Method Statement			
All tree work is to be undertaken in accordance with British Standard BS 3888:2010 Tree work - Recommendations. Please refer to Arbtech Consulting Ltd. Tree Schedule, Arboricultural Method Statement and Tree Protection Plan, for full details of all surveyed trees and how all aspects of the development may be implemented without detriment to retained trees.			

Unit 3, Well House Barns, Chester, CH4 0DH
<https://arbtech.co.uk>, 01244 661170

Project: Premier Inn, Salisbury North Bishopdown, Pearce Way, Salisbury, Wiltshire, SP1 3GU.

Client: Premier Inn Hotels

Drawing: Arboricultural Impact Assessment

Based on: 6213-F- PROP

Drawing No: Arbtech AIA 01

Date: Apr 2024 Scale: 1:100 @ A0 Drawn: MGM

Key:

Tree Nos.:	1	Tree Canopies:	Trunks:
RPA's:	Category 'B' trees	Category 'B' groups	Category 'B' (Top)
Category 'C' trees:	Category 'C' groups	Category 'C' (Top)	Category 'C' (Top)

Trees to be removed:

Incursion - Hard surfacing	Incursion - Hard surfacing
----------------------------	----------------------------

Arbtech Consulting Ltd. 2023
