

Product 4 - AIMS Information398527-WXDate:18/02/2025

| Map Ref | Asset ID | Asset Type             | Right or left bank | Asset Description                      | Approx length (m) | Actual fluvial downstream crest level (mAOD) | Actual fluvial downstream crest level accuracy                               | Actual fluvial upstream crest level (mAOD) | Actual fluvial upstream crest level accuracy                                 | Actual fluvial coastal crest level (mAOD) | Actual fluvial coastal crest level accuracy | NGR          | Most recent inspection | Overall condition |
|---------|----------|------------------------|--------------------|----------------------------------------|-------------------|----------------------------------------------|------------------------------------------------------------------------------|--------------------------------------------|------------------------------------------------------------------------------|-------------------------------------------|---------------------------------------------|--------------|------------------------|-------------------|
| 1       | 103369   | Natural High Ground    | Left               | REVTMENT - SIMPLE - MASONRY - WALL     | 125.73            | 45.70                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 46.70                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU13992985   | 29/08/2024             | 2 - Good          |
| 4       | 1038     | Natural High Ground    | Left               | NATURAL BANK                           | 95.22             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU13952974   | 29/08/2024             | 3 - Fair          |
| 10      | 106333   | Natural High Ground    | Left               | NATURAL BANK                           | 59.18             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU13812987   | 30/08/2024             | 3 - Fair          |
| 11      | 106334   | Natural High Ground    | Left               | NATURAL BANK                           | 147.46            | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1387429810 | 30/08/2024             | 3 - Fair          |
| 12      | 106335   | Natural High Ground    | Left               | NATURAL BANK                           | 128.11            | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1374029886 | 30/08/2024             | 3 - Fair          |
| 13      | 1072     | Engineered High Ground | Left               | WALL - NON-FLOOD - MASONRY             | 67.24             | 46.54                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.00                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14172986   | 23/10/2024             | 2 - Good          |
| 14      | 1073     | Engineered High Ground | Left               | REVTMENT - SIMPLE - MASONRY - WALL     | 36.10             | 47.25                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.58                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14212990   | 23/10/2024             | 3 - Fair          |
| 15      | 1074     | Engineered High Ground | Right              | WALL - ABUTMENT - MASONRY              | 16.51             | 47.66                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.56                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14132984   | 23/10/2024             | 2 - Good          |
| 21      | 1092     | Natural High Ground    | Right              | NATURAL BANK                           | 163.36            | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1386229792 | 30/08/2024             | 3 - Fair          |
| 22      | 1093     | Natural High Ground    | Left               | REVTMENT - SIMPLE - MASONRY - WALL     | 82.50             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU13752993   | 30/08/2024             | 3 - Fair          |
| 23      | 1094     | Natural High Ground    | Right              | REVTMENT - COMPLEX                     | 98.68             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1375929911 | 30/08/2024             | 3 - Fair          |
| 30      | 1171     | Engineered High Ground | Left               | WALL - ABUTMENT - MASONRY              | 16.55             | 47.64                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.57                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14152983   | 23/10/2024             | 3 - Fair          |
| 31      | 1172     | Engineered High Ground | Right              | NATURAL BANK                           | 53.27             | DNR                                          | DNR                                                                          | 47.97                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14283023   | 23/10/2024             | 3 - Fair          |
| 34      | 1173     | Engineered High Ground | Right              | EMBANKMENT - NON-FLOOD - EARTH         | 40.12             | 47.97                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.97                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14293028   | 23/10/2024             | 3 - Fair          |
| 54      | 1219     | Engineered High Ground | Right              | WALL - FLOOD - CONCRETE - MASONRY CLAD | 64.26             | 47.23                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.23                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14192992   | 23/10/2024             | 2 - Good          |
| 56      | 122307   | Natural High Ground    | Right              | NATURAL BANK                           | 105.77            | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14022970   | 29/08/2024             | 2 - Good          |
| 57      | 122308   | Natural High Ground    | Right              | REVTMENT - SIMPLE - STEEL - PILING     | 110.84            | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1409829787 | 29/08/2024             | 3 - Fair          |
| 58      | 122533   | Natural High Ground    | Left               | REVTMENT - SIMPLE - MASONRY            | 36.75             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14132981   | 29/08/2024             | 3 - Fair          |
| 59      | 122535   | Natural High Ground    | Left               | REVTMENT - SIMPLE - MASONRY            | 25.21             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1411229784 | 29/08/2024             | 3 - Fair          |
| 60      | 1244     | Engineered High Ground | Right              | WALL - ABUTMENT - CONCRETE             | 18.63             | 48.49                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 48.50                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14202995   | 23/10/2024             | 2 - Good          |
| 61      | 1245     | Engineered High Ground | Right              | WALL - FLOOD - CONCRETE - MASONRY CLAD | 41.21             | 46.70                                        | 1: +/- 0.01m to 0.05m vertical accuracy (Typically on site survey)           | 46.40                                      | 1: +/- 0.01m to 0.05m vertical accuracy (Typically on site survey)           | DNR                                       | DNR                                         | SU1416729889 | 23/10/2024             | 2 - Good          |

| Map Ref | Asset ID | Asset Type             | Right or left bank | Asset Description                      | Approx length (m) | Actual fluvial downstream crest level (mAOD) | Actual fluvial downstream crest level accuracy                               | Actual fluvial upstream crest level (mAOD) | Actual fluvial upstream crest level accuracy                                 | Actual fluvial coastal crest level (mAOD) | Actual fluvial coastal crest level accuracy | NGR          | Most recent inspection | Overall condition |
|---------|----------|------------------------|--------------------|----------------------------------------|-------------------|----------------------------------------------|------------------------------------------------------------------------------|--------------------------------------------|------------------------------------------------------------------------------|-------------------------------------------|---------------------------------------------|--------------|------------------------|-------------------|
| 62      | 1246     | Wall                   | Left               | WALL - FLOOD - CONCRETE - MASONRY CLAD | 161.30            | 46.97                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.04                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14243031   | 23/10/2024             | 3 - Fair          |
| 64      | 1248     | Engineered High Ground | Right              | REVTMENT - SIMPLE - STONE              | 8.87              | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14233040   | 23/10/2024             | 4 - Poor          |
| 68      | 1269     | Natural High Ground    | Right              | REVTMENT - SIMPLE - MASONRY - WALL     | 113.76            | 45.70                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1399929887 | 29/08/2024             | 4 - Poor          |
| 69      | 1270     | Engineered High Ground | Left               | REVTMENT - SIMPLE - MASONRY - WALL     | 76.71             | 45.90                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.30                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14113032   | 29/10/2024             | 3 - Fair          |
| 70      | 1273     | Engineered High Ground | Right              | WALL - NON-FLOOD - MASONRY             | 13.85             | 47.40                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.46                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1402830173 | 23/10/2024             | 2 - Good          |
| 71      | 1274     | Engineered High Ground | Right              | REVTMENT - SIMPLE - CONCRETE - WALL    | 62.20             | 47.20                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 51.31                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1402930222 | 29/10/2024             | 3 - Fair          |
| 78      | 1314     | Engineered High Ground | Left               | REVTMENT - COMPLEX                     | 37.07             | 46.80                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 46.40                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14242996   | 12/07/2022             | 3 - Fair          |
| 79      | 1315     | Engineered High Ground | Left               | REVTMENT - COMPLEX                     | 23.17             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1426329986 | 23/10/2024             | 3 - Fair          |
| 82      | 1341     | Engineered High Ground | Right              | REVTMENT - SIMPLE - MASONRY - WALL     | 33.33             | 47.00                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 48.50                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1423729981 | 23/10/2024             | 3 - Fair          |
| 83      | 1342     | Engineered High Ground | Left               | REVTMENT - COMPLEX                     | 12.48             | DNR                                          | DNR                                                                          | 48.50                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14272998   | 23/10/2024             | 3 - Fair          |
| 84      | 1343     | Engineered High Ground | Left               | REVTMENT - COMPLEX                     | 95.36             | 48.50                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 48.50                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1428730027 | 12/07/2022             | 3 - Fair          |
| 85      | 1344     | Engineered High Ground | Left               | REVTMENT - SIMPLE - MASONRY - WALL     | 47.59             | 48.50                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 46.70                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14293010   | 23/10/2024             | 3 - Fair          |
| 87      | 1345     | Engineered High Ground | Left               | REVTMENT - SIMPLE - MASONRY - WALL     | 77.47             | 46.70                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 48.26                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14293016   | 12/07/2022             | 2 - Good          |
| 88      | 1346     | Engineered High Ground | Right              | REVTMENT - COMPLEX                     | 77.77             | 48.75                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.84                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1427430048 | 23/10/2024             | 3 - Fair          |
| 89      | 1347     | Engineered High Ground | Left               | REVTMENT - COMPLEX - WALL              | 98.77             | 48.49                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 48.55                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14313043   | 23/10/2024             | 3 - Fair          |
| 90      | 1348     | Engineered High Ground | Right              | REVTMENT - SIMPLE - STEEL - PILING     | 33.07             | 47.20                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 48.50                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14283014   | 23/10/2024             | 3 - Fair          |
| 91      | 1349     | Engineered High Ground | Left               | WALL - NON-FLOOD - MASONRY             | 19.99             | 47.00                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.25                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1403430170 | 23/10/2024             | 3 - Fair          |
| 92      | 1350     | Engineered High Ground | Left               | REVTMENT - SIMPLE - MASONRY - WALL     | 39.60             | 47.30                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 46.20                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1404130191 | 23/10/2024             | 3 - Fair          |
| 101     | 136757   | Engineered High Ground | Left               | WALL - NON FLOOD - MASONRY             | 28.05             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14233010   | 23/10/2024             | 2 - Good          |
| 102     | 136758   | Engineered High Ground | Right              | WALL - NON FLOOD - MASONRY             | 23.30             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14223009   | 23/10/2024             | 2 - Good          |

| Map Ref | Asset ID | Asset Type             | Right or left bank | Asset Description                          | Approx length (m) | Actual fluvial downstream crest level (mAOD) | Actual fluvial downstream crest level accuracy                                                | Actual fluvial upstream crest level (mAOD) | Actual fluvial upstream crest level accuracy                                                  | Actual fluvial coastal crest level (mAOD) | Actual fluvial coastal crest level accuracy | NGR          | Most recent inspection | Overall condition |
|---------|----------|------------------------|--------------------|--------------------------------------------|-------------------|----------------------------------------------|-----------------------------------------------------------------------------------------------|--------------------------------------------|-----------------------------------------------------------------------------------------------|-------------------------------------------|---------------------------------------------|--------------|------------------------|-------------------|
| 103     | 136759   | Engineered High Ground | Left               | WALL - NON-FLOOD - COMPLEX                 | 64.22             | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU14233013   | 23/10/2024             | 3 - Fair          |
| 104     | 137752   | Engineered High Ground | Left               | REVTMENT - SIMPLE                          | 44.22             | 47.20                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | 47.65                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                       | DNR                                         | SU14253011   | 23/10/2024             | 3 - Fair          |
| 105     | 137753   | Engineered High Ground | Right              | REVTMENT - SIMPLE                          | 48.31             | 46.75                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | 47.20                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                       | DNR                                         | SU1425230121 | 23/10/2024             | 3 - Fair          |
| 106     | 137754   | Engineered High Ground | Left               | NATURAL BANK                               | 16.54             | 46.40                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU14262997   | 23/10/2024             | 3 - Fair          |
| 114     | 138065   | Wall                   | Left               | WALL - FLOOD - MASONRY                     | 66.46             | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU14243021   | 23/10/2024             | 2 - Good          |
| 117     | 138999   | Natural High Ground    | Left               | NATURAL BANK                               | 61.26             | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU1422030000 | 08/07/2022             | 2 - Good          |
| 118     | 139000   | Natural High Ground    | Right              | NATURAL BANK                               | 76.29             | 47.50                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU14212998   | 23/10/2024             | 3 - Fair          |
| 120     | 148219   | Natural High Ground    | Right              | NATURAL BANK                               | 581.76            | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU13962943   | 30/08/2024             | 2 - Good          |
| 140     | 166014   | Engineered High Ground | Right              | WALL - NON-FLOOD - MASONRY                 | 128.46            | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU14233018   | 11/07/2022             | 2 - Good          |
| 200     | 179799   | Engineered High Ground | Right              | CHANNEL - WATERCOURSE - EARTH              | 71.61             | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU1424130301 | 23/10/2024             | 4 - Poor          |
| 201     | 179800   | Natural High Ground    | Right              | CHANNEL - BERM - EARTH - MAINTAINED        | 13.21             | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU14233033   | 08/07/2022             | 3 - Fair          |
| 202     | 179801   | Engineered High Ground | Right              | CHANNEL - WATERCOURSE - EARTH - MAINTAINED | 57.76             | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU1422530362 | 23/10/2024             | 4 - Poor          |
| 215     | 327279   | Demountable Defence    | DNR                | ACCESS - PEDESTRIAN - TIMBER - STOPLOGS    | 5.00              | 47.94                                        | 3: +/- >0.15m to 0.75m vertical accuracy (Typically older (pre 2004) Lidar or Photogrammetry) | 47.94                                      | 3: +/- >0.15m to 0.75m vertical accuracy (Typically older (pre 2004) Lidar or Photogrammetry) | DNR                                       | DNR                                         | SU14313033   | 28/09/2021             | 3 - Fair          |
| 220     | 38524    | Engineered High Ground | Left               | WALL - FLOOD - CONCRETE - MASONRY CLAD     | 23.22             | 47.29                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | 47.29                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                       | DNR                                         | SU14222993   | 23/10/2024             | 2 - Good          |
| 221     | 38525    | Engineered High Ground | Right              | WALL - FLOOD - CONCRETE - MASONRY CLAD     | 56.92             | 46.59                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | 46.65                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                       | DNR                                         | SU14152985   | 23/10/2024             | 3 - Fair          |
| 222     | 38676    | Engineered High Ground | Right              | WALL - NON-FLOOD - MASONRY                 | 19.65             | 47.56                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | 47.25                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                       | DNR                                         | SU1413629854 | 08/07/2022             | 2 - Good          |
| 223     | 38677    | Engineered High Ground | Right              | WALL - BUILDING - MASONRY                  | 13.87             | 50.00                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | 50.00                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                       | DNR                                         | SU1416429869 | 23/10/2024             | 3 - Fair          |
| 224     | 38678    | Engineered High Ground | Left               | WALL - ABUTMENT - CONCRETE                 | 16.27             | 47.39                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | 47.39                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                       | DNR                                         | SU14243023   | 23/10/2024             | 3 - Fair          |
| 225     | 38679    | Engineered High Ground | Right              | WALL - ABUTMENT - CONCRETE                 | 24.76             | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU14233024   | 11/07/2022             | 3 - Fair          |
| 227     | 40827    | Engineered High Ground | Right              | REVTMENT - SIMPLE - CONCRETE - WALL        | 13.61             | 48.50                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | 48.75                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                       | DNR                                         | SU1426229993 | 23/10/2024             | 3 - Fair          |
| 228     | 40828    | Engineered High Ground | Right              | REVTMENT - SIMPLE - CONCRETE - WALL        | 24.41             | DNR                                          | DNR                                                                                           | DNR                                        | DNR                                                                                           | DNR                                       | DNR                                         | SU1427029988 | 23/10/2024             | 3 - Fair          |
| 229     | 40829    | Engineered High Ground | Left               | REVTMENT - SIMPLE - MASONRY - WALL         | 184.89            | 48.26                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | 48.40                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry)                  | DNR                                       | DNR                                         | SU1430930290 | 23/10/2024             | 4 - Poor          |

| Map Ref | Asset ID | Asset Type             | Right or left bank | Asset Description                   | Approx length (m) | Actual fluvial downstream crest level (mAOD) | Actual fluvial downstream crest level accuracy                               | Actual fluvial upstream crest level (mAOD) | Actual fluvial upstream crest level accuracy                                 | Actual fluvial coastal crest level (mAOD) | Actual fluvial coastal crest level accuracy | NGR          | Most recent inspection | Overall condition |
|---------|----------|------------------------|--------------------|-------------------------------------|-------------------|----------------------------------------------|------------------------------------------------------------------------------|--------------------------------------------|------------------------------------------------------------------------------|-------------------------------------------|---------------------------------------------|--------------|------------------------|-------------------|
| 230     | 40830    | Engineered High Ground | Right              | REVTMENT - SIMPLE - CONCRETE - WALL | 50.47             | 47.84                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.65                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1427930100 | 23/10/2024             | 3 - Fair          |
| 231     | 40831    | Engineered High Ground | Right              | EMBANKMENT - NON FLOOD - EARTH      | 43.86             | 48.52                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 48.33                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14283018   | 23/10/2024             | 3 - Fair          |
| 232     | 40832    | Engineered High Ground | Right              | REVTMENT - COMPLEX                  | 120.77            | 47.97                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 49.08                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14303035   | 23/10/2024             | 2 - Good          |
| 239     | 41069    | Natural High Ground    | Right              | NATURAL BANK                        | 91.88             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU13952971   | 29/08/2024             | 3 - Fair          |
| 240     | 41070    | Engineered High Ground | Left               | REVTMENT - SIMPLE - MASONRY - WALL  | 151.58            | 46.80                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.96                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14022997   | 23/10/2024             | 3 - Fair          |
| 241     | 41072    | Natural High Ground    | Right              | NATURAL BANK                        | 66.99             | 45.80                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 45.70                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1393829805 | 29/08/2024             | 3 - Fair          |
| 242     | 41073    | Natural High Ground    | Left               | NATURAL BANK                        | 98.93             | 46.20                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 45.90                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1406130257 | 23/10/2024             | 3 - Fair          |
| 244     | 41117    | Engineered High Ground | Right              | WALL - NON-FLOOD - MASONRY          | 154.15            | 46.77                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.46                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14003000   | 29/10/2024             | 3 - Fair          |
| 257     | 41645    | Engineered High Ground | Right              | REVTMENT - SIMPLE - MASONRY - WALL  | 39.22             | 47.83                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 46.82                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1401230139 | 23/10/2024             | 3 - Fair          |
| 258     | 54747    | Engineered High Ground | Right              | WALL - NON FLOOD - MASONRY          | 35.90             | 47.28                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 47.30                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1415129862 | 23/10/2024             | 2 - Good          |
| 263     | 5682     | Natural High Ground    | Left               | REVTMENT - COMPLEX                  | 96.47             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1398129486 | 30/08/2024             | 3 - Fair          |
| 264     | 5683     | Natural High Ground    | Left               | NATURAL BANK                        | 49.40             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1396129573 | 30/08/2024             | 3 - Fair          |
| 265     | 5684     | Natural High Ground    | Left               | REVTMENT - SIMPLE - TIMBER - PILING | 68.96             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1397029644 | 30/08/2024             | 3 - Fair          |
| 290     | 77851    | Natural High Ground    | Left               | NATURAL BANK                        | 70.20             | 45.70                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 45.70                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1394729809 | 29/08/2024             | 3 - Fair          |
| 295     | 812      | Engineered High Ground | Left               | REVTMENT - SIMPLE - MASONRY - WALL  | 42.08             | 47.83                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 48.41                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU1402030138 | 23/10/2024             | 3 - Fair          |
| 296     | 882      | Engineered High Ground | Right              | EMBANKMENT - RAIL - EARTH           | 140.66            | 51.31                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 51.99                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14043027   | 08/07/2022             | 3 - Fair          |
| 298     | 88514    | Natural High Ground    | Left               | REVTMENT - SIMPLE - MASONRY         | 44.26             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1400729681 | 29/08/2024             | 3 - Fair          |
| 299     | 88516    | Natural High Ground    | Left               | REVTMENT - SIMPLE - TIMBER          | 6.35              | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14022969   | 29/08/2024             | 3 - Fair          |
| 300     | 88517    | Natural High Ground    | Left               | WALL - NON-FLOOD - MASONRY          | 19.89             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14032968   | 29/08/2024             | 3 - Fair          |
| 301     | 88518    | Natural High Ground    | Left               | REVTMENT - SIMPLE - MASONRY         | 34.27             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14042970   | 29/08/2024             | 3 - Fair          |
| 302     | 88519    | Natural High Ground    | Left               | REVTMENT - SIMPLE - MASONRY - WALL  | 9.08              | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14052972   | 29/08/2024             | 4 - Poor          |
| 303     | 88520    | Natural High Ground    | Left               | REVTMENT - SIMPLE - MASONRY - WALL  | 17.37             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU14062973   | 29/08/2024             | 3 - Fair          |

| Map Ref | Asset ID | Asset Type             | Right or left bank | Asset Description                  | Approx length (m) | Actual fluvial downstream crest level (mAOD) | Actual fluvial downstream crest level accuracy                               | Actual fluvial upstream crest level (mAOD) | Actual fluvial upstream crest level accuracy                                 | Actual fluvial coastal crest level (mAOD) | Actual fluvial coastal crest level accuracy | NGR          | Most recent inspection | Overall condition |
|---------|----------|------------------------|--------------------|------------------------------------|-------------------|----------------------------------------------|------------------------------------------------------------------------------|--------------------------------------------|------------------------------------------------------------------------------|-------------------------------------------|---------------------------------------------|--------------|------------------------|-------------------|
| 304     | 88521    | Natural High Ground    | Left               | REVTMENT - SIMPLE - MASONRY - WALL | 57.35             | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU1407929753 | 29/08/2024             | 3 - Fair          |
| 311     | 94713    | Engineered High Ground | Left               | WALL - ABUTMENT - CONCRETE         | 21.45             | 48.49                                        | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | 48.48                                      | 2: +/- >0.05m to 0.15m vertical accuracy (Typically LIDAR or Photogrammetry) | DNR                                       | DNR                                         | SU14222995   | 08/07/2022             | 3 - Fair          |
| 317     | 971      | Natural High Ground    | Right              | NATURAL BANK                       | 170.38            | DNR                                          | DNR                                                                          | DNR                                        | DNR                                                                          | DNR                                       | DNR                                         | SU13742986   | 30/08/2024             | 3 - Fair          |

| Map Ref | Asset ID | Asset Type     | Right or left bank | Asset Description                     | Approx length (m) | Actual fluvial downstream crest level (mAOD) | Actual fluvial downstream crest level accuracy | Actual fluvial upstream crest level (mAOD) | Actual fluvial upstream crest level accuracy | Actual fluvial coastal crest level (mAOD) | Actual fluvial coastal crest level accuracy | NGR          | Most recent inspection | Overall condition |
|---------|----------|----------------|--------------------|---------------------------------------|-------------------|----------------------------------------------|------------------------------------------------|--------------------------------------------|----------------------------------------------|-------------------------------------------|---------------------------------------------|--------------|------------------------|-------------------|
| 1       | 1040     | Simple Culvert | DNR                | CULVERT - MINOR ROAD - CONCRETE       | 15.67             | DNR                                          | DNR                                            | DNR                                        | DNR                                          | DNR                                       | DNR                                         | SU14022994   | 29/10/2024             | 2 - Good          |
| 2       | 1041     | Simple Culvert | DNR                | CULVERT - MINOR ROAD - CONCRETE - BOX | 20.25             | DNR                                          | DNR                                            | DNR                                        | DNR                                          | DNR                                       | DNR                                         | SU14003010   | 23/10/2024             | 2 - Good          |
| 3       | 1271     | Simple Culvert | DNR                | CULVERT - WATERCOURSE - MASONRY       | 86.82             | DNR                                          | DNR                                            | DNR                                        | DNR                                          | DNR                                       | DNR                                         | SU1409330383 | 23/10/2024             | 2 - Good          |
| 9       | 138064   | Simple Culvert | DNR                | CULVERT - WATERCOURSE - STEEL - BOX   | 44.64             | DNR                                          | DNR                                            | DNR                                        | DNR                                          | DNR                                       | DNR                                         | SU14223006   | 23/10/2024             | 3 - Fair          |
| 17      | 41071    | Simple Culvert | DNR                | CULVERT - WATERCOURSE - CONCRETE      | 14.65             | DNR                                          | DNR                                            | DNR                                        | DNR                                          | DNR                                       | DNR                                         | SU14023016   | 23/10/2024             | 3 - Fair          |

**Notes**


\* Overall Condition has been taken from the most recent inspection

\* Inspections are of a purely visual nature and do not necessarily reflect the true condition of the asset

\* Condition: 1 = very good, Condtion 2 = good, Condition 3 = fair, Condition 4 = poor, Condition 5 = very poor

\* Crest level accuracy: 1 = ± 0.01 to 0.05m, 2 = ± 0.05 to 0.15m, 3 = ± 0.15 to 0.75m, 4 = ± 0.75 or greater

\* DNR = data not recorded

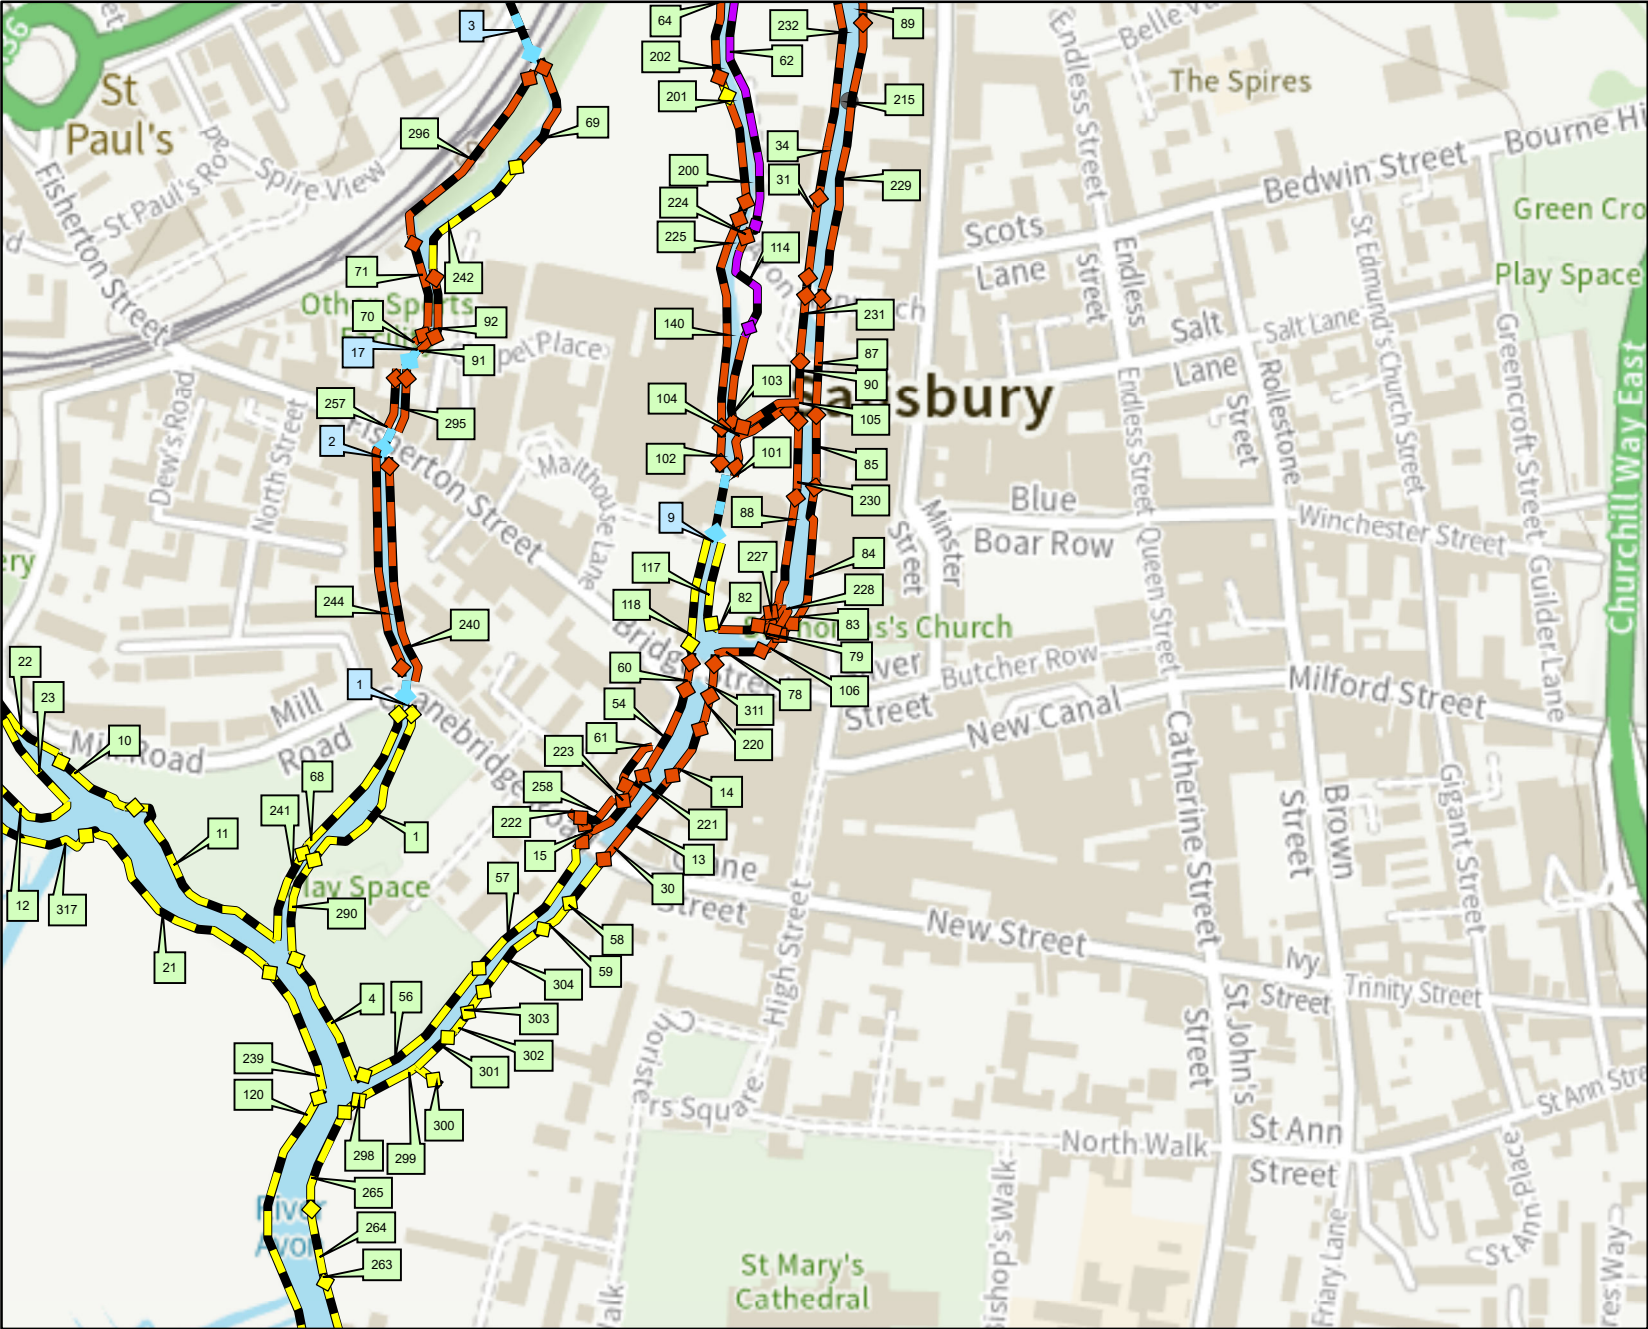

Scale: 1:5,000



### Legend

#### Defences

- Barrier Beach
- Beach
- Bridge Abutment
- Cliff
- Demountable Defence
- Dunes
- Embankment
- Engineered High Ground
- Flood Gate
- Natural High Ground
- Promenade
- Quay
- Spillway
- Wall

#### Culverts

- Simple Culvert
- Complex Culvert

This data has been extracted from the Asset Information Management System (AIMS OM) which was created to draw various data sources into one database and has been populated with information of varying quality.
