GT GARDINER &THEOBALD

Devizes Castle

Ladies Arch Restoration Works

Line	Name	Duration	Start	Finish
1	Scaffold Erect. Runway, laydown area, running gantry, nico rails	1w 4d	27/04/26	08/05/26
2	Record and controlled dismantle to laydown area, including butresses & wing walls	2w	11/05/26	22/05/26
3	Excavation	4d	26/05/26	29/05/26
4	C30 Concrete pour and curing	2w	01/06/26	12/06/26
5	Reconstruction of Arch and wing walls	5w	15/06/26	17/07/26
6	Scaffold strike	1w	20/07/26	24/07/26
7	Reinstatement of courtyard paved area	1w	27/07/26	31/07/26

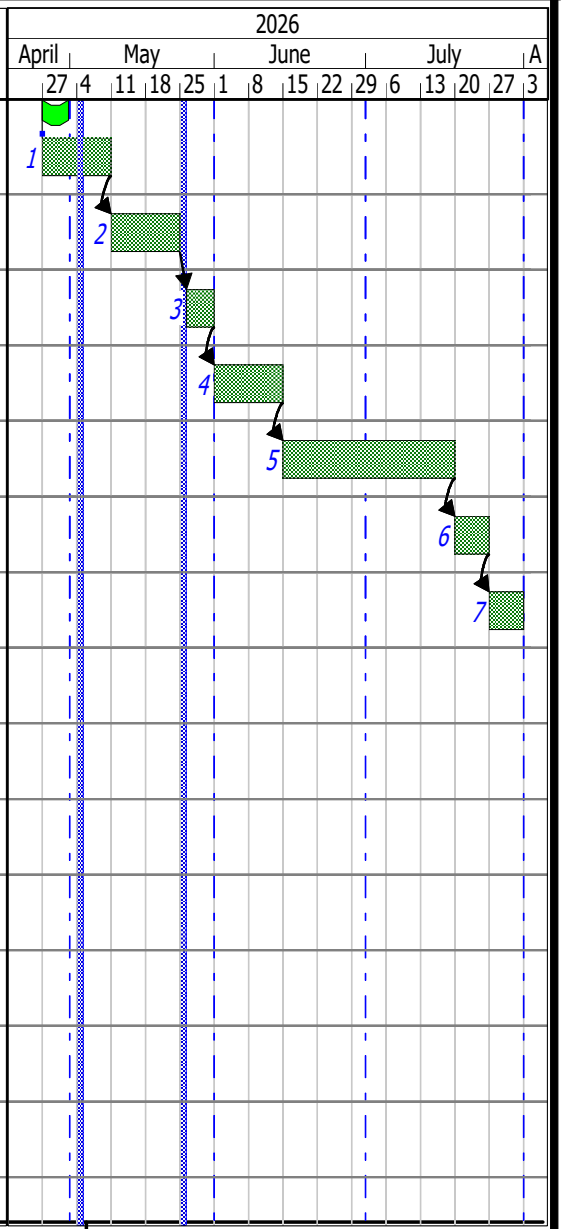

Drawn by: GTCM | Dwg No. 40109/03 | Comment: | Revision/Date of Issue: 1 / 16/12/2025

Planned by Asta Powerproject
